

Amber CAPEX Portal

How capital expenditure is planned, approved, sourced, awarded and paid — every screen, every role and every number, walked through end to end from a live run of the product.

CAPTURED	SCREENS	SCOPE
22 August 2026, from the running application	93	FY 2026-27 · 5 plants · 18 requests · 6 vendors

Prepared by **Genessence**

Contents

Amber CAPEX Portal — Product Walkthrough

Part 0 — The one-minute version

- Slide 0.1 · The problem this solves
- Slide 0.2 · Who does what
- Slide 0.3 · The product is two connected systems
- Slide 0.4 · The gates, and why they hold

Part 1 — Getting in

- Slide 1.1 · Sign in
- Slide 1.2 · The four portal seats
- Slide 1.3 · A clean slate
- Slide 1.4 · Switching between people

Part 2 — The budget year

- Slide 2.1 · The register of approved money starts empty
- Slide 2.2 · Budget Planning — a deliberately blank sheet
- Slide 2.3 · The Excel template, and bulk upload
- Slide 2.4 · Submitted — and handed to the plant head by email
- Slide 2.5 · The email
- Slide 2.6 · What the plant head sees
- Slide 2.7 · Approvers edit and send forward; they do not send back
- Slide 2.8 · Stage 2 — the administrator sees exactly what changed
- Slide 2.9 · Stage 3 — Global Accounts sign-off publishes the year
- Slide 2.10 · The budget approval chain, in one picture
- Slide 2.11 · FY 2026-27 is now live money

Part 3 — The supply base

- Slide 3.1 · Vendor Master
- Slide 3.2 · Adding a vendor

Part 4 — Raising a request

- Slide 4.1 · Step 1 — what kind of capital expenditure is this?
- Slide 4.2 · Steps 2 to 4 — narrowing down to approved money
- Slide 4.3 · The line-item grid
- Slide 4.4 · Review, submit, and the notification that goes out
- Slide 4.5 · The request list
- Slide 4.6 · The request detail — allocated against estimated, per line

Part 5 — Plant-head approval, by email

- Slide 5.1 · The email
- Slide 5.2 · The plant head's page

Part 6 — Sourcing: the quotation round

- Slide 6.0 · The shape of a sourcing round
- Slide 6.1 · In sourcing
- Slide 6.2 · Inviting vendors — and choosing their paperwork
- Slide 6.3 · The comparison grid appears
- Slide 6.4 · The vendor's first screen is terms, not prices
- Slide 6.5 · Quoting, line by line
- Slide 6.6 · GST is computed per line, from the HSN
- Slide 6.7 · Two quotations side by side
- Slide 6.8 · Countering, inline
- Slide 6.9 · The vendor answers

Part 7 — The technical specification gate

- Slide 7.1 · Why it is per vendor, not per request
- Slide 7.2 · Sourcing prepares the package
- Slide 7.3 · Sent to the technical team
- Slide 7.4 · The technical team's page

Part 8 — The award

- Slide 8.1 · Filling the Final Decision, line by line
- Slide 8.2 · Approve and request the invoices
- Slide 8.3 · One request, two fulfilment tracks

Part 9 — Fulfilment: from award to the last rupee

- Slide 9.1 · The vendor raises the proforma invoice
- Slide 9.2 · Internally, the request fans out per award
- Slide 9.3 · Email 1 — to Plant Accounts
- Slide 9.4 · Plant Accounts, step 1 — the FA codes
- Slide 9.5 · Email 2 — composed for them, automatically
- Slide 9.6 · Global Accounts issues the purchase order
- Slide 9.7 · The vendor gets the purchase order
- Slide 9.8 · Payment milestones — and the one that is locked
- Slide 9.9 · The trial
- Slide 9.10 · Settled

Part 10 — Foreign vendors, Incoterms and currency

- Slide 10.1 · Adding a foreign vendor mid-enquiry
- Slide 10.2 · Incoterms are collected with the quotation, not after it
- Slide 10.3 · Sourcing negotiates the terms like a price
- Slide 10.4 · Everything that compares vendors converts to rupees first

Part 11 — The reverse auction

- Slide 11.1 · Auctions are escalated, never started cold
- Slide 11.2 · Configuring the auction
- Slide 11.3 · The Business Rules document
- Slide 11.4 · Nobody bids until they have accepted
- Slide 11.5 · The vendor's acceptance screen
- Slide 11.6 · Live
- Slide 11.7 · The bid screen
- Slide 11.8 · Ranks, on a common basis

Part 12 — The dashboards

- Slide 12.1 · The idea behind all four
- Slide 12.2 · The buyer's dashboard
- Slide 12.3 · The sourcing cockpit — Desk
- Slide 12.4 · The sourcing cockpit — Performance
- Slide 12.5 · Administration — My Desk
- Slide 12.6 · Administration — Portfolio
- Slide 12.7 · Administration — Plants
- Slide 12.8 · The budget author's dashboard
- Slide 12.9 · Every number can show its own definition
- Slide 12.10 · A tile and its list always agree
- Slide 12.11 · The full request list

Part 13 — Trackers, transfers and configuration

- Slide 13.1 · The accounts queue
- Slide 13.2 · Ad-hoc budget reallocation — the only mid-year change
- Slide 13.3 · Configuration
- Slide 13.4 · The other three kinds of capital expenditure

Part 14 — Every email in one place

Part 15 — On any device

- Closing · The story in one paragraph
- Appendix · The route a request takes

Amber CAPEX Portal — Product Walkthrough

Every screen in this document was captured from the running product on 22 August 2026. Nothing here is a mock-up or a wireframe. A fiscal year was written from a blank sheet, pushed through three approval gates, spent against by eighteen requests across five plants, sourced from five onboarded vendors and one foreign one-time supplier, negotiated, split between two suppliers, taken through a reverse auction, and settled down to the last rupee — and the screens you see are what the people doing that work actually saw.

Read it front to back and you will know the product as well as someone who has used it. You should not need to open the portal to follow any of it.


Product	Amber CAPEX Portal — capital-expenditure management for Amber Enterprises India Ltd
What it covers	Budget planning, budget approval, capital requests, vendor sourcing, price negotiation, reverse auctions, technical sign-off, awards, purchase orders, milestone payments and management reporting
Who uses it	Plant buyers, the sourcing team, maintenance/budget authors and the administrator inside Amber; plant heads, the technical team, both accounts teams and every vendor from outside, by email
In this document	93 screens across 15 parts

Part 0 — The one-minute version

Slide 0.1 · The problem this solves

Amber commits capital across nine plants. Before this portal that money moved through spreadsheets, email threads and phone calls: a plant asks for a machine, somebody chases quotations, somebody else argues the price down, a third person raises the purchase order, and Accounts find out last. Nobody could answer *"where is this request, and who is sitting on it?"* without ringing four people, and nobody could answer *"how much of this year's budget have we actually committed?"* at all.

The portal turns that into **one tracked pipeline with named gates**, where every rupee can be traced from the budget line it came out of to the milestone it was paid against.



Two ideas carry the whole product:

1. **Money is pre-approved before it can be asked for.** Every request must point at a specific sub-particular inside an approved budget head. You cannot request what was never budgeted, and every screen shows allocated against committed.
2. **People outside the buying team never get a login.** Plant heads, the technical team, both accounts teams and every vendor act on a single-purpose link sent to them by email. They see the one thing they are being asked to do, and nothing else.

Slide 0.2 · Who does what

Who	How they get in	What they are responsible for
Plant buyer (one per plant)	Portal login	Raises capital requests against their own plant's approved budget
Maintenance / budget author	Portal login	Writes next year's budget and puts it up for approval
Sourcing team	Portal login	Vendors, quotations, negotiation, reverse auctions, awards, trial approval
Super admin	Portal login	The middle budget gate, ad-hoc budget transfers, configuration, full visibility
Plant head	Emailed link	Approves the plant's budget, and approves each request before it is sourced
Technical team	Emailed link	Signs off the machine specification, separately for each vendor
Plant Accounts	Emailed link	Assigns the fixed-asset codes, then records milestone payments
Global Accounts	Emailed link	Final budget sign-off; issues the purchase order to the vendor
Vendors	Emailed link	Accept Amber's terms, quote, negotiate, bid, raise the invoice, prove the machine

Inside Amber — portal login



Outside Amber — one emailed link per job

Four kinds of people have a portal seat: the plant buyer, the sourcing team, the maintenance engineer who writes the budget, and the super admin. Everyone else — plant heads, the Technical team, both Accounts teams and every vendor — works from a single-purpose link sent to them by email. They never see the rest of the portal.

Slide 0.3 · The product is two connected systems

- **The budget system** — *how much may be spent, per plant, per head, per line item, per year*. Written by maintenance, approved by the plant head, then the admin, then Global Accounts, and only then published as the live budget everybody spends against.
- **The procurement system** — *spending it*. Request → plant-head approval → sourcing (quotation or reverse auction) → technical sign-off → award → invoice → FA codes → purchase order → milestone payments → done.

Everything else in the product — the dashboards, the ad-hoc transfers, the delay penalties, the accounts queue — hangs off those two.


Slide 0.4 · The gates, and why they hold

A gate in this product is not a greyed-out button. Each one is enforced on the record itself, so a step cannot be skipped even by someone who knows the system well.

Gate	Who clears it	What it prevents
Budget — plant head	Plant head, by email	A budget going forward that the plant has not seen
Budget — admin	Super admin	A plant budget entering the books without a central check
Budget — publish	Global Accounts, by email	Money becoming spendable without a finance sign-off
Request approval	Plant head, by email	Sourcing effort spent on something the plant does not want
Contract terms	The vendor	A vendor quoting before accepting Amber's terms and penalties
Incoterms	Vendor and sourcing	A foreign order awarded with delivery and duty responsibility unsettled
Technical specification	Technical team, by email	Awarding a machine that engineering has not approved
Auction participation	The vendor	A vendor bidding without agreeing to the auction rules
Final payment	Sourcing, after the trial	The last instalment leaving before the machine is proven


Part 1 — Getting in

Slide 1.1 • Sign in

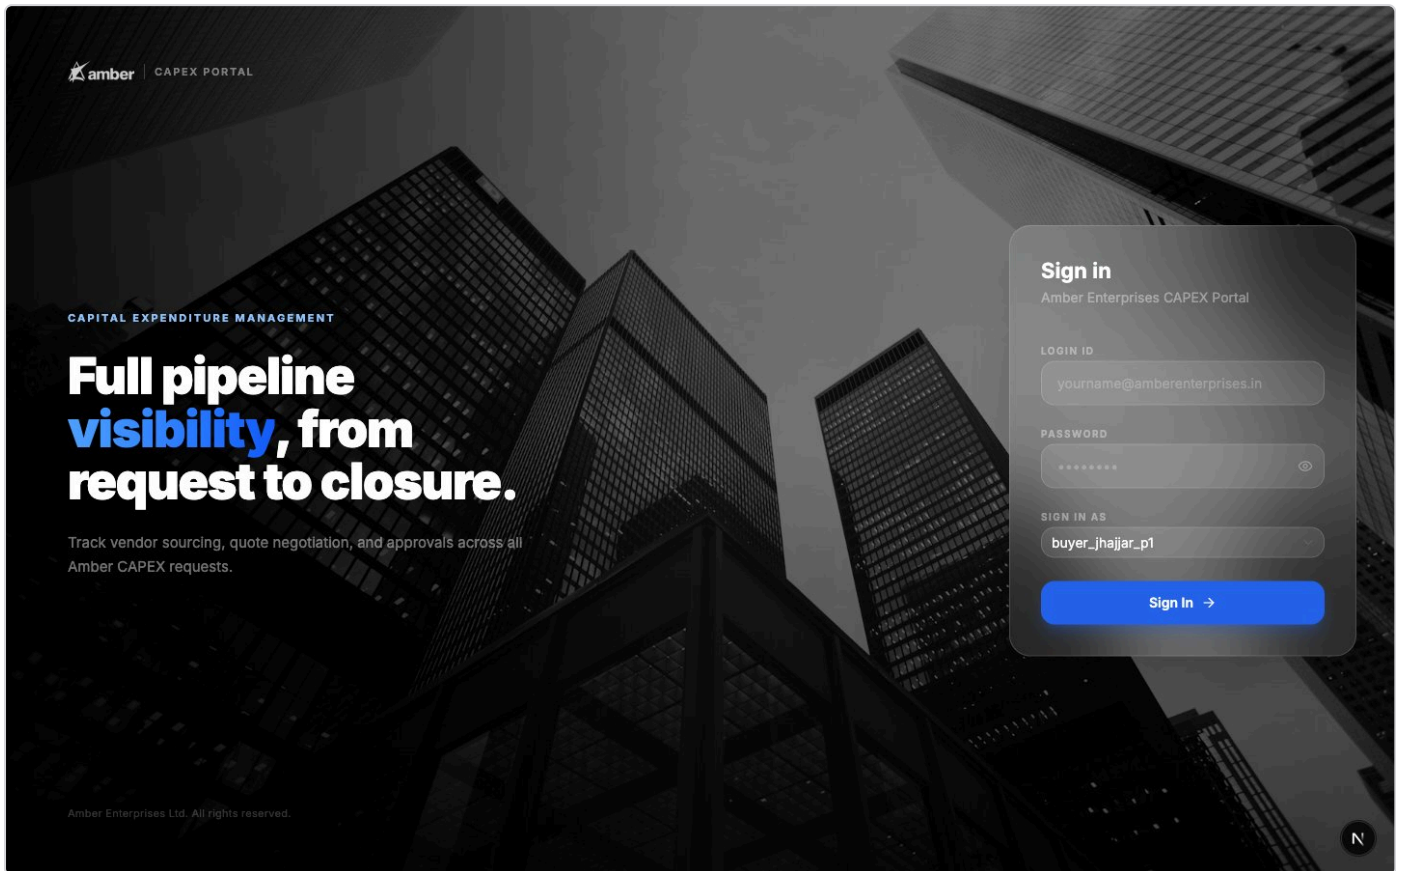

One sign-in screen for the whole company. The user picks who they are and lands in a portal shaped to that job — a plant buyer sees three menu items, the administrator sees ten.

Slide 1.2 · The four portal seats

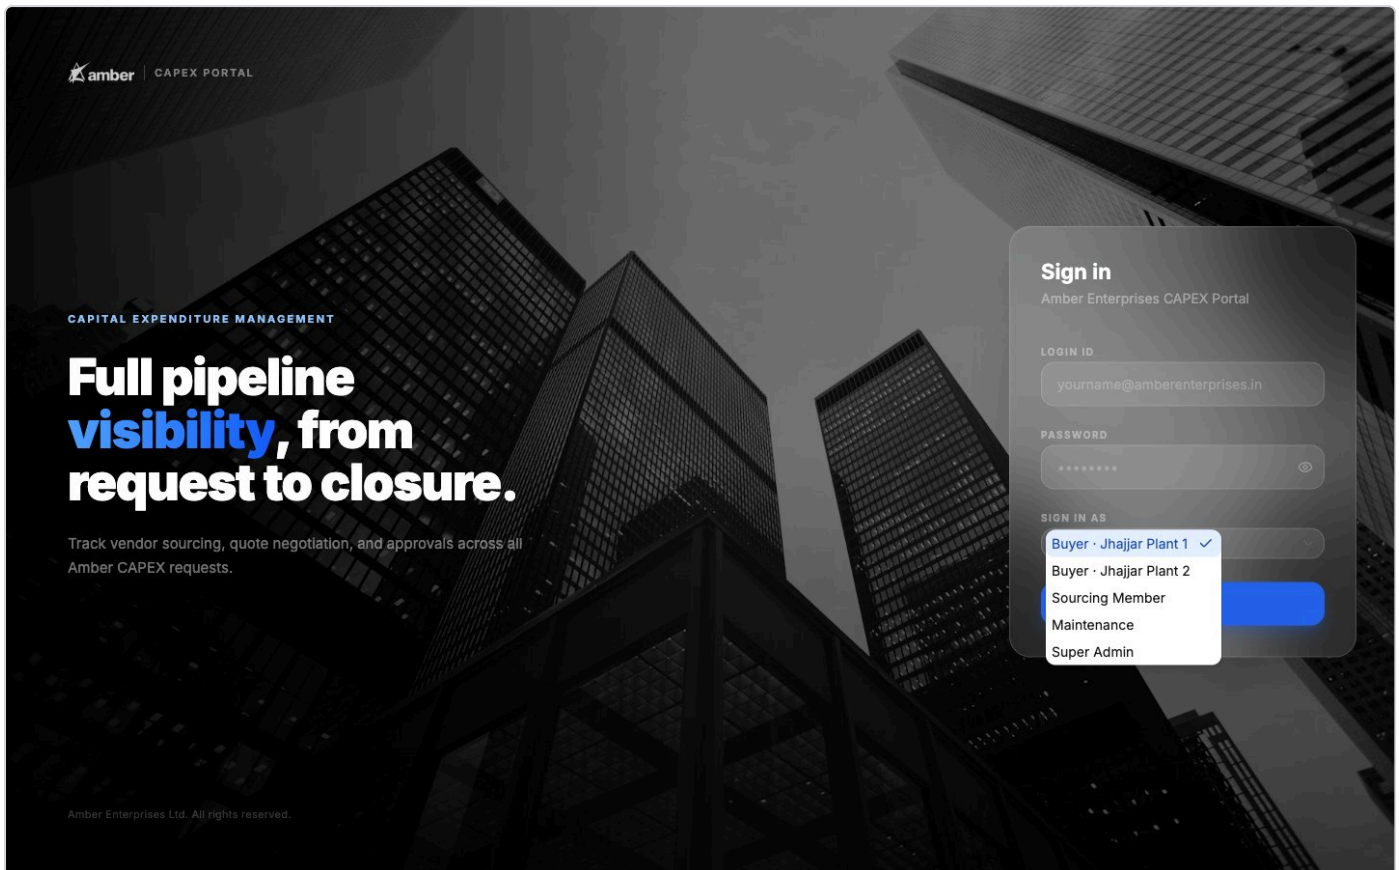

Only four kinds of people get a seat in the portal, and two of those are plant-scoped buyers:

- **Buyer · Jhajjar Plant 1** and **Buyer · Jhajjar Plant 2** — each sees only their own plant's budget, their own requests and their own numbers.
- **Sourcing Member** — runs quotations, negotiations, auctions and awards across all plants.
- **Maintenance** — writes next year's budget.
- **Super Admin** — the middle budget gate, ad-hoc transfers, configuration, and full visibility.

Everyone else in the chain works from an emailed link. That is deliberate: a plant head who approves four budgets a year should not have to remember a password, and a vendor should never be inside Amber's systems at all.

Slide 1.3 · A clean slate



This run starts genuinely empty — no requests, no committed spend, no budget. The left-hand navigation is the whole internal product: Dashboard, New Request, Requests, Vendors, CAPEX Master, Budget Planning, Ad-hoc Budget, Budget Approvals, Accounts and Configurations. Each entry is filtered by role.

Slide 1.4 · Switching between people

**CAPEX Portal**
Amber Enterprises

WORKSPACE

Dashboard

New Request

Requests

Vendors

CAPEX Master

Budget Planning

Adhoc Budget

Budget Approvals

Accounts

Configurations

< Collapse

 **Super Admin**
Full Access

[-> Log out

All Plants | **Vendor Directory** > Manage and onboard vendors

Vendor Master

All onboarded vendors across CAPEX requests.

Search by name, code, or category...

VENDOR CODE	NAME	CATEGORY	GSTIN	CONTACT NAME	CONTACT EMAIL
VND-001	Tata Motors Ancillaries	Machinery	27AABCT3518Q1ZK	Ramesh Tiwari	ramesh.tiwari@tata-ancillaries
BANK NAME: HDFC Bank ACCOUNT NUMBER: 50200012345678 IFSC: HDFC0001234 PAN: ONBOARDED AT: 10 Apr 2023					
VND-002	Siemens India	IT	27AAACS6560P1ZX	Anita Sharma	anita.sharma@siemens.com
VND-003	Bosch Packaging	Tooling	29AABCB1234A1ZZ	Klaus Mueller	k.mueller@bosch-packaging.i
VND-004	L&T Infrastructure	Infrastructure	27AAACL1234B1ZP	Suresh Iyer	suresh.iyer@lnt-infra.com
VND-005	Delta Electronics	Machinery	07AABCD5678E1ZQ	Priya Venkatesh	p.venkatesh@delta-electronic

SWITCH USER

BUYERS

 **Arjun Mehta**
Jhajjar Plant 1

 **Ravi Kumar**
Jhajjar Plant 2

SOURCING

 **Neha Kapoor**
Machinery

MAINTENANCE

 **Sunil Verma**
CAPEX Master / Budget

ADMINISTRATION


 **Super Admin**
Full Access

The portal names the person, not just the role — Arjun Mehta at Jhajjar Plant 1, Ravi Kumar at Jhajjar Plant 2, Neha Kapoor in sourcing, Sunil Verma in maintenance. Throughout this document you will see the same names, so you can always tell whose screen you are looking at.

Part 2 — The budget year

This is where the product starts. Until a budget exists and has been approved, no request can be raised at all, because every line of a request has to point at an approved budget line.

Slide 2.1 · The register of approved money starts empty

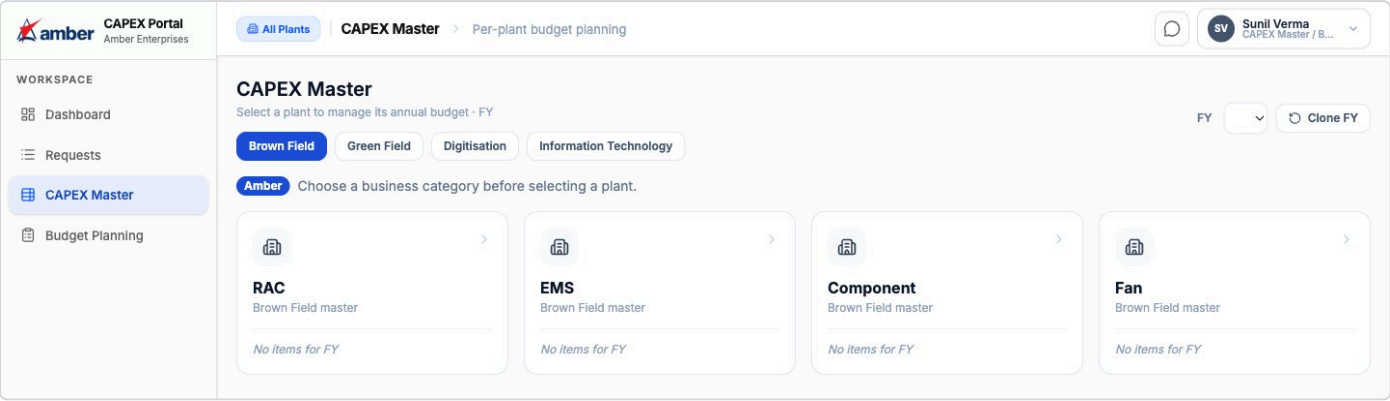

CAPEX Master is the register of approved money. It is organised into four kinds of capital expenditure — **Brown Field** (existing plants), **Green Field** (new plants), **Digitisation** and **Information Technology** — and Brown and Green Field are further split by business category (**RAC · EMS · Component · Fan**), so one plant can run four independent budgets.

Every category reads "No items for FY". FY 2026-27 is about to be written from scratch.

Slide 2.2 · Budget Planning — a deliberately blank sheet





CAPEX Portal
Amber Enterprises

WORKSPACE

Dashboard

Requests

CAPEX Master

Budget Planning

< Collapse

SV

Sunil Verma
Maintenance

Log out

All Plants

Budget Planning

Author next-FY budget proposals

SV

Sunil Verma
CAPEX Master / B...

<

Budget Proposal · Jhajjar Plant 1

Blank draft · status

Draft

Target FY

2027-28

+ Add Line

Append

Replace

Bulk Upload

Template

Save Draft

Submit to Plant Head

Total: ₹0.00 Cr

HEAD	DEPARTMENT	SUB PARTICULARS	QTY	TOTAL (CR)
No lines. Add a line or bulk-upload a workbook.				

Sunil Verma picks the category and the plant and clicks **New Next-FY Proposal**. What he gets is a **blank draft** — the portal never pre-fills last year's lines. That is a deliberate product decision: each year is argued on its own merits rather than inherited by default.

He sets the target year to 2026-27, and has three ways to fill it: type rows by hand, download the Excel template, or upload a filled workbook.

Slide 2.3 · The Excel template, and bulk upload

The downloadable template is not an empty grid. Its columns are exactly the ones the portal reads — S.No · Head · Department · Sub Particulars · Qty · Total Cost (Cr) · Reason for Requirement · Benefits · ROI — and it arrives pre-filled with worked examples from that plant's own history, so the expected shape is never ambiguous. A downloaded template can be edited and uploaded back unchanged.

amber

CAPEX Portal

Amber Enterprises

WORKSPACE

Dashboard

Requests

CAPEX Master

Budget Planning

SV

Sunil Verma

Maintenance

Log out

All Plants

Budget Planning

Author next-FY budget proposals

SV

Sunil Verma

CAPEX Master / B...

Budget Proposal · Jhajjar Plant 1

Blank draft · status Draft

Target FY 2026-27

+ Add Line

Append

Replace

Bulk Upload

Template

Save Draft

Submit to Plant Head

Assembly Shop: ₹0.05 Cr · 1

Automation: ₹1.38 Cr · 2

Copper Shop: ₹2.10 Cr · 1

Digitization: ₹0.98 Cr · 2

General: ₹2.53 Cr · 3

New Business: ₹30.60 Cr · 2

Press Shop: ₹1.35 Cr · 1

Total: ₹38.99 Cr

HEAD	DEPARTMENT	SUB PARTICULARS	QTY	TOTAL (CR)
Automation	HEX	HEX Black Copper Detection	3	0.33
Automation	IMM	Robotic Part Removal — 1300T Press	2	1.05
Copper Shop	HEX	Shrink less Vertical M/C	1	2.1
Assembly Shop	Assembly	Scissor Lifter	2	0.05
Press Shop	Press Shop	400T Hydraulic Press Retrofit	1	1.35
General	IMM	Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton)	1	1.5
General	Utilities	Compressed Air Line Re-piping — Block C	1	0.41
General	Safety	Fire Hydrant Network Upgrade	1	0.62
Digitization	Innovation / De	Plant ESG / EMS Monitoring	1	0.4
Digitization	IT	Line-side MES Terminals (32 nos)	1	0.58
New Business	HEX	Mezzanine, Goods Lift & Utilities	1	2.1
New Business	HEX	New HEX Line — Phase 1 Civil & Utilities	1	28.5

The uploaded workbook lands as **12 lines totalling ₹38.99 Cr**, grouped into seven budget heads — Automation ₹1.38 Cr, Copper Shop ₹2.10 Cr, Assembly Shop ₹0.05 Cr, Press Shop ₹1.35 Cr, General ₹2.53 Cr, Digitization ₹0.98 Cr and New Business ₹30.60 Cr. Every cell stays editable afterwards.

Slide 2.4 · Submitted — and handed to the plant head by email

amber

CAPEX Portal

Amber Enterprises

WORKSPACE

Dashboard

Requests

CAPEX Master

Budget Planning

SV

Sunil Verma

CAPEX Master / B...

All Plants

Budget Planning

Author next-FY budget proposals

SV

Sunil Verma

CAPEX Master / B...

Budget Planning

Author next-FY Brown Field budgets. Submitted proposals go to admin for approval, then publish as the new live FY.

RAC

EMS

Component

Fan

Jhajjar Plant 1

New Next-FY Proposal

TARGET FY	LINES	TOTAL	STATUS	CREATED BY
2026-27	12	₹38.99 Cr	With Plant Head	Sunil Verma

View

amber

CAPEX Portal

Amber Enterprises

Workspace

Dashboard

Requests

CAPEX Master

Budget Planning

SV

Sunil Verma

CAPEX Master / B...

Log out

All Plants

Budget Planning

Author next-FY budget proposals

Budget Proposal · Jhajjar Plant 1

Blank draft · status With Plant Head

Target FY 2026-27

Awaiting Plant Head approval (sent via email)

The plant head approves or rejects through the secure link.

Copy link

Preview email

Assembly Shop: ₹0.05 Cr · 1

Automation: ₹1.38 Cr · 2

Copper Shop: ₹2.10 Cr · 1

Digitization: ₹0.98 Cr · 2

General: ₹2.53 Cr · 3

New Business: ₹30.60 Cr · 2

Press Shop: ₹1.35 Cr · 1

Total: ₹38.99 Cr

HEAD	DEPARTMENT	SUB PARTICULARS	QTY	TOTAL (CR)
Automation	HEX	HEX Black Copper Detection	3	0.33
Automation	IMM	Robotic Part Removal — 1300T Press	2	1.05
Copper Shop	HEX	Shrink less Vertical M/C	1	2.1
Assembly Shop	Assembly	Scissor Lifter	2	0.05
Press Shop	Press Shop	400T Hydraulic Press Retrofit	1	1.35
General	IMM	Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton)	1	1.5
General	Utilities	Compressed Air Line Re-piping — Block C	1	0.41
General	Safety	Fire Hydrant Network Upgrade	1	0.62
Digitization	Innovation / De	Plant ESG / EMS Monitoring	1	0.4
Digitization	IT	Line-side MES Terminals (32 nos)	1	0.58
New Business	HEX	Mezzanine, Goods Lift & Utilities	1	2.1
New Business	HEX	New HEX Line — Phase 1 Civil & Utilities	1	28.5

Submit to Plant Head moves the proposal to *With Plant Head* and mints a single-use approval link. The author now sees a banner with two things he can do: **copy the link**, or **preview the email**.

Slide 2.5 · The email

amber

CAPEX Portal

Amber Enterprises

Workspace

Dashboard

Requests

CAPEX Master

Budget Planning

SV

Sunil Verma

CAPEX Master / B...

Log out

All Plants

Budget Planning

Author next-FY budget proposals

Budget Proposal · Jhajjar Plant 1

Blank draft · status With Plant Head

Target FY 2026-27

Awaiting Plant Head approval (sent via email)

The plant head approves or rejects through the secure link.

Copy link

Preview email

Assembly Shop: ₹0.05 Cr · 1

Automation: ₹1.38 Cr · 2

Copper Shop: ₹2.10 Cr · 1

Digitization: ₹0.98 Cr · 2

General: ₹2.53 Cr · 3

New Business: ₹30.60 Cr · 2

Press Shop: ₹1.35 Cr · 1

Total: ₹38.99 Cr

HEAD	DEPARTMENT	SUB PARTICULARS	QTY	TOTAL (CR)
Automation	HEX	HEX Black Copper Detection	3	0.33
Automation	IMM	Robotic Part Removal — 1300T Press	2	1.05
Copper Shop	HEX	Shrink less Vertical M/C	1	2.1
Assembly Shop	Assembly	Scissor Lifter	2	0.05
Press Shop	Press Shop	400T Hydraulic Press Retrofit	1	1.35
General	IMM	Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton)	1	1.5
General	Utilities	Compressed Air Line Re-piping — Block C	1	0.41
General	Safety	Fire Hydrant Network Upgrade	1	0.62
Digitization	Innovation / De	Plant ESG / EMS Monitoring	1	0.4
Digitization	IT	Line-side MES Terminals (32 nos)	1	0.58
New Business	HEX	Mezzanine, Goods Lift & Utilities	1	2.1
New Business	HEX	New HEX Line — Phase 1 Civil & Utilities	1	28.5

Plant Head Budget Approval — Email Preview

To

plant.head@amber-enterprises.in

Subject

Budget Approval — Jhajjar Plant 1 · FY 2026-27

Message

Dear Plant Head,

A next-FY Brown Field budget proposal for Jhajjar Plant 1 (FY 2026-27) requires your approval.

Please review and Approve / Reject using the secure link below:
http://localhost:3000/approve/aprv_budget_bp-f59e213b-d897-4c63-bb4e-5c943a8de749_ed73e235eba74fbda351521f7aac064

Regards,
Amber Enterprises CAPEX Portal

Plant-head approval link

http://localhost:3000/approve/aprv_budget_

Copy


Open link

Cancel

Send to Plant Head

Recipient, subject and body are written for him and are editable; the secure link appears in the body and again as a copyable field. The same email panel is reused at every handoff in the product, so there is one thing to learn rather than eight.

Slide 2.6 · What the plant head sees

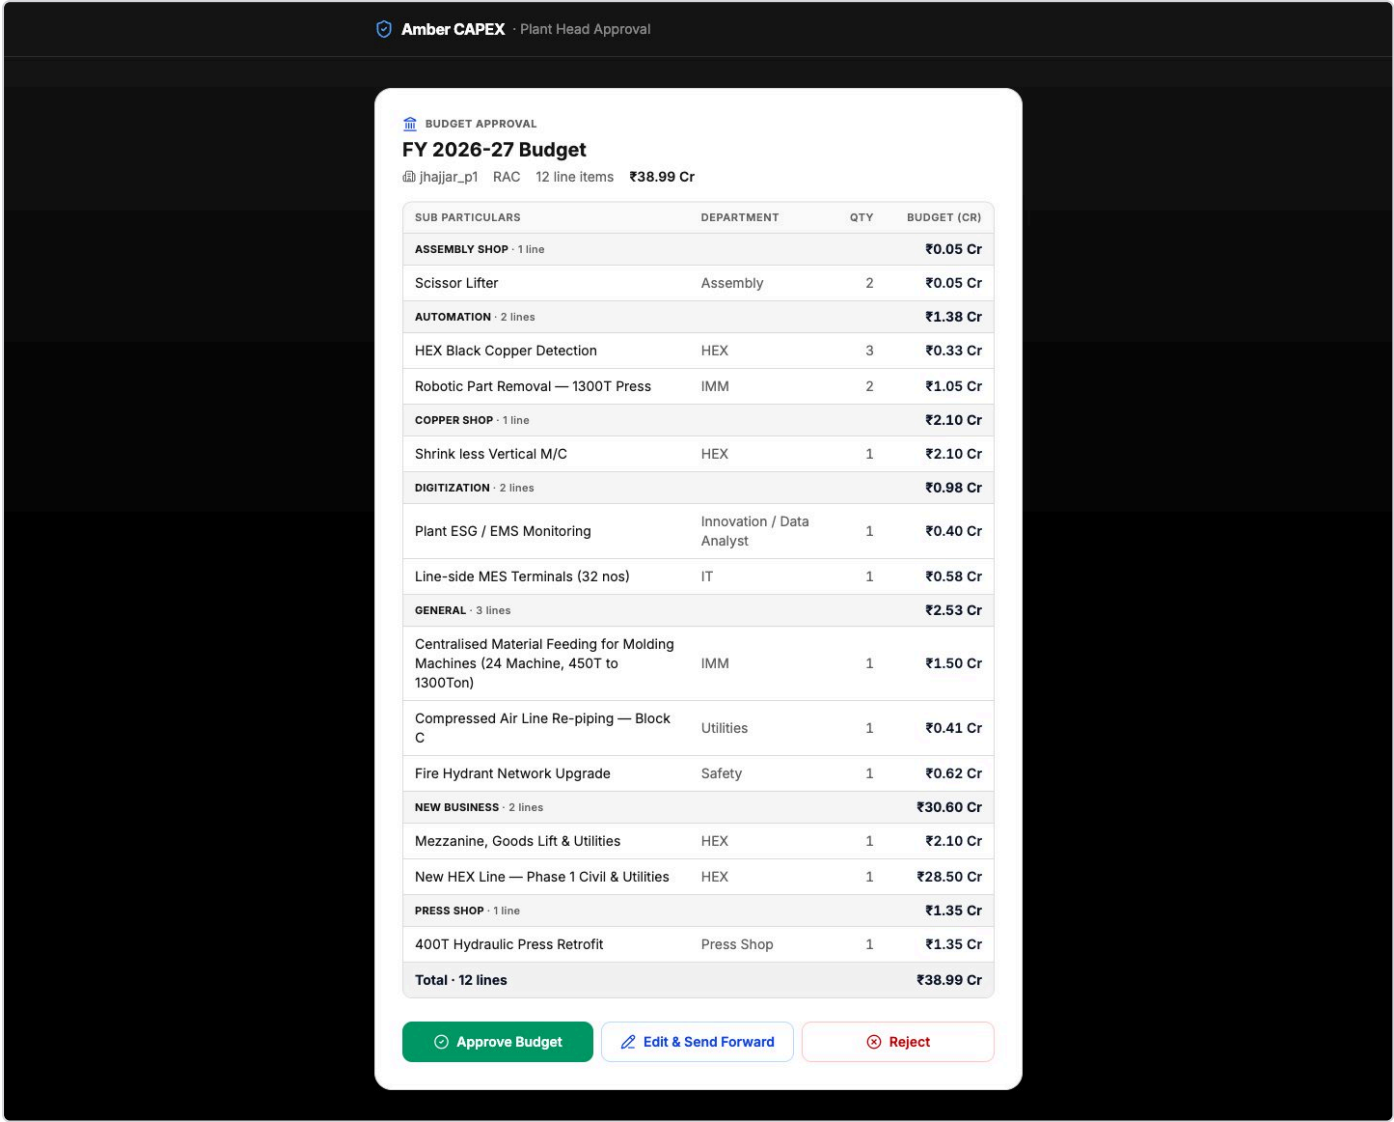

No login, no menu, no navigation — a single page titled **Plant Head Approval** showing the whole proposal grouped by head, with every sub-particular, its department, its quantity and its budget, a subtotal per head and a grand total. Every approver in the chain reviews this same breakdown, so no two gates are ever looking at different numbers.

Three things he can do: approve it, reject it, or — the interesting one — **edit it and send it forward**.

Slide 2.7 · Approvers edit and send forward; they do not send back

Approve Budget

Edit & Send Forward

Reject

Edit & Send Forward

Adjust any line or its budget, add a remark, and send the budget on to Admin with your edits applied. It does not go back to the author.

Reset edits

HEAD	SUB PARTICULARS	DEPARTMENT	QTY	BUDGET (CR)
Automation	HEX Black Copper	HEX	3	0.33
Automation	Robotic Part Rem	IMM	2	1.05
Copper Shop	Shrink less Vertic	HEX	1	2.1
Assembly Shop	Scissor Lifter	Assembly	2	0.05
Press Shop	400T Hydraulic F	Press Shop	1	1.35
General	Centralised Mate	IMM	1	1.5
General	Compressed Air	Utilities	1	0.41
General	Fire Hydrant Net	Safety	1	0.62
Digitization	Plant ESG / EMS	Innovation / Dat	1	0.4
Digitization	Line-slide MES Tr	IT	1	0.58
New Business	Mezzanine, Goo	HEX	1	2.1
New Business	New HEX Line —	HEX	1	26.5
Total				₹36.99 Cr

+ Add line

Submitted ₹38.99 Cr → ₹36.99 Cr (–₹2.00 Cr)

Phase 1 civil scope trimmed — the substation bay moves to FY 2027-28 with the Phase 2 line, so ₹2.00 Cr comes out of this year. Rest of the plan is approved as submitted.


Save Edits & Send to Admin →

The plant head can change any line's budget, quantity, department or description, add lines, remove lines, and attach a remark — then approve **with those edits applied, in one action**. The panel shows the effect live: **submitted ₹38.99 Cr → revised ₹36.99 Cr (–₹2.00 Cr)**, with a **Reset edits** control if he changes his mind.

Here he trims the new HEX line's Phase 1 civil scope by ₹2.00 Cr, and says why:

"Phase 1 civil scope trimmed — the substation bay moves to FY 2027-28 with the Phase 2 line, so ₹2.00 Cr comes out of this year. Rest of the plan is approved as submitted."

This replaced an older send-it-back-for-correction loop. An approver who knows what the number should be can simply set it, and the budget keeps moving forward instead of bouncing.



The link is consumed the moment he decides, so a forwarded copy of the email cannot be used to decide again.

Slide 2.8 · Stage 2 — the administrator sees exactly what changed

amber

CAPEX Portal
Amber Enterprises

WORKSPACE

Dashboard

New Request

Requests

Vendors

CAPEX Master

Budget Planning

Adhoc Budget

Budget Approvals

Accounts

Configurations

< Collapse

SA

Super Admin
Full Access

[->

Log out

All Plants

Budget Approvals

Next-FY proposals & adhoc transfers

SA

Super Admin
Full Access

Budget Approvals

Review next-FY Brown Field budget proposals. Approving publishes the proposal as a new live FY that buyers will use.

WITH ADMIN (1)

Jhajjar Plant 1 · RAC · FY 2026-27

12 lines · ₹36.99 Cr · from FY — · by Sunil Verma

Edit & Send Forward

Reject

Approve → Accounts

PROPOSED FY 2026-27BUDGET · HEAD & SUB PARTICULARS

REVISED IN APPROVAL (1)

Plant Head · 22 Aug, 06:20 am — ₹38.99 Cr → ₹36.99 Cr (–₹2.00 Cr)

"Phase 1 civil scope trimmed — the substation bay moves to FY 2027-28 with the Phase 2 line, so ₹2.00 Cr comes out of this year. Rest of the plan is approved as submitted."

SUB PARTICULARS	DEPARTMENT	QTY	BUDGET (CR)
ASSEMBLY SHOP · 1 line			₹0.05 Cr
Scissor Lifter	Assembly	2	₹0.05 Cr
AUTOMATION · 2 lines			₹1.38 Cr
HEX Black Copper Detection	HEX	3	₹0.33 Cr
Robotic Part Removal — 1300T Press	IMM	2	₹1.05 Cr
COPPER SHOP · 1 line			₹2.10 Cr
Shrink less Vertical M/C	HEX	1	₹2.10 Cr
DIGITIZATION · 2 lines			₹0.98 Cr
Plant ESG / EMS Monitoring	Innovation / Data Analyst	1	₹0.40 Cr
Line-side MES Terminals (32 nos)	IT	1	₹0.58 Cr
GENERAL · 3 lines			₹2.53 Cr
Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton)	IMM	1	₹1.50 Cr
Compressed Air Line Re-piping — Block C	Utilities	1	₹0.41 Cr
Fire Hydrant Network Upgrade	Safety	1	₹0.62 Cr

Budget Approvals is the super admin's screen. The proposal is now *With Admin*, and above the breakdown sits the revision trail: **Plant Head · 22 Aug — ₹38.99 Cr → ₹36.99 Cr (–₹2.00 Cr)**, with the plant head's remark quoted underneath.

The next approver never has to ask what was changed or why. The admin has the same three options — approve, edit and send forward, or reject — and approving here does **not** publish the budget. It moves it to the third gate.

Slide 2.9 · Stage 3 — Global Accounts sign-off publishes the year

 **CAPEX Portal**
Amber Enterprises

WORKSPACE

- Dashboard
- New Request
- Requests
- Vendors
- CAPEX Master
- Budget Planning
- Adhoc Budget
- Budget Approvals**
- Accounts
- Configurations

SA Super Admin
Full Access

Log out

All Plants | **Budget Approvals** | Next-FY proposals & adhoc transfers

 **Budget Approvals**

Review next-FY Brown Field budget proposals. Approving publishes the proposal as a new live FY that buyers will use.

WITH ADMIN (0)

No proposals awaiting approval.

WITH GLOBAL ACCOUNTS (1)

Jhajjar Plant 1 · RAC · FY 2026-27

12 lines · ₹36.99 Cr · admin-approved by super_admin

Global Accounts approve or reject on the secure link — approving publishes FY 2026-27 as the live budget.

Copy link

Preview email

Open

PROPOSED FY 2026-27BUDGET · HEAD & SUB PARTICULARS

REVISED IN APPROVAL (1)

Plant Head · 22 Aug, 06:20 am — ₹38.99 Cr → ₹36.99 Cr (–₹2.00 Cr)

"Phase 1 civil scope trimmed — the substation bay moves to FY 2027-28 with the Phase 2 line, so ₹2.00 Cr comes out of this year. Rest of the plan is approved as submitted."

SUB PARTICULARS	DEPARTMENT	QTY	BUDGET (CR)
ASSEMBLY SHOP · 1 line			₹0.05 Cr
Scissor Lifter	Assembly	2	₹0.05 Cr
AUTOMATION · 2 lines			₹1.38 Cr
HEX Black Copper Detection	HEX	3	₹0.33 Cr
Robotic Part Removal — 1300T Press	IMM	2	₹1.05 Cr
COPPER SHOP · 1 line			₹2.10 Cr
Shrink less Vertical M/C	HEX	1	₹2.10 Cr
DIGITIZATION · 2 lines			₹0.98 Cr
Plant ESG / EMS Monitoring	Innovation / Data Analyst	1	₹0.40 Cr
Line-side MES Terminals (32 nos)	IT	1	₹0.58 Cr
GENERAL · 2 lines			₹0.52 Cr

 **CAPEX Portal**
Amber Enterprises

WORKSPACE

- Dashboard
- New Request
- Requests
- Vendors
- CAPEX Master
- Budget Planning
- Adhoc Budget
- Budget Approvals**
- Accounts
- Configurations

SA Super Admin
Full Access

Log out

All Plants | **Budget Approvals** | Next-FY proposals & adhoc transfers

 **Budget Approvals**

Review next-FY Brown Field budget proposals. Approving publishes the proposal as a new live FY that buyers will use.

WITH ADMIN (0)

No proposals awaiting approval.

WITH GLOBAL ACCOUNTS (1)

Jhajjar Plant 1 · RAC · FY 2026-27

12 lines · ₹36.99 Cr · admin-approved by super_admin

Global Accounts approve or reject on the secure link — approving publishes FY 2026-27 as the live budget.

Copy link

Preview email

Open

PROPOSED FY 2026-27BUDGET · HEAD & SUB PARTICULARS

REVISED IN APPROVAL (1)

Plant Head · 22 Aug, 06:20 am — ₹38.99 Cr → ₹36.99 Cr (–₹2.00 Cr)

"Phase 1 civil scope trimmed — the substation bay moves to FY 2027-28 with the Phase 2 line, so ₹2.00 Cr comes out of this year. Rest of the plan is approved as submitted."

SUB PARTICULARS	DEPARTMENT	QTY	BUDGET (CR)
ASSEMBLY SHOP · 1 line			₹0.05 Cr
Scissor Lifter	Assembly	2	₹0.05 Cr
AUTOMATION · 2 lines			₹1.38 Cr
HEX Black Copper Detection	HEX	3	₹0.33 Cr
Robotic Part Removal — 1300T Press	IMM	2	₹1.05 Cr
COPPER SHOP · 1 line			₹2.10 Cr
Shrink less Vertical M/C	HEX	1	₹2.10 Cr
DIGITIZATION · 2 lines			₹0.98 Cr
Plant ESG / EMS Monitoring	Innovation / Data Analyst	1	₹0.40 Cr
Line-side MES Terminals (32 nos)	IT	1	₹0.58 Cr
GENERAL · 2 lines			₹0.52 Cr

Global Accounts Sign-off — Email Preview

To

satish.accounts@amber-enterprises.in

Subject

Budget Sign-off Needed — Jhajjar Plant 1 · FY 2026-27

Message

Dear Global Accounts team,
A next-FY CAPEX budget has cleared the plant head and admin approvals and needs your final sign-off. Approving it publishes the budget as the live FY 2026-27 master.
Plant: Jhajjar Plant 1
Category: RAC
Target FY: 2026-27
Line items: 12
Total: ₹36.99 Cr
Admin approval: super_admin
Please review and Approve / Reject using the secure link below (no portal login required):
http://localhost:3000/approve/aprv_budget_accounts_bp-f59e213b-d897-4c63-bb4e-5c943a8de749_c9966c89acfa4b1aaa33a1b0b49f1b2a
Regards,
Amber Enterprises CAPEX Portal

Global Accounts sign-off link

http://localhost:3000/approve/aprv_budget_accounts_bp-f59e213b-d897-4c63-bb4e-5c943a8de749_c9966c89acfa4b1aaa33a1b0b49f1b2a

Copy

Open link

Cancel

Send to Global Accounts

Approving at the admin stage mints the Global Accounts link and moves the row into *With Global Accounts*, where the admin can copy the link, preview the email or open it directly.

BUDGET SIGN-OFF · GLOBAL ACCOUNTS

FY 2026-27 Budget

jhajjar_p1 RAC 12 line items ₹36.99 Cr

Already approved by the plant head and the admin (super_admin). Your approval is the final gate — it publishes this proposal as the live FY 2026-27 budget.

REVISED IN APPROVAL (1)

Plant Head · 22 Aug, 06:20 am — ₹38.99 Cr → ₹36.99 Cr (–₹2.00 Cr)

"Phase 1 civil scope trimmed — the substation bay moves to FY 2027-28 with the Phase 2 line, so ₹2.00 Cr comes out of this year. Rest of the plan is approved as submitted."

SUB PARTICULARS	DEPARTMENT	QTY	BUDGET (CR)
ASSEMBLY SHOP · 1 line			₹0.05 Cr
Scissor Lifter	Assembly	2	₹0.05 Cr
AUTOMATION · 2 lines			₹1.38 Cr
HEX Black Copper Detection	HEX	3	₹0.33 Cr
Robotic Part Removal — 1300T Press	IMM	2	₹1.05 Cr
COPPER SHOP · 1 line			₹2.10 Cr
Shrink less Vertical M/C	HEX	1	₹2.10 Cr
DIGITIZATION · 2 lines			₹0.98 Cr
Plant ESG / EMS Monitoring	Innovation / Data Analyst	1	₹0.40 Cr
Line-side MES Terminals (32 nos)	IT	1	₹0.58 Cr
GENERAL · 3 lines			₹2.53 Cr
Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton)	IMM	1	₹1.50 Cr

The page tells him plainly what his click does: *"Already approved by the plant head and the admin. Your approval is the final gate — it publishes this proposal as the live FY 2026-27 budget."* He sees the same breakdown and the same revision trail as everyone before him.



Approved

Your sign-off has been recorded and this proposal is now published as the live FY budget.

Slide 2.10 · The budget approval chain, in one picture

Draft (blank) → Plant head → Admin → Global Accounts → Published as the live FY budget

The first two approvers can **edit the numbers and send the budget forward** with their changes applied — the next approver sees exactly what was changed and why. Any of the three gates can **reject**. Nothing is spendable until the third gate signs.

Slide 2.11 · FY 2026-27 is now live money

CAPEX Portal
Amber Enterprises

WORKSPACE

- Dashboard
- New Request
- Requests
- Vendors
- CAPEX Master**
- Budget Planning
- Adhoc Budget
- Budget Approvals

All Plants

CAPEX Master > Per-plant budget planning

SA Super Admin Full Access

CAPEX Master

Select a plant to manage its annual budget · FY 2026-27

FY 2026-27 Clone FY

Brown Field Green Field Digitisation Information Technology

Amber Choose a business category before selecting a plant.

RAC
Brown Field master
₹36.99
Crore · 12 line items

EMS
Brown Field master
No items for FY 2026-27

Component
Brown Field master
No items for FY 2026-27

Fan
Brown Field master
No items for FY 2026-27

CAPEX Portal
Amber Enterprises

WORKSPACE

- Dashboard
- New Request
- Requests
- Vendors
- CAPEX Master**
- Budget Planning
- Adhoc Budget
- Budget Approvals
- Accounts
- Configurations

All Plants

CAPEX Master > Per-plant budget planning

SA Super Admin Full Access

CAPEX Master

Select a plant to manage its annual budget · FY 2026-27

FY 2026-27 Clone FY

Brown Field Green Field Digitisation Information Technology

< Categories / RAC

Jhajjar Plant 1
Haryana
₹36.99
Crore · 12 line items

Jhajjar Plant 2
Haryana
No items for FY 2026-27

DDN-4
Uttarakhand
No items for FY 2026-27

DDN-5
Uttarakhand
No items for FY 2026-27

DDN-6
Uttarakhand
No items for FY 2026-27

SUPA
Maharashtra
No items for FY 2026-27

Rudrapur
Uttarakhand
No items for FY 2026-27

Sri City-1
Andhra Pradesh
No items for FY 2026-27

Sri City-2
Andhra Pradesh
No items for FY 2026-27

SA Super Admin Full Access

Log out

The proposal's twelve lines are now the live FY 2026-27 budget. Drill down category → plant → head → line item: RAC ₹36.99 Cr → Jhajjar Plant 1 ₹36.99 Cr, with every other plant reading "No items for FY 2026-27" until it publishes its own.

CAPEX Portal
Amber Enterprises

WORKSPACE

- Dashboard
- New Request
- Requests
- Vendors
- CAPEX Master
- Budget Planning
- Adhoc Budget
- Budget Approvals
- Accounts
- Configurations

SA Super Admin
Full Access

Log out

All PlantsCAPEX MasterPer-plant budget planning

Plants / Jhajjar Plant 1Brown FieldRAC

Brown FieldGreen FieldDigitisationInformation TechnologyFY2026-27Plan Next-FY Budget

Select a budget head for Jhajjar Plant 1.

Automation
₹1.38 Cr
2 sub-particulars

General
₹2.53 Cr
3 sub-particulars

Digitization
₹0.98 Cr
2 sub-particulars

New Business
₹28.60 Cr
2 sub-particulars

Assembly Shop
₹0.05 Cr
1 sub-particular

Copper Shop
₹2.10 Cr
1 sub-particular

Press Shop
₹1.35 Cr
1 sub-particular

CAPEX Portal
Amber Enterprises

WORKSPACE

- Dashboard
- New Request
- Requests
- Vendors
- CAPEX Master
- Budget Planning
- Adhoc Budget
- Budget Approvals
- Accounts
- Configurations

SA Super Admin
Full Access

Log out

All PlantsCAPEX MasterPer-plant budget planning

Plants / Jhajjar Plant 1 / GeneralGeneral

Brown FieldGreen FieldDigitisationInformation TechnologyFY2026-27Plan Next-FY Budget

Automation ₹1.38 CrGeneral ₹2.53 CrDigitization ₹0.98 CrNew Business ₹28.60 CrAssembly Shop ₹0.05 CrCopper Shop ₹2.10 CrPress Shop ₹1.35 Cr

#	HEAD	DEPARTMENT	SUB PARTICULARS	QTY	RATE (CR)	TOTAL COST (CR)	REQ. NO.	SOURCING
General								
1	General	IMM	Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton)	1	—	1.50	—	—
2	General	Utilities	Compressed Air Line Re-piping — Block C	1	—	0.41	—	—
3	General	Safety	Fire Hydrant Network Upgrade	1	—	0.62	—	—
JHAJJAR PLANT 1 — GRAND TOTAL (3 items)						₹2.53 Cr		

Two things worth noticing on the line-item table:

- The **padlock** on each row. A live budget year is **read-only**. Nobody can quietly edit approved money. The only mid-year change is an ad-hoc transfer between heads, which itself needs the administrator's approval (Part 13).

- The **Req. No.** and **Sourcing** columns. Once a request consumes a budget line, it appears here, so the budget row and the spend against it sit side by side.
-

Part 3 — The supply base

Slide 3.1 · Vendor Master

amber

CAPEX Portal

Amber Enterprises

WORKSPACE

Dashboard

New Request

Requests

Vendors

CAPEX Master

Budget Planning

Adhoc Budget

Budget Approvals

Accounts

Configurations

< Collapse

SA Super Admin

Full Access

[-> Log out

All Plants

Vendor Directory

Manage and onboard vendors

SA Super Admin

Full Access

Vendor Master

All onboarded vendors across CAPEX requests.

Onboard New Vendor

Search by name, code, or category...

VENDOR CODE	NAME	CATEGORY	GSTIN	CONTACT NAME	CONTACT EMAIL	PAYMENT TERMS	ACTIONS
VND-001	Tata Motors Ancillaries	Machinery	27AABCT3518Q1ZK	Ramesh Tiwari	ramesh.tiwari@tata-ancillaries.in	Net-30	View
VND-002	Siemens India	IT	27AAACS6560P1ZX	Anita Sharma	anita.sharma@siemens.com	Net-60	View
VND-003	Bosch Packaging	Tooling	29AABCB1234A1ZZ	Klaus Mueller	k.mueller@bosch-packaging.in	Advance	View
VND-004	L&T Infrastructure	Infrastructure	27AAACL1234B1ZP	Suresh Iyer	suresh.iyer@lnt-infra.com	Net-30	View
VND-005	Delta Electronics	Machinery	07AABCD5678E1ZQ	Priya Venkatesh	p.venkatesh@delta-electronics.in	Net-60	View

Every onboarded supplier, with its code, category, GSTIN, contact and payment terms. The payment terms matter later: they are what generates the milestone split on the purchase order — the 30 / 60 / 10 you will see in Part 9 comes from the vendor record, not from a number somebody typed.

Expanding a row shows the banking and registration detail that Accounts need.

Slide 3.2 · Adding a vendor

The screenshot shows a web application interface for adding a vendor. A modal window titled "Add Vendor to Request" is open, displaying a form with the following fields:

- Existing Vendors** / **Onboard New** (tabs)
- VENDOR CODE ***: VND-XXX
- VENDOR NAME ***: Company name
- CATEGORY ***: Select category (dropdown)
- GSTIN**: 27AABCT3518Q1ZK
- PAN**: AABCT3518Q
- CONTACT NAME**: Full name
- CONTACT EMAIL ***: contact@vendor.com
- PAYMENT TERMS**: Select terms (dropdown)
- BANK NAME**: HDFC Bank
- ACCOUNT NUMBER**: Account number
- IFSC**: HDFC0001234

At the bottom of the modal are two buttons: "Cancel" and "Onboard & Invite".

Vendors can be onboarded formally here, or added on the fly by the sourcing team during a quotation round — including a **one-time vendor** who is quoting for a single machine and will never be onboarded, and a **foreign vendor**, which switches on the Incoterms questionnaire (Part 10).

Part 4 — Raising a request

Slide 4.1 · Step 1 — what kind of capital expenditure is this?

 CAPEX Portal
Amber Enterprises

Jhajjar Plant 1

New Request

Submit a capital expenditure request

WORKSPACE

- Dashboard
- New Request
- Requests

< Back to requests

New CAPEX Request

Amber Choose a field type to begin.

Brown Field

Capex for existing plants — machinery, automation, utilities, and site improvements scoped by RAC/EMS/Component/Fan.

Green Field

New Green Field plant budgets — select plant, section, and head from CAPEX Master.

Digitisation

Digitisation capex from the dedicated Digitisation master (migrated from Brown Field Digitization).

Information Technology

IT capex — hardware, software, network, cloud, and support from the IT master.

Arjun Mehta, the buyer at Jhajjar Plant 1, starts a request. The first choice changes the route the request takes:

Kind	What it means	How it is routed
Brown Field	Existing plants — machinery, automation, utilities, site work	Needs plant-head approval first
Green Field	A brand-new plant being built	Goes straight to sourcing
Digitisation	Digital, MES and ESG capital expenditure	Needs plant-head approval
Information Technology	Hardware, software, network, cloud	Needs plant-head approval

Slide 4.2 · Steps 2 to 4 — narrowing down to approved money

Business category, then plant. Notice that the buyer at Jhajjar Plant 1 is offered exactly one plant. A plant buyer cannot raise a request against another plant's budget; there is no dropdown to get it wrong in.

 CAPEX Portal
Amber Enterprises

Jhajjar Plant 1

New Request

Submit a capital expenditure request

WORKSPACE

- Dashboard
- New Request
- Requests

< Back to plants

Change category

Change field type

New CAPEX Request

Amber Brown Field RAC Choose a budget head — allocated budget is shown on each card.

Automation

₹1.38 Cr
2 sub-particulars

General

₹2.53 Cr
3 sub-particulars

Digitization

₹0.98 Cr
2 sub-particulars

New Business

₹28.60 Cr
2 sub-particulars

Assembly Shop

₹0.05 Cr
1 sub-particular

Copper Shop

₹2.10 Cr
1 sub-particular

Press Shop

₹1.35 Cr
1 sub-particular

Then the budget head — and each card **shows the money approved against it**. Heads with no approved lines simply do not appear. By the time the buyer reaches the grid, he is already inside approved money.

Every step has **Back** and **Change...** controls, and changing the scope clears the dependent rows, so a line item can never be carried across into the wrong budget head by accident.

Slide 4.3 · The line-item grid

CAPEX Portal
Amber Enterprises

WORKSPACE

- Dashboard
- New Request
- Requests

< Collapse

AM Arjun Mehta
Buyer - Jhajar P1

Log out

Jhajar Plant 1New Request> Submit a capital expenditure request

AM Arjun Mehta
Jhajar Plant 1

< Back to budget heads

1 Fill Details2 Review3 Submitted

New CAPEX Request

AmberBrown FieldRACGeneral

Add one row per line item. Fields marked * are required. Budget is in ₹ (rupees).

Change field typeChange categoryChange plantChange head

#	HEAD	SUB PARTICULAR *	QTY *	ALLOCATED BUDGET	
1	General	Select...	e.g. 2 units	—	X
	Share complete description...				
	PREFERRED VENDOR — None — Sourcing will obtain quotations via RFQ or reverse auction — buyers do not enter prices.				

+ Add Row

1 item * required per rowReview Request >

Columns: # · Head (locked) · Sub Particular · Qty · Allocated Budget (read-only).

The **Sub Particular** is a dropdown of that head's approved lines — it *is* the item's identity, and selecting it pulls the approved allocation in with it. Beneath each row sits a required description, which is the specification the vendors will quote against, and an optional preferred vendor with a reason.

Note the line under the vendor box: "*Sourcing will obtain quotations via RFQ or reverse auction — buyers do not enter prices.*" Requesters describe **what** they need. Sourcing discovers **what it costs**. That separation is the point.

amber

CAPEX Portal

Amber Enterprises

Workspace

Dashboard

New Request

Requests

Arjun Mehta

Buyer - Jhajjar P1

Log out

Jhajjar Plant 1

New Request

Submit a capital expenditure request

AM

Arjun Mehta

Jhajjar Plant 1

Back to budget heads

1

Fill Details

2

Review

3

Submitted

New CAPEX Request

Amber

Brown Field

RAC

General

Add one row per line item. Fields marked * are required. Budget is in ₹ (rupees).

Change field type

Change category

Change plant

Change head

#	HEAD	SUB PARTICULAR *	QTY *	ALLOCATED BUDGET	
1	General	Centralised Material Feeding for Molding Machines (24 Machine)	1	₹1,50,00,000	×
	Centralised granule feeding system for 24 injection moulding machines (450T-1300T), covering vacuum conveying, central dryers, dosing units, closed-loop piping and PLC control with recipe management. Must integrate with the existing IMM line controls and support colour changeover without manual hopper cleaning. Commissioning and operator training included.				
	PREFERRED VENDOR Tata Motors Ancillaries WHY THIS VENDOR (OPTIONAL) Supplied and commissioned the same central feeding system at DDN-5 in 2024; their controls already speak to our IMM line PLCs. Sourcing will obtain quotations via RFQ or reverse auction — buyers do not enter prices.				
2	General	Compressed Air Line Re-piping — Block C	1	₹41,00,000	×
	Complete re-piping of the Block C compressed-air header in stainless/aluminium modular pipe — approximately 620 running metres including drop legs, isolation valves, filters, condensate drains and flow meters at each shop boundary. Existing MS headers to be removed. Leak-down test at 7 bar and a metered leakage report are part of handover.				
	PREFERRED VENDOR L&T Infrastructure				

+ Add Row

2 items * required per row

Review Request

Two lines, both under the General head:

- Centralised Material Feeding for Molding Machines — qty 1, allocated ₹1,50,00,000, preferred vendor Tata Motors Ancillaries, with the reason recorded.
- Compressed Air Line Re-piping — Block C — qty 1, allocated ₹41,00,000, preferred vendor L&T Infrastructure.

Slide 4.4 · Review, submit, and the notification that goes out

 CAPEX Portal
Amber Enterprises

Workspace

Dashboard

New Request

Requests

Collapse

Arjun Mehta
Buyer - Jhajjar P1

Log out

Jhajjar Plant 1

New Request

Submit a capital expenditure request

AM

Arjun Mehta
Jhajjar Plant 1

Back to edit details

Fill Details

2 Review

3 Submitted

Confirm Your Request

Review all items below. Once submitted, requests are routed immediately to sourcing.

ITEM 1

Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton)

General · Qty 1 · Jhajjar Plant 1

Centralised granule feeding system for 24 injection moulding machines (450T–1300T), covering vacuum conveying, central dryers, dosing units, closed-loop piping and PLC control with recipe management. Must integrate with the existing IMM line controls and support colour changeover without manual hopper cleaning. Commissioning and operator training included.

Preferred vendor: **Tata Motors Ancillaries** — Supplied and commissioned the same central feeding system at DDN-5 in 2024; their controls already speak to our IMM line PLCs.

Assigned to Neha Kapoor

ITEM 2

Compressed Air Line Re-piping — Block C

General · Qty 1 · Jhajjar Plant 1

Complete re-piping of the Block C compressed-air header in stainless/aluminium modular pipe — approximately 620 running metres including drop legs, isolation valves, filters, condensate drains and flow meters at each shop boundary. Existing MS headers to be removed. Leak-down test at 7 bar and a metered leakage report are part of handover.

Preferred vendor: **L&T Infrastructure**

Assigned to Neha Kapoor

Edit Details

Submit Request (2 items)

A three-step wizard — Fill Details, Review, Submitted. Review restates each line with its allocation, its specification and its preferred vendor.

 CAPEX Portal
Amber Enterprises

Workspace

Dashboard

New Request

Requests

Collapse

Arjun Mehta
Buyer - Jhajjar P1

Log out

Jhajjar Plant 1

New Request

Submit a capital expenditure request

AM

Arjun Mehta
Jhajjar Plant 1

Back to requests

Fill Details

Review

3 Submitted

Request Submitted (2 items)

Routed to the sourcing team. A confirmation email has been sent.

EMAIL PREVIEW

To: Neha Kapoor <sourcing@amberenterprises.in>

From: Arjun Mehta <procurement@amberenterprises.in>

Subject: CAPEX Request — 2 items submitted [22 August 2026]

Dear Neha Kapoor,

A new CAPEX request was submitted by **Arjun Mehta** and assigned to you for sourcing. Please review and initiate vendor outreach at the earliest.

#	Item	Qty	Budget	Plant
1	Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton)	1	—	Jhajjar Plant 1
2	Compressed Air Line Re-piping — Block C	1	—	Jhajjar Plant 1

Automated notification — Amber Enterprises CAPEX Portal

Create Another Request

View Submitted Request

View All Requests

On submit the request gets its number, a sourcing engineer is assigned automatically — buyers never pick one — and the confirmation screen shows the notification that went to sourcing, with the item table inline.

Slide 4.5 · The request list

 **CAPEX Portal**
Amber Enterprises

WORKSPACE

- Dashboard
- New Request
- Requests**

< Collapse

 Log out

Jhajjar Plant 1 | **CAPEX Requests** > Vendor sourcing & negotiation

CAPEX Requests
Your submitted requests — 2 requests

Filter by status: All Statuses

REQ. NO.	SUBJECT	STATUS	PLANT	FINALIZED	DATE	ACTION
CAP-2627-0001	Centralised Material Feed... 2 items	 With Plant Head	Jhajjar Plant 1	—	22 Aug 2026	View
CAP-2627-0002	Shrink less Vertical M/C	 With Plant Head	Jhajjar Plant 1	—	22 Aug 2026	View

CAP-2627-0001 · *Centralised Material Feeding...* · **2 items** · **With Plant Head** · Jhajjar Plant 1 · assigned to Neha Kapoor. The number encodes the year: CAP- **2627** -0001 is the first request of FY 2026-27.

A second request, CAP-2627-0002 for a *Shrink less Vertical M/C* against the Copper Shop head, was raised the same way. It is the one that goes to a reverse auction in Part 11.

Slide 4.6 · The request detail — allocated against estimated, per line

CAPEX Portal
Amber Enterprises

WORKSPACE

- Dashboard
- New Request
- Requests

Arjun Mehta
Buyer · Jhajjar P1

Log out

Jhajjar Plant 1CAPEX DetailRequest view

With Plant Head

MultipleQty: 2 Items₹1,91,00,000Neha KapoorCAP-2627-0001Brown Field71340ab1...

REQUEST DETAILS

FIELD TYPEBrown FieldPLANTJhajjar Plant 1, HaryanaSUBMITTED22 Aug 2026ITEMS2

#	DESCRIPTION	CATEGORY	QTY	ALLOCATED	EST. COST	STATUS	VENDOR	DOC
1	Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton) Other Brown Field · General Centralised granule feeding system for 24 Injection moulding machines (450T–1300T), covering vacuum conveying, central dryers, dosing units, closed-loop piping and PLC control with recipe management. Must integrate with the existing IMM line controls and support colour changeover without manual hopper cleaning. Commissioning and operator training included.	General	1	₹1,50,00,000	₹1,50,00,000	On budget	Tata Motors Ancillaries	—
2	Compressed Air Line Re-piping — Block C Other Brown Field · General Complete re-piping of the Block C compressed-air header in stainless/aluminium modular pipe — approximately 620 running metres including drop legs, isolation valves, filters, condensate drains and flow meters at each shop boundary. Existing MS headers to be removed. Leak-down test at 7 bar and a metered leakage report are part of handover.	General	1	₹41,00,000	₹41,00,000	On budget	L&T Infrastructure	—
BUDGET SUMMARY				Allocated: ₹1,91,00,000	Est. Cost: ₹1,91,00,000	On budget		

PREFERRED VENDOR
Tata Motors Ancillaries
Supplied and commissioned the same central feeding system at DDN-5 in 2024; their controls already speak to our IMM line PLCs.

QUOTATION
VENDOR QUOTATIONS (0)
No vendor quotation has been captured yet — sourcing will obtain quotations by RFQ or reverse auction after approval.

Awaiting Plant Head approval (sent via email).
Submitted by Arjun Mehta · jhajjar_p1 · Assigned to Neha Kapoor
Share the secure link below with the plant head to approve or reject.


Copy linkPreview email

The detail page is the spine of the product; everyone in the chain works from it. At this stage it shows both line items with the money **allocated** to them, the **estimated cost**, and an **on budget / ₹X over** chip per line, plus a summary row totalling both. Underneath sit the preferred vendor and reason, an empty quotation section, and the amber banner handing the request to the plant head.

Right at the bottom of the page — visible in later screens — is the **status history**: every transition, who made it and when, appended and never edited.

Part 5 — Plant-head approval, by email

Slide 5.1 · The email

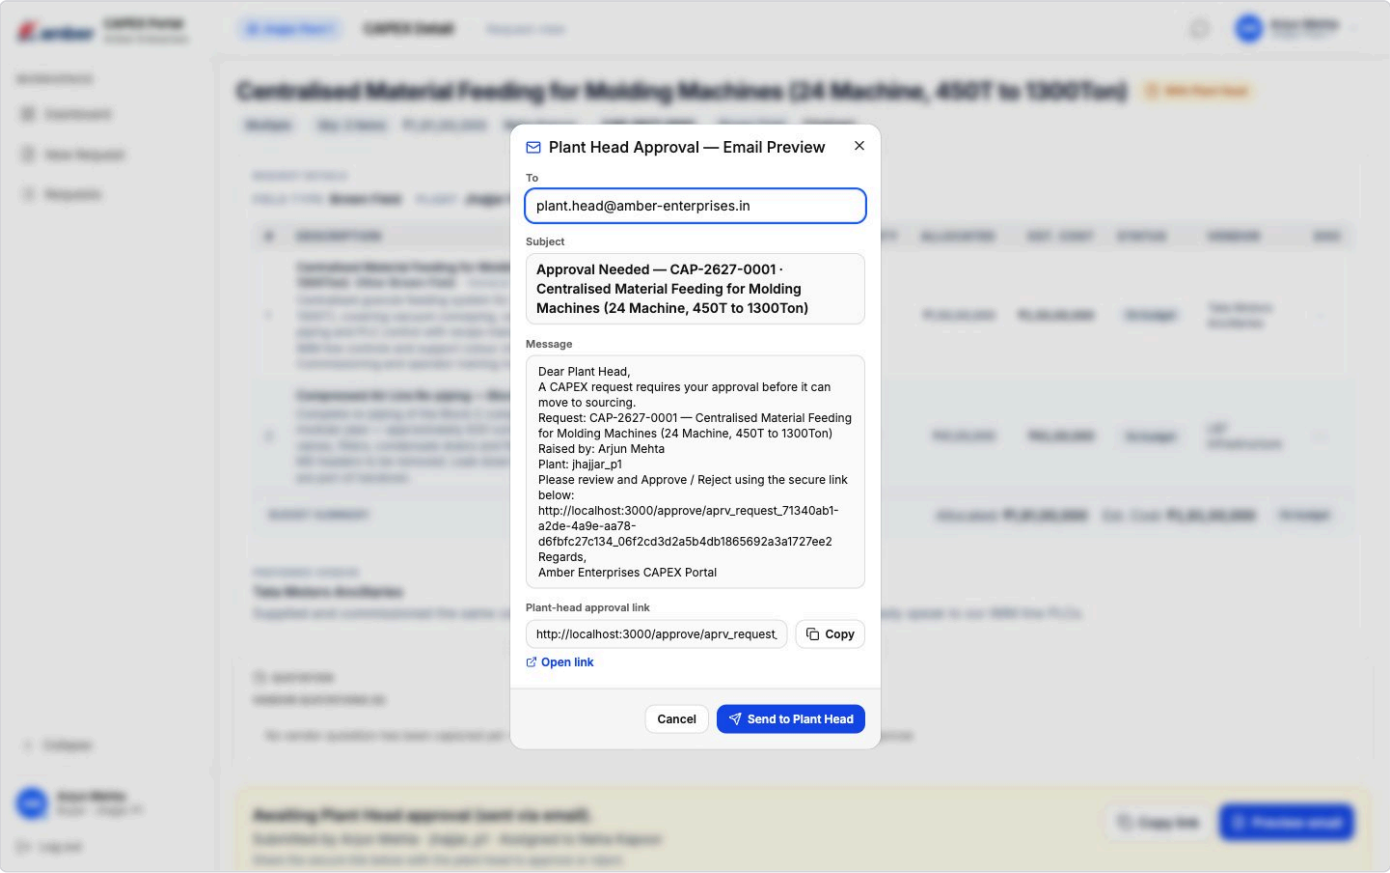

The same email panel as the budget gate, addressed to the plant head, carrying a link that does exactly one thing.

Slide 5.2 · The plant head's page

Amber CAPEX · Plant Head Approval

CAPEX REQUEST APPROVAL

Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton)
CAP-2627-0001

Field Type: **Brown Field**Plant: **jhajjar_p1**
Category: **Multiple**Priority: **Medium**

BUDGET & QUOTATION

#	ITEM	QTY	ALLOCATED	EST. COST	VS BUDGET	PREFERRED VENDOR
1	Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton) - General Centralised granule feeding system for 24 injection moulding machines (450T-1300T), covering vacuum conveying, central dryers, dosing units, closed-loop piping and PLC control with recipe management. Must integrate with the existing IMM line controls and support colour changeover without manual hopper cleaning. Commissioning and operator training included.	1	₹1,50,00,000	₹1,50,00,000	On budget	Tata Motors Ancillaries
2	Compressed Air Line Re-piping — Block C - General Complete re-piping of the Block C compressed-air header in stainless/aluminium modular pipe — approximately 620 running metres including drop legs, isolation valves, filters, condensate drains and flow meters at each shop boundary. Existing MS headers to be removed. Leak-down test at 7 bar and a metered leakage report are part of handover.	1	₹41,00,000	₹41,00,000	On budget	L&T Infrastructure
Total - 2 lines			₹1,91,00,000	₹1,91,00,000	On budget	

VENDOR QUOTATIONS (0)
No vendor quotation has been captured yet — sourcing will obtain quotations by RFQ or reverse auction after approval.

Approve for Sourcing

Reject

Request number, field type, plant, priority, and a table of the requested items with **allocated**, **estimated cost** and a **vs budget** chip on each line and on the total. If quotations had already been captured, they would be listed here too, compared on a common basis.

Two buttons: **Approve for Sourcing** or **Reject**. This gate is deliberately about *"should we buy this at all?"* — not about price, which nobody knows yet.

Part 6 — Sourcing: the quotation round

Slide 6.0 · The shape of a sourcing round



A vendor cannot see a price field until they have accepted the Commercial Terms, the Performance Bank Guarantee and the Delay Liability Clause. A vendor cannot be awarded until Amber's Technical team has signed off their machine specification.

Slide 6.1 · In sourcing

The screenshot shows the 'In sourcing' interface. On the left is a sidebar with a 'Collapse' button and the user's name 'Neha Kapoor'. The main content area is divided into three sections:

- Sourcing setup**: Includes a sub-header 'Optionally require an item trial before you approve a vendor. Add vendors from the invite options below.' and a checked checkbox 'Require an item trial before final payment' with a descriptive note.
- RFQ — Request for Quotation**: Includes a sub-header 'Vendors quote each line first. Counter inline, set the per-line Final Decision, then accept — or escalate to a live auction.' and two buttons: 'Invite vendors (send link)' and 'Invite new vendor'. Below these buttons is a message: 'No vendors invited yet. Invite vendors to send them the quotation link.'
- STATUS HISTORY**: A list of status changes, including 'In Sourcing' by Plant Head (email) on 22 Aug 2026, 06:48, and 'With Plant Head' by Arjun Mehta on 22 Aug 2026, 06:40.

Approval flips the request to **In Sourcing** and hands it to Neha Kapoor. Two new sections appear on the detail page.

The first is **Sourcing setup**, and it carries one switch: **require an item trial before final payment**. Ticked *before* awarding, it means the winning vendor will have to upload evidence that the machine works, and the last payment instalment stays locked until sourcing accepts it. It is ticked for this request.

The second is the **RFQ panel**. Brown Field requests are quotation-first by default; a reverse auction can only be escalated out of a quotation round that already has competing prices, never started cold.

Slide 6.2 · Inviting vendors — and choosing their paperwork

 CAPEX Portal
Amber Enterprises

WORKSPACE

- Dashboard
- Requests
- Vendors
- CAPEX Master
- Budget Planning
- Adhoc Budget
- Accounts

NK Neha Kapoor
Sourcing Member

Log out

All PlantsCAPEX DetailRequest view

2

Complete re-piping of the block C compressed-air header in stainless/aluminium modular pipe — approximately 620 running metres including drop legs, isolation valves, filters, condensate drains and flow meters at each shop boundary. Existing MS headers to be removed. Leak-down test at 7 bar and a metered leakage report are part of handover.

General1

₹41,00,000₹41,00,000

On budget

L&T Infrastructure

BUDGET SUMMARY

Allocated: ₹1,91,00,000Est. Cost: ₹1,91,00,000On budget

PREFERRED VENDOR

Tata Motors Ancillaries
Supplied and commissioned the same central feeding system at DDN-5 in 2024; their controls already speak to our IMM line PLCs.

QUOTATION

VENDOR QUOTATIONS (0)

No vendor quotation has been captured yet — sourcing will obtain quotations by RFQ or reverse auction after approval.

Sourcing setup

Optionally require an item trial before you approve a vendor. Add vendors from the invite options below.

☒ **Require an item trial before final payment** — after the advance is paid, the awarded vendor uploads a trial video / photo / report for your approval; the final payment stays blocked until you approve it. Set this before approving the vendor.

RFQ — Request for Quotation

Vendors quote each line first. Counter inline, set the per-line Final Decision, then accept — or escalate to a live auction.

Invite vendors (send link) · 2 selected

Invite new vendor

CHOOSE VENDORS & THE DOCUMENTS EACH MUST APPROVE

ADD CUSTOM DOCUMENT

Document name (e.g. NDA)

Optional details / clause text

+ Add

☒ **Tata Motors Ancillaries**
VND-001

SEND: ☒ Commercial Terms ☒ Performance Bank Guarantee (PBG) ☒ Delay Liability Clause (DLC) ☐ Payment Terms

☐ **Siemens India**
VND-002

☐ **Bosch Packaging**
VND-003

☒ **L&T Infrastructure**
VND-004

Send link

No vendors invited yet. Invite vendors to send them the quotation link.

STATUS HISTORY

In Sourcing

Plant Head (email)

22 Aug 2026, 06:48

With Plant Head

Arjun Mehta

22 Aug 2026, 06:40

The picker is titled "**Choose vendors & the documents each must approve.**" Per vendor, sourcing selects which contracts go out with the enquiry:

- **Commercial Terms**
- **Performance Bank Guarantee** — 10% of order value, held through the warranty period
- **Delay Liability Clause** — the penalty regime for late delivery
- **Payment Terms** — defaulted on for one-time vendors
- **Add custom document** — any additional clause, by name and text

This is per vendor, not per enquiry: a long-standing supplier and a one-time vendor can be sent different packages in the same round.

Slide 6.3 · The comparison grid appears

 **CAPEX Portal**
Amber Enterprises

WORKSPACE

Dashboard

Requests

Vendors

CAPEX Master

Budget Planning

Adhoc Budget

Accounts

All Plants

CAPEX Detail

Request view

 **Neha Kapoor**
Machinery

2

Complete re-piping of the Block C compressed-air header in stainless/aluminium modular pipe — approximately 620 running metres including drop legs, isolation valves, filters, condensate drains and flow meters at each shop boundary. Existing MS headers to be removed. Leak-down test at 7 bar and a metered leakage report are part of handover.

General

1

₹41,00,000

₹41,00,000

On budget

L&T Infrastructure

BUDGET SUMMARY

Allocated: ₹1,91,00,000

Est. Cost: ₹1,91,00,000

On budget

PREFERRED VENDOR

Tata Motors Ancillaries

Supplied and commissioned the same central feeding system at DDN-5 in 2024; their controls already speak to our IMM line PLCs.

QUOTATION

VENDOR QUOTATIONS (0)

No vendor quotation has been captured yet — sourcing will obtain quotations by RFQ or reverse auction after approval.

Sourcing setup

Optionally require an item trial before you approve a vendor. Add vendors from the invite options below.

☒ **Require an item trial before final payment** — after the advance is paid, the awarded vendor uploads a trial video / photo / report for your approval; the final payment stays blocked until you approve it. Set this before approving the vendor.

 **RFQ — Request for Quotation**

Vendors quote each line first. Counter inline, set the per-line Final Decision, then accept — or escalate to a live auction.

2 awaiting quote

 Invite vendors (send link)

 Invite new vendor

ITEM	DESCRIPTION	QTY	HSN / GST	Q1 VND-001 Tata Motors Ancillaries Awaiting Quote Copy link	Q2 VND-004 L&T Infrastructure Awaiting Quote Copy link	FINAL DECISION
Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton) General	Centralised granule feeding system for 24 injection moulding machines (450T–1300T), covering vacuum conveying, central dryers, dosing units, closed-loop piping and PLC control with recipe management. Must integrate with the existing IMM line controls and support colour changeover without manual hopper cleaning. Commissioning and operator training included.	1	Awaiting HSN	—	—	PRICE (₹) 0 DISC % 0 Select vendor... Price x Qty: ₹0
Compressed Air Line Re-piping — Block C General	Complete re-piping of the Block C compressed-air header in stainless/aluminium modular pipe — approximately 620 running metres including drop legs, isolation valves, filters, condensate drains and flow meters at each shop boundary. Existing MS headers to be removed. Leak-down test at 7 bar and a metered leakage report are part of handover.	1	Awaiting HSN	—	—	PRICE (₹) 0 DISC % 0 Select vendor... Price x Qty: ₹0
Transportation / Freight				—	—	
Packing / Forwarding				—	—	
Service / Installation				—	—	
Delivery Lead Time (Weeks)				—	—	
Warranty (Years)				—	—	
Currency				—	—	
Grand Total (incl. GST)				—	—	
ACTIONS				Awaiting vendor quote Copy link	Awaiting vendor quote Copy link	

< Collapse

 **Neha Kapoor**
Sourcing Member

[Log out](#)

This grid is the sourcing team's working surface for the rest of the round: **line items as rows, vendors as columns**. Both vendors read *Awaiting Quote*; the HSN column reads *Awaiting HSN*, because the vendor supplies it; and the right-hand **Final Decision** column — price, discount, vendor, computed net — is already there, per line.

Slide 6.4 · The vendor's first screen is terms, not prices

 REVERSE AUCTION

CAP-2627-0001: Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton)

You are bidding as: **Tata Motors Ancillaries** (VND-001)

All prices in **INR**



First, Approve the Contract Terms

Please review and accept the documents below. Your quotation form unlocks once you accept.



Approval Documents

Please review and accept the following terms before this requirement proceeds.



Commercial Terms

These commercial terms govern the supply against this enquiry, including scope, quality, inspection, packing, freight, and warranty obligations as communicated by Amber Enterprises India Ltd.



Performance Bank Guarantee

Performance Bank Guarantee (PBG): The supplier shall furnish a Performance Bank Guarantee equal to 10% of the order value, valid through the warranty period, towards due performance of the contract. The PBG will be released on successful completion of supply, installation, and the warranty obligations.



Delay Liability Clause

Delay Liability Clause (DLC): A Turn-Around-Time (TAT) begins one week after the Proforma Invoice is raised. A deduction of 0.5% of the order value applies for every week of delay. Once cumulative deductions reach 5%, the deduction rate escalates to 5% of the order value per week thereafter. Deductions stop when the final payment is released.

"First, approve the contract terms — your quotation form unlocks once you accept."

The vendor reads the actual clauses, including the delay penalty in full — 0.5% of order value per week, capped at a cumulative 5%, then 5% per week thereafter — and must accept before any price field exists. Declining locks the enquiry, and sourcing can re-send.

This is the single most useful thing in the sourcing flow: Amber's commercial terms are agreed **before** the commercial conversation starts, not argued about after the price is settled.

Slide 6.5 · Quoting, line by line

 REVERSE AUCTION
CAP-2627-0001: Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton)

You are bidding as: **Tata Motors Ancillaries** (VND-001)

All prices in **INR**

Action needed — submit your quotation.

Awaiting Quote

Your Quotation
Enter your unit price and HSN code for each line item below.

#	DESCRIPTION	QTY	UOM	HSN / GST	UNIT PRICE (₹) *	LINE TOTAL
1	Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton) Centralised granule feeding system for 24 injection moulding machines (450T-1300T), covering vacuum conveying, central dryers, dosing units, closed-loop piping and PLC control with recipe management. Must integrate with the existing IMM line controls and support colour changeover without manual hopper cleaning. Commissioning and operator training included. Centralised granule feeding system for 24 injection moulding machines (450T-1300T), covering vacuum conveying, central dryers, dosing units, closed-loop piping and PLC control with recipe management. Must integrate with the existing IMM line controls and support colour changeover without manual hopper cleaning. Commissioning and operator training included.	1	EA	Select HSN...	0	—
2	Compressed Air Line Re-piping — Block C Complete re-piping of the Block C compressed-air header in stainless/aluminium modular pipe — approximately 620 running metres including drop legs, isolation valves, filters, condensate drains and flow meters at each shop boundary. Existing MS headers to be removed. Leak-down test at 7 bar and a metered leakage report are part of handover. Complete re-piping of the Block C compressed-air header in stainless/aluminium modular pipe — approximately 620 running metres including drop legs, isolation valves, filters, condensate drains and flow meters at each shop boundary. Existing MS headers to be removed. Leak-down test at 7 bar and a metered leakage report are part of handover.	1	EA	Select HSN...	0	—

Additional Charges
Freight & Handling (₹) Packing & Forwarding (₹) Service / Installation (₹)

Enter a unit price for each line to continue

Reset

Submit Quotation

Delivery Lead Time (days) *

Warranty (years)

Currency

Grand Total Summary
Subtotal (line items) —
Total Additional —
GST (as per HSN) —
Grand Total (incl. GST) —

The unlocked form mirrors the internal grid: number, description, quantity, unit of measure, HSN and GST, unit price and line total; then additional charges — freight, packing, service and installation; then delivery lead time in days, warranty in years, and currency.

The vendor picks the HSN code, not Amber. The HSN belongs to the item, so once one vendor sets it every other vendor's form shows it read-only and GST is computed identically for all of them. That is what makes the comparison honest — sourcing can see the code but cannot change it.

Slide 6.6 · GST is computed per line, from the HSN



REVERSE AUCTION
CAP-2627-0001: Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton)

You are bidding as: **Tata Motors Ancillaries** (VND-001)

All prices in INR

Your Quotation
Enter your unit price and HSN code for each line item below.

#	DESCRIPTION	QTY	UOM	HSN / GST	UNIT PRICE (₹) *	LINE TOTAL
1	Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton) Centralised granule feeding system for 24 injection moulding machines (450T-1300T), covering vacuum conveying, central dryers, dosing units, closed-loop piping and PLC control with recipe management. Must integrate with the existing IMM line controls and support colour changeover without manual hopper cleaning. Commissioning and operator training included. Centralised granule feeding system for 24 injection moulding machines (450T-1300T), covering vacuum conveying, central dryers, dosing units, closed-loop piping and PLC control with recipe management. Must integrate with the existing IMM line controls and support colour changeover without manual hopper cleaning. Commissioning and operator training included.	1	EA	8479 · 18% GST 18%	14200000	₹1,67,56,000 ₹1,42,00,000 + ₹25,56,000 GST
2	Compressed Air Line Re-piping — Block C Complete re-piping of the Block C compressed-air header in stainless/aluminium modular pipe — approximately 620 running metres including drop legs, isolation valves, filters, condensate drains and flow meters at each shop boundary. Existing MS headers to be removed. Leak-down test at 7 bar and a metered leakage report are part of handover. Complete re-piping of the Block C compressed-air header in stainless/aluminium modular pipe — approximately 620 running metres including drop legs, isolation valves, filters, condensate drains and flow meters at each shop boundary. Existing MS headers to be removed. Leak-down test at 7 bar and a metered leakage report are part of handover.	1	EA	8481 · 18% GST 18%	3950000	₹46,61,000 ₹39,50,000 + ₹7,11,000 GST

Additional Charges

Freight & Handling (₹)	Packing & Forwarding (₹)	Service / Installation (₹)
280000	65000	420000

Delivery & Validity

Grand total **₹2,21,82,000**

ResetSubmit Quotation

Currency

INR

Grand Total Summary

Subtotal (line items)	₹1,81,50,000
Total Additional	+₹7,65,000
GST (as per HSN)	+₹32,67,000
Grand Total (incl. GST)	₹2,21,82,000

Tata's quotation: line items ₹1,81,50,000 + charges ₹7,65,000 + **GST ₹32,67,000 = ₹2,21,82,000**. GST is calculated line by line from each item's own HSN code; freight, packing and service are not taxed.

After submitting, the vendor sees a read-only summary and a plain statement that it is under review.

Slide 6.7 · Two quotations side by side

CAPEX Portal
Amber Enterprises

WORKSPACE

- Dashboard
- Requests
- Vendors
- CAPEX Master
- Budget Planning
- Adhoc Budget
- Accounts

All PlantsCAPEX DetailRequest view

RFQ — Request for Quotation

Vendors quote each line first. Counter inline, set the per-line Final Decision, then accept — or escalate to a live auction.

2 need review

Invite vendors (send link)Invite new vendor

ITEM	DESCRIPTION	QTY	HSN / GST	Q1 VND-001 Tata Motors Ancillaries Needs Review Counter Copy link	Q2 VND-004 L&T Infrastructure Needs Review Counter Copy link	FINAL DECISION
Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton) General	Centralised granule feeding system for 24 injection moulding machines (450T-1300T), covering vacuum conveying, central dryers, dosing units, closed-loop piping and PLC control with recipe management. Must integrate with the existing IMM line controls and support colour changeover without manual hopper cleaning. Commissioning and operator training included.	1	8479 GST 18%	₹1,42,00,000 Subtotal: ₹1,42,00,000 + ₹25,56,000 GST Total: ₹1,67,56,000 ↓ Lowest	₹1,48,00,000 Subtotal: ₹1,48,00,000 + ₹26,64,000 GST Total: ₹1,74,64,000	PRICE (₹) 0 DISC % 0 Select vendor... Price x Qty: ₹0
Compressed Air Line Re-piping — Block C General	Complete re-piping of the Block C compressed-air header in stainless/aluminium modular pipe — approximately 620 running metres including drop legs, isolation valves, filters, condensate drains and flow meters at each shop boundary. Existing MS headers to be removed. Leak-down test at 7 bar and a metered leakage report are part of handover.	1	8481 GST 18%	₹39,50,000 Subtotal: ₹39,50,000 + ₹7,11,000 GST Total: ₹46,61,000	₹36,50,000 Subtotal: ₹36,50,000 + ₹6,57,000 GST Total: ₹43,07,000 ↓ Lowest	PRICE (₹) 0 DISC % 0 Select vendor... Price x Qty: ₹0
Transportation / Freight				₹2,80,000	₹1,90,000	
Packing / Forwarding				₹65,000	₹40,000	
Service / Installation				₹4,20,000	₹6,10,000	
Delivery Lead Time (Weeks)				—	—	
Warranty (Years)				2	2	
Currency				INR	INR	
Grand Total (incl. GST)				₹2,21,82,000 L1 incl. ₹32,67,000 GST	₹2,26,11,000 incl. ₹33,21,000 GST	
ACTIONS				Accept Decline	Accept Decline	

The Final Decision column (Price / Disc / Vendor) records the negotiated award per line — the same as the reverse auction. Acceptfinalizes a vendor for the single-vendor Proforma Invoice & fulfillment.

TECHNICAL SPEC APPROVAL — REQUIRED BEFORE AWARD

Tata Motors Ancillaries SPEC-Z4228B
Attach the spec documents and send them to the Technical team.
Spec Not Sent Prepare

L&T Infrastructure SPEC-ZY0VB8
Attach the spec documents and send them to the Technical team.
Spec Not Sent Prepare

Pick a vendor and final price for each line in the Final Decisioncolumn to approve & request Pls.

Escalate to a live reverse auction. The current best price (₹2,21,82,000) drops 5% to become the new price to beat, and every vendor's rank resets — vendors must submit a fresh bid to reveal their rank.
Start Reverse Auction

NEGOTIATION HISTORY (2)

STATUS HISTORY

In Sourcing Plant Head (email) 22 Aug 2026, 06:48

With Plant Head Arjun Mehta 22 Aug 2026, 06:40

Neha Kapoor
Sourcing Member

Log out

Now the grid earns its keep. Per line, the cheaper vendor is highlighted green with a ↓ **Lowest** chip — and it is **not the same vendor on both lines**:

Line	Tata Motors Ancillaries	L&T Infrastructure	Cheaper
Centralised Material Feeding	₹1,42,00,000 (₹1,67,56,000 incl. GST)	₹1,48,00,000	Tata
Compressed Air Re-piping	₹39,50,000	₹36,50,000 (₹43,07,000 incl. GST)	L&T
Whole quotation	₹2,21,82,000 L1	₹2,26,11,000	

Footer rows compare freight, packing, service, delivery lead time, warranty and currency. The L1 badge marks the cheapest whole quotation.

Notice what this makes possible: the buyer's preferred vendors were Tata for one line and L&T for the other, and the market agrees — but with two vendors quoting both lines, Amber can see it rather than assume it.

Slide 6.8 · Countering, inline

CAPEX Portal

Amber Enterprises

WORKSPACE

Dashboard

Requests

Vendors

CAPEX Master

Budget Planning

Adhoc Budget

Accounts

All Plants

CAPEX Detail

Request View

NK

Neha Kapoor

Machinery

RFQ — Request for Quotation

Vendors quote each line first. Counter inline, set the per-line Final Decision, then accept — or escalate to a live auction.

2 need review

Invite vendors (send link)

Invite new vendor

ITEM	DESCRIPTION	QTY	HSN / GST	Q1 VND-001 Tata Motors Ancillaries Needs Review Copy link	Q2 VND-004 L&T Infrastructure Needs Review Counter Copy link	FINAL DECISION
Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton) General	Centralised granule feeding system for 24 injection moulding machines (450T–1300T), covering vacuum conveying, central dryers, dosing units, closed-loop piping and PLC control with recipe management. Must integrate with the existing IMM line controls and support colour changeover without manual hopper cleaning. Commissioning and operator training included.	1	8479 GST 18%	14200000	₹1,48,00,000 Subtotal: ₹1,48,00,000 + ₹26,64,000 GST Total: ₹1,74,64,000	PRICE (₹) 0 DISC % 0 Select vendor... Price x Qty: ₹0
Compressed Air Line Re-piping — Block C General	Complete re-piping of the Block C compressed-air header in stainless/aluminium modular pipe — approximately 620 running metres including drop legs, isolation valves, filters, condensate drains and flow meters at each shop boundary. Existing MS headers to be removed. Leak-down test at 7 bar and a metered leakage report are part of handover.	1	8481 GST 18%	3950000	₹36,50,000 Subtotal: ₹36,50,000 + ₹6,57,000 GST Total: ₹43,07,000 Lowest	PRICE (₹) 0 DISC % 0 Select vendor... Price x Qty: ₹0
Transportation / Freight				280000	₹1,90,000	
Packing / Forwarding				65000	₹40,000	
Service / Installation				420000	₹6,10,000	
Delivery Lead Time (Weeks)				0	—	
Warranty (Years)				2	2	
Currency				INR	INR	
Grand Total (incl. GST)				₹2,21,82,000 incl. ₹32,67,000 GST	₹2,26,11,000 incl. ₹33,21,000 GST	
ACTIONS				Send to vendor Cancel	Accept Decline	

The Final Decision column (Price / Disc / Vendor) records the negotiated award per line — the same as the reverse auction. Accept finalizes a vendor for the single-vendor Proforma Invoice & fulfillment.

TECHNICAL SPEC APPROVAL — REQUIRED BEFORE AWARD

Tata Motors Ancillaries

SPEC-Z42288

Attach the spec documents and send them to the Technical team.

Spec Not Sent

Prepare

L&T Infrastructure

SPEC-ZY0VB8

Attach the spec documents and send them to the Technical team.

Spec Not Sent

Prepare

Pick a vendor and final price for each line in the Final Decision column to approve & request PIs.

Escalate to a live reverse auction. The current best price (₹2,21,82,000) drops 5% to become the new price to beat, and every vendor's rank resets — vendors must submit a fresh bid to reveal their rank.

Start Reverse Auction

NEGOTIATION HISTORY (2)

Counter turns one vendor's column into editable fields — per-line unit prices and the footer charges. Here Tata's unit price is pushed from ₹1,42,00,000 to ₹1,36,50,000 and the freight from ₹2,80,000 to ₹2,20,000.

amber

CAPEX Portal
Amber Enterprises

WORKSPACE

Dashboard

Requests

Vendors

CAPEX Master

Budget Planning

Adhoc Budget

Accounts

All Plants

CAPEX Detail

Request view

RFQ — Request for Quotation

Vendors quote each line first. Counter inline, set the per-line Final Decision, then accept — or escalate to a live auction.

1 need review

1 counter sent

Invite vendors (send link)

Invite new vendor

ITEM	DESCRIPTION	QTY	HSN / GST	Q1 VND-001 Tata Motors Ancillaries Counter Sent Counter Copy link	Q2 VND-004 L&T Infrastructure Needs Review Counter Copy link	FINAL DECISION
Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton) General	Centralised granule feeding system for 24 injection moulding machines (450T-1300T), covering vacuum conveying, central dryers, dosing units, closed-loop piping and PLC control with recipe management. Must integrate with the existing IMM line controls and support colour changeover without manual hopper cleaning. Commissioning and operator training included.	1	8479 GST 18%	₹1,36,50,000 Subtotal: ₹1,36,50,000 + ₹24,57,000 GST Total: ₹1,61,07,000 Lowest	₹1,48,00,000 Subtotal: ₹1,48,00,000 + ₹26,64,000 GST Total: ₹1,74,64,000	PRICE (₹) 0 DISC % 0 Select vendor... Price x Qty: ₹0
Compressed Air Line Re-piping — Block C General	Complete re-piping of the Block C compressed-air header in stainless/aluminium modular pipe — approximately 620 running metres including drop legs, isolation valves, filters, condensate drains and flow meters at each shop boundary. Existing MS headers to be removed. Leak-down test at 7 bar and a metered leakage report are part of handover.	1	8481 GST 18%	₹39,50,000 Subtotal: ₹39,50,000 + ₹7,11,000 GST Total: ₹46,61,000	₹36,50,000 Subtotal: ₹36,50,000 + ₹6,57,000 GST Total: ₹43,07,000 Lowest	PRICE (₹) 0 DISC % 0 Select vendor... Price x Qty: ₹0
Transportation / Freight				₹2,20,000	₹1,90,000	
Packing / Forwarding				₹65,000	₹40,000	
Service / Installation				₹4,20,000	₹6,10,000	
Delivery Lead Time (Weeks)				—	—	
Warranty (Years)				2	2	
Currency				INR	INR	
Grand Total (incl. GST)				₹2,14,73,000 incl. ₹31,68,000 GST	₹2,26,11,000 incl. ₹33,21,000 GST	
ACTIONS				Counter sent — awaiting vendor	Accept Decline	

The Final Decision column (Price / Disc / Vendor) records the negotiated award per line — the same as the reverse auction. Acceptfinalizes a vendor for the single-vendor Proforma Invoice & fulfillment.

TECHNICAL SPEC APPROVAL — REQUIRED BEFORE AWARD

Tata Motors Ancillaries SPEC-Z4228B

Attach the spec documents and send them to the Technical team.

Spec Not Sent Prepare

L&T Infrastructure SPEC-ZY0VB8

Attach the spec documents and send them to the Technical team.

Spec Not Sent Prepare

Pick a vendor and final price for each line in the Final Decisioncolumn to approve & request Pls.

Escalate to a live reverse auction. The current best price (₹2,14,73,000) drops 5% to become the new price to beat, and every vendor's rank resets — vendors must submit a fresh bid to reveal their rank.

Start Reverse Auction

NEGOTIATION HISTORY (3)

STATUS HISTORY

In Sourcing

Plant Head (email) 22 Aug 2026, 06:48

NK

Neha Kapoor

Sourcing Member

Log out

The column reads "Counter sent — awaiting vendor", the total drops to ₹2,14,73,000, and the negotiation history logs every move by both sides.

Slide 6.9 · The vendor answers

 REVERSE AUCTION

CAP-2627-0001: Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton)

You are bidding as: **Tata Motors Ancillaries** (VND-001)

All prices in **INR**

Action needed — review Amber's counter-quotation.

Counter Sent

Amber's Counter-Quotation

#	DESCRIPTION	QTY	UOM	HSN / GST	UNIT PRICE (₹)	LINE TOTAL
1	Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton) Centralised granule feeding system for 24 injection moulding machines (450T-1300T), covering vacuum conveying, central dryers, dosing units, closed-loop piping and PLC control with recipe management. Must integrate with the existing IMM line controls and support colour changeover without manual hopper cleaning. Commissioning and operator training included.	1	EA	8479 · 18% GST ₹24,57,000	₹1,36,50,000	₹1,61,07,000 ₹1,36,50,000 + ₹24,57,000 GST
2	Compressed Air Line Re-piping — Block C Complete re-piping of the Block C compressed-air header in stainless/aluminium modular pipe — approximately 620 running metres including drop legs, isolation valves, filters, condensate drains and flow meters at each shop boundary. Existing MS headers to be removed. Look down text	1	EA	8481 · 18% GST ₹7,11,000	₹39,50,000	₹46,61,000 ₹39,50,000 + ₹7,11,000 GST

The vendor sees Amber's revised numbers laid out exactly as they will stand if accepted, and can **approve**, **counter back**, or **decline**. Either side accepting closes the price.

Tata accepts. The quotation is settled at ₹2,14,73,000 — **₹7,09,000 below their opening number**, which is the kind of figure that shows up later as negotiation savings on the sourcing dashboard.

Part 7 — The technical specification gate

The most consequential rule in the product: **a vendor cannot be awarded until Amber's technical team has signed off that vendor's machine specification.**

Slide 7.1 · Why it is per vendor, not per request

Different vendors offer different machines, and a split award hands different lines to different suppliers. So the gate is per vendor. Both vendors start at **Spec Not Sent** — and *not sent* blocks an award exactly as firmly as *rejected* does. The step cannot be skipped by ignoring it.

Slide 7.2 · Sourcing prepares the package

**CAPEX Portal**
Amber Enterprises

WORKSPACE

Dashboard

Requests

Vendors

CAPEX Master

Budget Planning

Adhoc Budget

Accounts

All Plants

CAPEX Detail

Request view

General

filters, condensate drains and flow meters at each shop boundary. Existing MS headers to be removed. Leak-down test at 7 bar and a metered leakage report are part of handover.

Transportation / Freight

Packing / Forwarding

Service / Installation

Delivery Lead Time (Weeks)

Warranty (Years)

Currency

Grand Total (incl. GST)

+ ₹7,11,000 GST

Total: ₹46,61,000

₹2,20,000

₹65,000

₹4,20,000

—

2

INR

₹1,90,000

₹40,000

₹6,10,000

—

2

INR

₹2,14,73,000 incl. ₹31,68,000 GST

₹2,26,11,000 incl. ₹33,21,000 GST

Documents Approved

Quotation & docs approved — approve & request PI in the Final Decision area below.

Reopen negotiation

Accept

Decline

Price x Qty: ₹0

The Final Decision column (Price / Disc / Vendor) records the negotiated award per line — the same as the reverse auction. **Accept** finalizes a vendor for the single-vendor Proforma Invoice & fulfillment.

TECHNICAL SPEC APPROVAL — REQUIRED BEFORE AWARD

Tata Motors Ancillaries SPEC-Z42288

Attach the spec documents and send them to the Technical team.

Spec Not Sent Close

The Technical team sees this package as SPEC-Z42288 — the vendor name and the document filenames are hidden from them. Keep the vendor's name out of your notes below.

Specification documents (1/6)

TechnicalSpecSheet_CentralFeedingSystem.pdf

Upload vendor spec document (PDF / image / doc, max 2 MB)

Notes for the Technical team

Model CMF-24-1300 central feeding system. Please verify: (1) 1,200 kg/h aggregate conveying is adequate for 24 machines at peak shot weight, (2) dryer dew point of -40 °C holds for PA66-GF30, (3) gravimetric dosing at ±0.3% meets the masterbatch tolerance on white RAC panels, (4) OPC-UA integration with the existing line MES is confirmed in writing. Deviation from enquiry: offered PLC is Siemens S7-1200 where the enquiry asked for S7-1500.

Send to Technical team

L&T Infrastructure SPEC-ZY0VB8

Attach the spec documents and send them to the Technical team.

Spec Not Sent Prepare

Pick a vendor and final price for each line in the Final Decision column to approve & request PIs.


Per vendor, sourcing uploads the spec sheet **the vendor supplied**, and writes notes telling the technical team what to check. Here:

"Model CMF-24-1300 central feeding system. Please verify: (1) 1,200 kg/h aggregate conveying is adequate for 24 machines at peak shot weight, (2) dryer dew point of -40°C holds for PA66-GF30, (3) gravimetric dosing at $\pm 0.3\%$ meets the masterbatch tolerance on white RAC panels, (4) OPC-UA integration with the existing line MES is confirmed in writing. **Deviation from enquiry: offered PLC is Siemens S7-1200 where the enquiry asked for S7-1500.**"

The vendor's identity is withheld from the technical team. The banner across the top of the panel says so: "The Technical team sees this package as SPEC-Z4228B — the vendor name and the document filenames are hidden from them. Keep the vendor's name out of your notes below."

That is a real anti-bias control. Engineering assesses the machine on technical merit, not on which supplier it came from — and because vendors habitually name their datasheets after themselves, the filenames are replaced too.

Slide 7.3 · Sent to the technical team

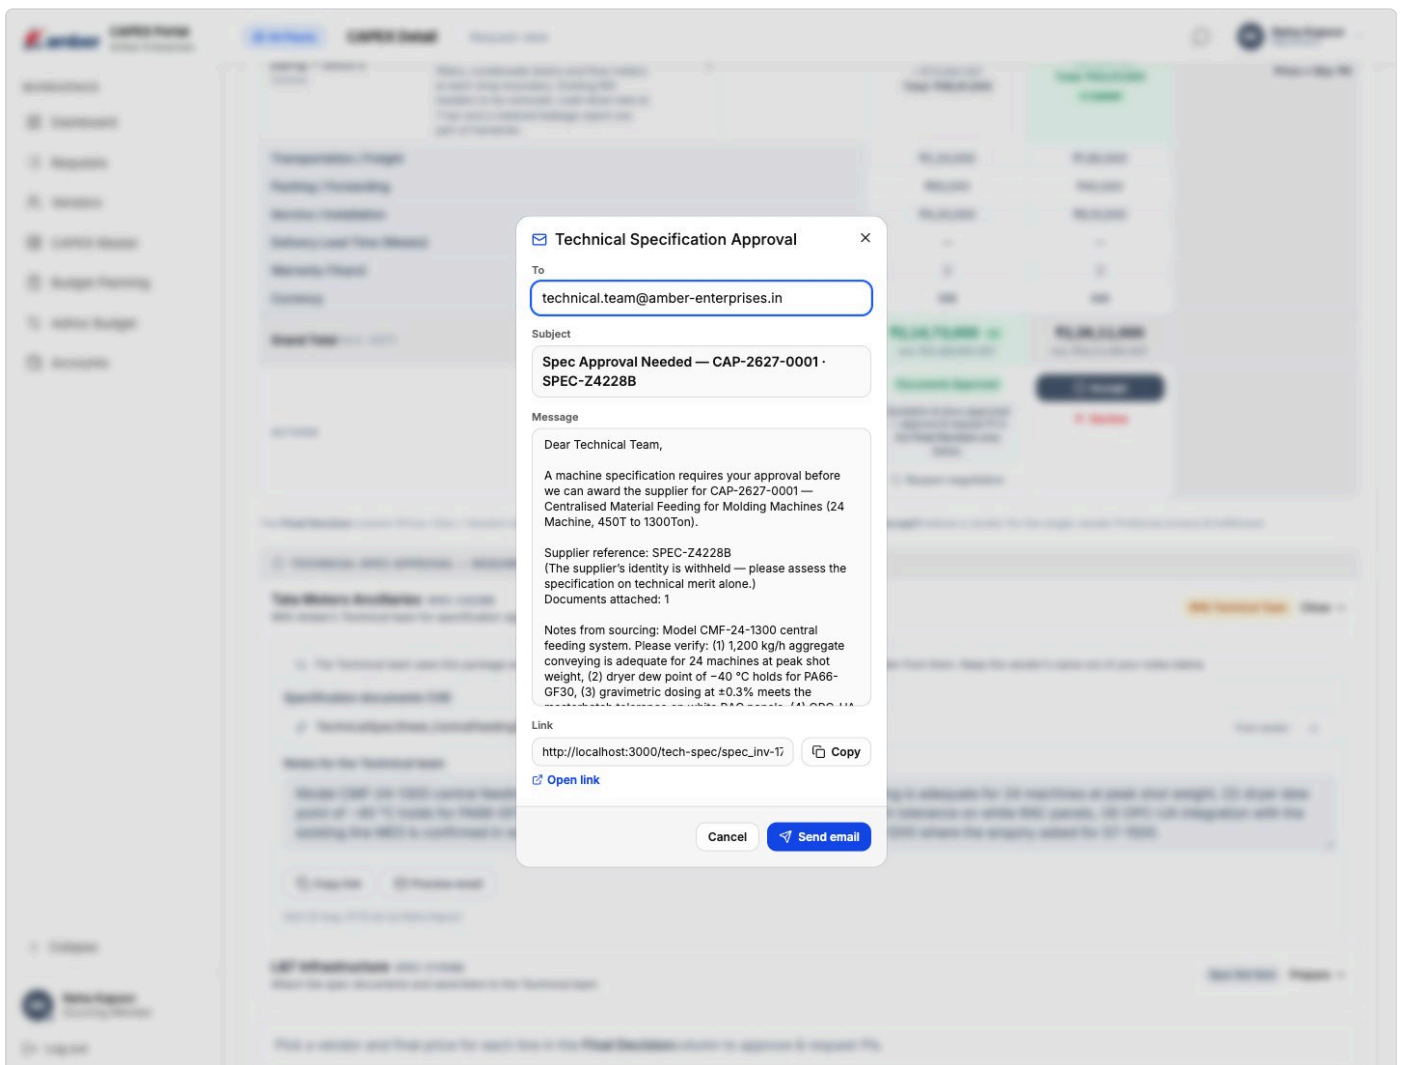

The email carries the anonymous reference, the document count, sourcing's notes verbatim, and the link. Its subject line is "Spec Approval Needed — CAP-2627-0001 · SPEC-Z4228B" and the body states the withholding explicitly.

Slide 7.4 · The technical team's page

Amber CAPEX · Technical Specification Approval

MACHINE SPECIFICATION APPROVAL

Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton)

CAP-2627-0001 · jhajjar_p1 · Brown Field

SUPPLIER REFERENCE

SPEC-Z4228B

The supplier's identity is withheld so the specification is assessed on technical merit alone. Quote this reference to the sourcing team if you need to discuss the package.

REQUESTED SPECIFICATION (2 ITEMS)

Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton)Qty 1

Centralised granule feeding system for 24 injection moulding machines (450T–1300T), covering vacuum conveying, central dryers, dosing units, closed-loop piping and PLC control with recipe management. Must integrate with the existing IMM line controls and support colour changeover without manual hopper cleaning. Commissioning and operator training included.

Compressed Air Line Re-piping — Block CQty 1

Complete re-piping of the Block C compressed-air header in stainless/aluminium modular pipe — approximately 620 running metres including drop legs, isolation valves, filters, condensate drains and flow meters at each shop boundary. Existing MS headers to be removed. Leak-down test at 7 bar and a metered leakage report are part of handover.

NOTES FROM SOURCING

Model CMF-24-1300 central feeding system. Please verify: (1) 1,200 kg/h aggregate conveying is adequate for 24 machines at peak shot weight, (2) dryer dew point of –40 °C holds for PA66-GF30, (3) gravimetric dosing at ±0.3% meets the masterbatch tolerance on white RAC panels, (4) OPC-UA integration with the existing line MES is confirmed in writing. Deviation from enquiry: offered PLC is Siemens S7-1200 where the enquiry asked for S7-1500.

SPECIFICATION DOCUMENTS (1)

Specification Document 1 · PDF

Approve Specification

Send Back for Revision

Reject

No login. They see the request, the **supplier reference SPEC-Z4228B** in place of a name, the specification Amber asked for, sourcing's notes, and the documents to download — renamed *"Specification Document 1 · PDF"*.

Then they decide:

- **Approve Specification** — this vendor becomes awardable.
- **Send Back for Revision** — returns to sourcing with a remark, which is required. Sourcing revises and re-sends on a fresh link, and the loop repeats until it is right.
- **Reject** — also requires a remark.

The link is consumed on decision, so a forwarded copy cannot re-decide. Both vendors on this request were sent, reviewed and approved separately.

Part 8 — The award

Slide 8.1 · Filling the Final Decision, line by line

amber

CAPEX Portal

Amber Enterprises

All Plants

CAPEX Detail

Request view

NK

Neha Kapoor

Machinery

WORKSPACE

Dashboard

Requests

Vendors

CAPEX Master

Budget Planning

Adhoc Budget

Accounts

RFQ — Request for Quotation

Vendors quote each line first. Counter inline, set the per-line Final Decision, then accept — or escalate to a live auction.

1 need review

1 approved

Invite vendors (send link)

Invite new vendor

ITEM	DESCRIPTION	QTY	HSN / GST	Q1 VND-001 Tata Motors Ancillaries Quotation Approved Copy link	Q2 VND-004 L&T Infrastructure Needs Review Counter Copy link	FINAL DECISION
Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton) General	Centralised granule feeding system for 24 injection moulding machines (450T–1300T), covering vacuum conveying, central dryers, dosing units, closed-loop piping and PLC control with recipe management. Must integrate with the existing IMM line controls and support colour changeover without manual hopper cleaning. Commissioning and operator training included.	1	8479 GST 18%	₹1,36,50,000 Subtotal: ₹1,36,50,000 + ₹24,57,000 GST Total: ₹1,61,07,000 Lowest	₹1,48,00,000 Subtotal: ₹1,48,00,000 + ₹26,64,000 GST Total: ₹1,74,64,000	PRICE (₹) 13650000 DISC % 0 Tata Motors Ancillaries — ₹ Price × Qty: ₹1,36,50,000
Compressed Air Line Re-piping — Block C General	Complete re-piping of the Block C compressed-air header in stainless/aluminium modular pipe — approximately 620 running metres including drop legs, isolation valves, filters, condensate drains and flow meters at each shop boundary. Existing MS headers to be removed. Leak-down test at 7 bar and a metered leakage report are part of handover.	1	8481 GST 18%	₹39,50,000 Subtotal: ₹39,50,000 + ₹7,11,000 GST Total: ₹46,61,000	₹36,50,000 Subtotal: ₹36,50,000 + ₹6,57,000 GST Total: ₹43,07,000 Lowest	PRICE (₹) 3650000 DISC % 0 L&T Infrastructure — ₹36,50 Price × Qty: ₹36,50,000
Transportation / Freight				₹2,20,000	₹1,90,000	
Packing / Forwarding				₹65,000	₹40,000	
Service / Installation				₹4,20,000	₹6,10,000	
Delivery Lead Time (Weeks)				—	—	
Warranty (Years)				2	2	
Currency				INR	INR	
Grand Total (incl. GST)				₹2,14,73,000 incl. ₹31,68,000 GST	₹2,26,11,000 incl. ₹33,21,000 GST	
ACTIONS				Documents Approved Quotation & docs approved — approve & request PI in the Final Decision area below. Reopen negotiation	Accept Decline	

The Final Decision column (Price / Disc / Vendor) records the negotiated award per line — the same as the reverse auction. Acceptfinalizes a vendor for the single-vendor Proforma Invoice & fulfillment.

TECHNICAL SPEC APPROVAL — REQUIRED BEFORE AWARD

Tata Motors Ancillaries SPEC-Z4228B
Specification approved — this vendor can be awarded. Spec Approved Open

L&T Infrastructure SPEC-ZY0VB8
Specification approved — this vendor can be awarded. Spec Approved Open

Final Decision — Approve & Request PI
2 vendors selected — approve all at once, or each separately. Approve & Request PI — All (2)

Item trial is ON — the awarded vendor(s) will upload a trial and the final payment is blocked until you approve it.

Tata Motors Ancillaries
1 line · ₹1,61,07,000 incl. GST Approve & Request PI

L&T Infrastructure
1 line · ₹43,07,000 incl. GST Approve & Request PI

Collapse

NK

Neha Kapoor

Sourcing Member

Log out

Per line, sourcing picks the winning vendor and the final price. Choosing a vendor **auto-fills that line's price** from what they actually quoted, and there is a discount field and a computed price × quantity beside it. The decision saves as it is typed.

Both technical specifications now read **Spec Approved — this vendor can be awarded**. Until they did, the award bar underneath refused to act and said why.

The split is the one the market indicated:

- Line 1, Centralised Material Feeding → **Tata Motors Ancillaries** at ₹1,36,50,000 (the countered price)
- Line 2, Compressed Air Re-piping → **L&T Infrastructure** at ₹36,50,000

Slide 8.2 · Approve and request the invoices

The award bar offers **Approve & Request PI — All (2)** to award both vendors at once, or a button per vendor to award them separately — Tata now, L&T next week. It also reminds sourcing that *"Item trial is ON — the awarded vendor(s) will upload a trial and the final payment is blocked until you approve it."*

The result is **two independent awards**:

Vendor	Line awarded	Order value (incl. GST)
Tata Motors Ancillaries	Centralised Material Feeding × 1	₹1,61,07,000
L&T Infrastructure	Compressed Air Re-piping × 1	₹43,07,000

Slide 8.3 · One request, two fulfilment tracks

CAPEX Portal
Amber Enterprises

WORKSPACE

Dashboard

Requests

Vendors

CAPEX Master

Budget Planning

Adhoc Budget

Accounts

All Plants

CAPEX Detail

Request view

PI Requested

Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton)

0 / 2 awards complete

Multiple Qty: 2 Items ₹1,91,00,000 Neha Kapoor CAP-2627-0001 Brown Field 71340ab1...

REQUEST DETAILS

FIELD TYPE

Brown Field

PLANT

Jhajjar Plant 1, Haryana

SUBMITTED

22 Aug 2026

ITEMS

2

#	DESCRIPTION	CATEGORY	QTY	ALLOCATED	EST. COST	STATUS	VENDOR	DOC
1	Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton) Other Brown Field - General Centralised granule feeding system for 24 injection moulding machines (450T–1300T), covering vacuum conveying, central dryers, dosing units, closed-loop piping and PLC control with recipe management. Must integrate with the existing IMM line controls and support colour changeover without manual hopper cleaning. Commissioning and operator training included.	General	1	₹1,50,00,000	₹1,50,00,000	On budget	Tata Motors Ancillaries	—
2	Compressed Air Line Re-piping — Block C Other Brown Field - General Complete re-piping of the Block C compressed-air header in stainless/aluminium modular pipe — approximately 620 running metres including drop legs, isolation valves, filters, condensate drains and flow meters at each shop boundary. Existing MS headers to be removed. Leak-down test at 7 bar and a metered leakage report are part of handover.	General	1	₹41,00,000	₹41,00,000	On budget	L&T Infrastructure	—
BUDGET SUMMARY				Allocated: ₹1,91,00,000	Est. Cost: ₹1,91,00,000	On budget		

PREFERRED VENDOR

Tata Motors Ancillaries
Supplied and commissioned the same central feeding system at DDN-5 in 2024; their controls already speak to our IMM line PLCs.

QUOTATION

VENDOR QUOTATIONS (2) · compared GST-inclusive, on an INR basis

Tata Motors Ancillaries

Lowest

RFQ quotation

Freight ₹2,20,000 Packing ₹65,000 Service ₹4,20,000 Warranty 2 yr

₹2,14,73,000
incl. GST

Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton)
Compressed Air Line Re-piping — Block C

₹1,36,50,000 × 1 = ₹1,36,50,000
₹39,50,000 × 1 = ₹39,50,000

L&T Infrastructure

RFQ quotation

Freight ₹1,90,000 Packing ₹40,000 Service ₹6,10,000 Warranty 2 yr

₹2,26,11,000
incl. GST

Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton)
Compressed Air Line Re-piping — Block C

₹1,48,00,000 × 1 = ₹1,48,00,000
₹36,50,000 × 1 = ₹36,50,000

The request header now reads **PI Requested · 0 / 2 awards complete**. Each award runs its **own complete track** from here — its own proforma invoice, its own FA codes, its own purchase order, its own payment milestones, its own trial, its own delay clock. The request is only *Completed* when every award is.

Also visible on this screen: the **quotation record**. Every quotation captured against the request stays on the page, compared GST-inclusive on a common rupee basis, with the cheapest flagged. An approver looking at this request in six months can see what the alternatives were.



CAPEX Portal
Amber Enterprises

WORKSPACE

- Dashboard
- Requests
- Vendors
- CAPEX Master
- Budget Planning
- Adhoc Budget
- Accounts

NK Neha Kapoor
Sourcing Member

Log out

All Plants

CAPEX Detail

Request view

QUOTATION

VENDOR QUOTATIONS (2) - compared GST-inclusive, on an INR basis

Tata Motors Ancillaries

Lowest

RFQ quotation

Freight ₹2,20,000 Packing ₹65,000 Service ₹4,20,000 Warranty 2 yr

Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton)
Compressed Air Line Re-piping — Block C

₹2,14,73,000
Incl. GST

L&T Infrastructure

RFQ quotation

Freight ₹1,90,000 Packing ₹40,000 Service ₹6,10,000 Warranty 2 yr

Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton)
Compressed Air Line Re-piping — Block C

₹2,26,11,000
Incl. GST

RFQ — Request for Quotation

Vendors quote each line first. Counter inline, set the per-line Final Decision, then accept — or escalate to a live auction.

1 need review

1 approved

Invite vendors (send link)

Invite new vendor

ITEM	DESCRIPTION	QTY	HSN / GST	Q1 VND-001 Tata Motors Ancillaries Quotation Approved Copy link	Q2 VND-004 L&T Infrastructure Needs Review Counter Copy link	FINAL DECISION
	Centralised granule feeding system for 24	8479				PRICE (₹)DISC %

Because both vendors accepted the Commercial Terms, the Performance Bank Guarantee and the Delay Liability Clause before they were allowed to quote, there is **no post-award terms round**. Sourcing goes straight to asking for the invoice.

Part 9 — Fulfilment: from award to the last rupee

Followed here for the **Tata award (₹1,61,07,000)**. The L&T award ran the identical track in parallel with its own documents, links, purchase order and payments.

Sourcing awards and requests the PI



Vendor uploads the Proforma Invoice



Email to Plant Accounts



Plant Accounts assign the FA codes



Email to Global Accounts (Satish)



Satish uploads and issues the PO



Vendor downloads the PO



Plant Accounts release the advance



Vendor uploads the item trial



Sourcing approves the trial



Final milestone released — order complete

Slide 9.1 · The vendor raises the proforma invoice

 REVERSE AUCTION
CAP-2627-0001: Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton)

You are bidding as: **Tata Motors Ancillaries** (VND-001) All prices in **INR**

Action needed — upload your Proforma Invoice.

Quotation Approved

Upload Proforma Invoice

Your quotation of ₹1,61,07,000 (grand total) was approved. Upload your Proforma Invoice to proceed.

PI Amount (₹)

Proforma Invoice File *

Attach PDF / image (max 500 KB)

Note (optional)

Submit Proforma Invoice

"Your quotation of ₹1,61,07,000 was approved. Upload your Proforma Invoice to proceed." — the amount is pre-filled from the agreed price, so the invoice and the award cannot silently drift apart.

 REVERSE AUCTION
CAP-2627-0001: Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton)

You are bidding as: **Tata Motors Ancillaries** (VND-001) All prices in **INR**

No action needed — waiting on Amber.

Quotation Approved

Proforma Invoice Submitted

Thank you. Your PI has been sent to Amber's buyer and accounts team for PO processing and payment.

TAT Clock — Grace Period

Delay liability begins in 7 days (PI + 1 week). No deduction yet.

On submit, the **delay clock starts**: "Delay liability begins in 7 days (PI + 1 week). No deduction yet." From this moment the penalty clause the vendor accepted in Part 6 becomes live arithmetic — 0.5% per week, cumulative cap 5%, then 5% per week — and it stops when the final payment is released.

Slide 9.2 · Internally, the request fans out per award


The screenshot displays the CAPEX Portal interface for a user named Neha Kapoor. The sidebar on the left lists navigation options: Dashboard, Requests, Vendors, CAPEX Master, Budget Planning, Adhoc Budget, and Accounts. The main content area is titled 'CAPEX Detail' and 'Request view'. It shows a 'NEGOTIATION HISTORY (4)' section with two 'TAT Clock — Grace Period' entries, each indicating a delay liability beginning in 7 days. Below these are two 'Item Trial' entries, both marked as 'Awaiting Trial Upload'. The main section displays two awards: 'Award — Tata Motors Ancillaries' and 'Award — L&T Infrastructure'. Each award entry includes the awarded vendor, order value, a downloadable Proforma Invoice, and a section for 'Awaiting Plant Accounts to assign FA codes on the emailed link'. The Tata Motors award has an order value of ₹1,61,07,000 and a link to a Proforma Invoice. The L&T Infrastructure award has an order value of ₹43,07,000 and a link to a Technical Spec Sheet. Both awards include a table for FA codes and a note stating 'The PO can be issued once FA codes are submitted.' The status history at the bottom shows recent actions: 'PI Requested' by Neha Kapoor on 22 Aug 2026, 07:25, and 'In Sourcing' by Plant Head (email) on 22 Aug 2026, 06:48.

Award — Tata Motors Ancillaries: order value, the downloadable invoice, an item-trial card, the FA-code table, a live delay clock, and the handoff banner — *"Awaiting Plant Accounts to assign FA codes on the emailed link. Plant Accounts act on the secure emailed link — no portal login."*

The same block appears again for L&T, with its own everything.

This whole panel is read-only for everyone with a portal seat. Nobody inside the portal can type an FA code or tick a payment. They can see the state and re-send the link. That separation is the point of the design, not a limitation of it.

Slide 9.3 · Email 1 — to Plant Accounts

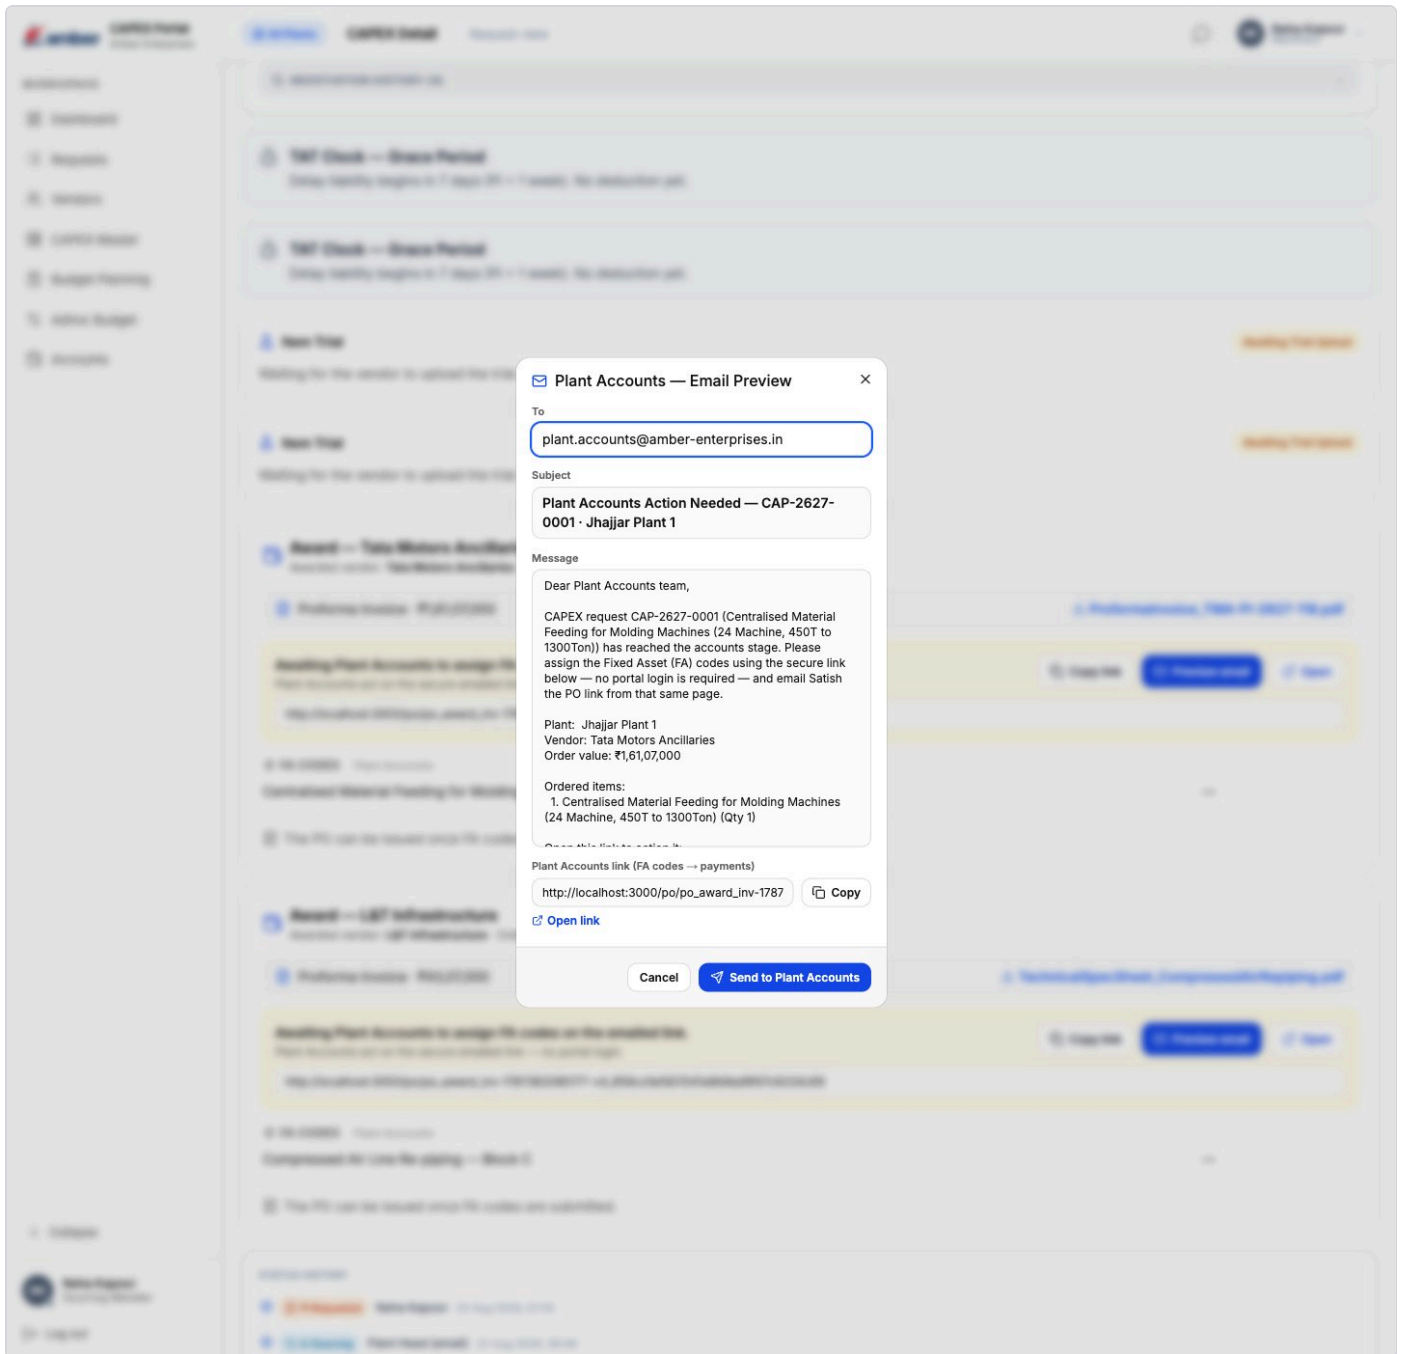

Plant, vendor, order value, the ordered items and the link. The body spells out both of their jobs: assign the fixed-asset codes, and then email Global Accounts the purchase-order link from that same page.

Slide 9.4 · Plant Accounts, step 1 — the FA codes

The screenshot shows a web application interface for 'Amber CAPEX · Plant Accounts'. The main heading is 'PLANT ACCOUNTS — FA CODES, PO & PAYMENTS'. Below this, the title is 'Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton)' with ID 'CAP-2627-0001'. A progress bar at the top indicates four steps: '1. FA codes' (active), '2. PO (Satish)', '3. Payments', and '4. Done'. The form displays 'Field: Brown Field' and 'Plant: Jhajjar Plant 1'. The vendor is 'Tata Motors Ancillaries' and the order value is '₹1,61,07,000'. There are links for 'Proforma Invoice · ₹1,61,07,000' and a PDF download 'ProformaInvoice_TMA-PI-2627-118.pdf'. A table titled '# ORDERED ITEMS & FA CODES' contains one item: '1. Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton) · Qty 1' with an adjacent 'FA code' input field. A large blue button at the bottom says 'Submit FA codes & continue to PO'. Below the button, a note states 'Assign an FA code to every item to continue.'

Their page carries a four-step rail — **1. FA codes** → **2. PO (Satish)** → **3. Payments** → **4. Done** — so they always know where the order stands. They see the vendor, the order value, the invoice to download, and an FA-code field per ordered item.

Submit is blocked until every item has a code.

Slide 9.5 · Email 2 — composed for them, automatically

The screenshot shows an email composition window titled 'PO Request → Satish (Global Accounts)'. The 'To' field is 'satish.accounts@amber-enterprises.in'. The 'Subject' is 'PO Required — CAP-2627-0001 · Jhajjar Plant 1'. The 'Message' body contains the following text: 'Dear Satish, Fixed Asset (FA) codes have been assigned for CAPEX request CAP-2627-0001 (Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton)). Please raise the Purchase Order for the finalized vendor using the secure link below — no portal login is required. Plant: Jhajjar Plant 1 Vendor: Tata Motors Ancillaries Order value: ₹1,61,07,000 Ordered items & FA codes: 1. Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton) (Qty 1) — FA Code: FA-JP1-2627-0114'. Below the message, there is a 'Link for Satish to issue the PO' field containing 'http://localhost:3000/po-issue/poissue_awa' and a 'Copy' button. At the bottom, there are 'Cancel' and 'Send to Satish' buttons.

Submitting the FA codes mints the Global Accounts link **and immediately opens the email**, pre-filled with the items and the codes just assigned. Plant Accounts do not have to remember what happens next — it opens in front of them.

The rail advances to **2. PO (Satish)** and the panel keeps copy-link, re-send and open, so the handoff can be repeated without regenerating anything.

Slide 9.6 · Global Accounts issues the purchase order

Amber CAPEX · Global Accounts — Issue PO

ISSUE PURCHASE ORDER

Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton)

CAP-2627-0001

Field: Brown FieldPlant: Jhajjar Plant 1

Vendor: Tata Motors Ancillaries

Order value: ₹1,61,07,000

Proforma Invoice · ₹1,61,07,000

ProformaInvoice_TMA-PI-2627-118.pdf

ORDERED ITEMS & FA CODES

1. Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton) · Qty 1

FA-JP1-2627-0114

PO Number

Amount (₹)

PO-CAP-2627-0001-VND

16107000

PO Documents (PDF / image / Office · max 500 KB each)

Add file

No files selected

Next: the vendor re-uploads their PI against this PO → Plant Accounts pay the milestones → trial after the advance (final payment gated).

Issue PO to vendor

A different link on a different page — and each page rejects the other's link outright, so one person's link can never do the other's job. Satish sees the invoice and the FA codes, enters the PO number, confirms the amount and attaches the PO document.

Amber CAPEX · Global Accounts — Issue PO

✓

PO Issued · PO/JP1/2627/0091

The vendor can now download the PO and re-upload their Proforma Invoice against it. Plant Accounts then record the milestone payments; after the advance is paid the vendor uploads the item trial, and the final payment waits for sourcing approval.

1. PO issued to vendor

2. Vendor re-uploads the PI against the PO

3. Plant Accounts tick the advance payment

4. Trial upload (after advance) → sourcing approve → final payment unlocks

PO Issued · PO/JP1/2627/0091, with the remaining sequence restated so nobody has to hold it in their head.

Slide 9.7 · The vendor gets the purchase order

 REVERSE AUCTION

CAP-2627-0001: Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton)

You are bidding as: **Tata Motors Ancillaries** (VND-001)

All prices in INR

No action needed — waiting on Amber.

Quotation Approved

✓

Proforma Invoice Submitted

Thank you. Your PI has been sent to Amber's buyer and accounts team for PO processing and payment.

🕒

TAT Clock — Grace Period

Delay liability begins in 7 days (PI + 1 week). No deduction yet.

📄

Purchase Order

PO NUMBER

PO/JP1/2627/0091

PO AMOUNT

₹1,61,07,000

Download PO Document

PO received from Amber · Issued 22 Aug 2026, 07:54

📄

Re-upload Proforma Invoice against the PO

Amber has requested a revised Proforma Invoice against the issued PO. Upload the updated document below.

PI Amount (₹)

16107000

Proforma Invoice File *

ProformaInvoice_TMA-PI-2627-118.pdf

Note (optional)

Any remarks for the buyer...

Submit Revised Proforma Invoice

Payment Status

Advance (30%)	₹48,32,100 Pending
On Dispatch (60%)	₹96,64,200 Pending
On Installation (10%)	₹16,10,700 Pending

A purchase-order card with number, amount, a download button and the issue timestamp — plus a **re-upload the proforma invoice against this PO** card, because an invoice raised before the PO often has to be reissued against it, and the payment status showing what is due and when.That re-upload window **closes the moment the first payment is made**. Once money has moved against the invoice on file, revising it would change what was already paid.

Slide 9.8 · Payment milestones — and the one that is locked

Amber CAPEX · Plant Accounts

PLANT ACCOUNTS — FA CODES, PO & PAYMENTS

Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton)

CAP-2627-0001

1. FA codes

2. PO (Satish)

3. Payments

4. Done

Field: Brown Field

Plant: Jhajjar Plant 1

Vendor: Tata Motors Ancillaries

Order value: ₹1,61,07,000

Proforma Invoice · ₹1,61,07,000

ProformaInvoice_TMA-PI-2627-118.pdf

ORDERED ITEMS & FA CODES

1. Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton) · Qty 1

FA-JP1-2627-0114

PO/JP1/2627/0091

PO value ₹1,61,07,000 · Issued by Global Accounts (Satish)

PurchaseOrder_PO-JP1-2627-0091.pdf

PAYMENT MILESTONES

☐ Advance (30% · On PO)

₹48,32,100

☐ On Dispatch (60% · On dispatch)

₹96,64,200

☐ On Installation (10% · On installation) FINAL

₹16,10,700

Blocked until the item trial is approved by sourcing.

Paid: ₹0

Outstanding: ₹1,61,07,000

The milestones come from the vendor's payment terms, not from a number somebody typed:

Milestone	Share	Amount	Trigger
Advance	30%	₹48,32,100	On PO
On Dispatch	60%	₹96,64,200	On dispatch
On Installation FINAL	10%	₹16,10,700	On installation

The last one is visibly locked: *"Blocked until the item trial is approved by sourcing."* It is not merely greyed out in the interface — the underlying action refuses it.

Ticking the advance also starts the expected final-payment date, calculated from the vendor's own delivery lead time, and opens the trial.

Slide 9.9 · The trial

No action needed — waiting on Amber.

Quotation Approved

✓

Proforma Invoice Submitted

Thank you. Your PI has been sent to Amber's buyer and accounts team for PO processing

 **REVERSE AUCTION**
CAP-2627-0001: Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton)

You are bidding as: **Tata Motors Ancillaries** (VND-001)

All prices in **INR**

Delay liability begins in 7 days (PI + 1 week). No deduction yet.

Purchase Order

PO NUMBER
PO/JP1/2627/0091

PO AMOUNT
₹1,61,07,000

[Download PO Document](#)

PO received from Amber · issued 22 Aug 2026, 07:54

Payment Status

Advance (30%)	₹48,32,100 ☒ Paid
On Dispatch (60%)	₹96,64,200 ☒ Paid
On Installation (10%)	₹16,10,700 ☐ Pending

Item Trial Awaiting Trial Upload

Upload a trial video, photo, or inspection report of the item for sourcing to review.

[Choose file](#) TrialReport_CMF-24-1300.pdf

Trial run completed at our Pune works on 19-Aug-2026 and witnessed by Amber QA. 8-hour continuous run, 1,244 kg/h against a 1,200 kg/h target, dosing accuracy $\pm 0.21\%$, full colour changeover in 9 min 40 s. All 42 MES tags read over OPC-UA. Report attached.

[Submit Trial](#)

"Upload a trial video, photo, or inspection report of the item for sourcing to review." The vendor attaches the evidence and a note:

"Trial run completed at our Pune works on 19-Aug-2026 and witnessed by Amber QA. 8-hour continuous run, 1,244 kg/h against a 1,200 kg/h target, dosing accuracy $\pm 0.21\%$, full colour changeover in 9 min 40 s. All 42 MES tags read over OPC-UA. Report attached."



CAPEX Portal
Amber Enterprises

WORKSPACE

Dashboard

Requests

Vendors

CAPEX Master

Budget Planning

Adhoc Budget

Accounts

NK

Neha Kapoor
Sourcing Member

Log out

All Plants

CAPEX Detail

Request view

Delay maturity begins in 7 days (17.17 weeks). No deduction yet.

Item Trial

Trial Under Review

TrialReport_CMF-24-1300.pdf

Trial run completed at our Pune works on 19-Aug-2026 and witnessed by Amber QA. 8-hour continuous run, 1,244 kg/h against a 1,200 kg/h target, dosing accuracy ±0.21%, full c...

Download

Reason (if rejecting)...

Approve Trial

Reject Trial

Vendor submitted: Trial run completed at our Pune works on 19-Aug-2026 and witnessed by Amber QA. 8-hour continuous run, 1,244 kg/h against a 1,200 kg/h target, dosing accuracy ±0.21%, full colour changeover in 9 min 40 s. All 42 MES tags read over OPC-UA. Report attached.

Item Trial

Awaiting Trial Upload

Waiting for the vendor to upload the trial.

Award — Tata Motors Ancillaries

Awarded vendor: Tata Motors Ancillaries · Order value ₹1,61,07,000

Proforma Invoice · ₹1,61,07,000

ProformaInvoice_TMA-PI-2627-118.pdf

PO issued — Plant Accounts are recording milestone payments on the emailed link.

Plant Accounts act on the secure emailed link — no portal login.

Copy link

Preview email

Open

http://localhost:3000/po/po_award_inv-1787362085177-v1_1a30b9b3f50f4011b90041db30c7d3ec

FA CODES · Plant Accounts

Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton)

FA-JP1-2627-0114

PO/JP1/2627/0091

PO value ₹1,61,07,000 · Issued by Global Accounts (Satish)

PurchaseOrder_PO-JP1-2627-0091.pdf

PAYMENT MILESTONES

Advance (30% · On PO)

₹48,32,100

On Dispatch (60% · On dispatch)

₹96,64,200

On Installation (10% · On installation) FINAL

₹16,10,700

Sourcing reviews it on the request page: download the file, read the note, then **Approve Trial** or **Reject Trial** with a reason — a rejection sends the vendor back to re-upload.

Slide 9.10 · Settled

Amber CAPEX · Plant Accounts

PLANT ACCOUNTS — FA CODES, PO & PAYMENTS

Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton)

CAP-2627-0001

1. FA codes

2. PO (Satisfish)

3. Payments

4. Done

Field: Brown Field

Plant: Jhajjar Plant 1

Vendor: Tata Motors Ancillaries

Order value: ₹1,61,07,000

Proforma Invoice · ₹1,61,07,000

ProformaInvoice_TMA-PI-2627-118.pdf

ORDERED ITEMS & FA CODES

1. Centralised Material Feeding for Molding Machines (24 Machine, 450T to 1300Ton) · Qty 1

FA-JP1-2627-0114

PO/JP1/2627/0091

PO value ₹1,61,07,000 · Issued by Global Accounts (Satisfish)

PurchaseOrder_PO-JP1-2627-0091.pdf

PAYMENT MILESTONES

☒

Advance (30% · On PO)

₹48,32,100

☒

On Dispatch (60% · On dispatch)

₹96,64,200

☒

On Installation (10% · On installation) FINAL

₹16,10,700

Paid: ₹1,61,07,000

Outstanding: ₹0

All payments cleared · ₹1,61,07,000

With the trial approved, the final milestone unlocks. All three ticked: **Paid ₹1,61,07,000 · Outstanding ₹0 · All payments cleared**, the rail on **4. Done**, and the delay clock stopped.

The vendor's own view of the same moment, on a phone: **TAT Closed — Final Payment Made · Delivered within TAT — no delay deduction**, the purchase order still downloadable, all three milestones paid and the trial marked approved. Every screen a vendor ever sees works at this size.

Once the L&T award finished the same way, CAP-2627-0001 moved to **Completed**.

Part 10 — Foreign vendors, Incoterms and currency

Run on the second request, CAP-2627-0002 — a *Shrink less Vertical M/C* for the Copper Shop, allocated ₹2.10 Cr — which was quoted by an Indian vendor and a German one.

Slide 10.1 · Adding a foreign vendor mid-enquiry

 CAPEX Portal
Amber Enterprises

WORKSPACE

- Dashboard
- Requests
- Vendors
- CAPEX Master
- Budget Planning
- Adhoc Budget
- Accounts

 Neha Kapoor
Sourcing Member

[Log out](#)

[All Plants](#) CAPEX Detail > Request view

COMPLETE DESCRIPTION Shrinkless vertical hairpin expander for the HEX line — 1200 mm bed, expansion force not less than 120 kN, suitable for 9.52 mm copper hairpins with NIL shrinkage....
[Show more](#)

QUOTATION

VENDOR QUOTATIONS (0)

No vendor quotation has been captured yet — sourcing will obtain quotations by RFQ or reverse auction after approval.

Sourcing setup

Optionally require an item trial before you approve a vendor. Add vendors from the invite options below.

☐ **Require an item trial before final payment** — after the advance is paid, the awarded vendor uploads a trial video / photo / report for your approval; the final payment stays blocked until you approve it. Set this **before** approving the vendor.

RFQ — Request for Quotation

Vendors quote each line first. Counter inline, set the per-line Final Decision, then accept — or escalate to a live auction.

[Invite vendors \(send link\)](#)

[Invite new vendor](#)

NEW / ONE-TIME VENDOR — MARK FOREIGN TO COLLECT INCOTERMS WITH THEIR QUOTATION

Name

Email

Phone

Vendor name

name@vendor.com

Optional

☐ **Foreign / international vendor** — the Incoterms (2020) questionnaire is presented when they submit their quotation, then negotiated here until agreed.

[Send invite](#)

No vendors invited yet. Invite vendors to send them the quotation link.

STATUS HISTORY

 In Sourcing

 Plant Head (email) 22 Aug 2026, 06:49

 With Plant Head

 Arjun Mehta 22 Aug 2026, 06:44

Sourcing can add a vendor who is not on the master by name, email and phone — and tick **foreign / international vendor**. The caption states what that does: *"the Incoterms (2020) questionnaire is presented when they submit their quotation, then negotiated here until agreed."*

Slide 10.2 · Incoterms are collected with the quotation, not after it

REVERSE AUCTION
CAP-2627-0002: Shrink less Vertical M/C

You are bidding as: Kolbenschmidt Präzision GmbH (OT-598519)

All prices in INR

#	DESCRIPTION	QTY	UOM	HSN / GST	UNIT PRICE (€)	LINE TOTAL
1	Shrink less Vertical Expansion Force with NIL shrinkage with the Amber H PLC with recipe validation trial and shrinkless vertical expansion force with NIL shrinkage with the Amber H PLC with recipe validation trial and					€250,160 €212,000 + €38,160 GST

Additional Charges

Freight & Handling (€) 9800

Delivery & Validity

Delivery Lead Time (days) 150

Currency EUR

Grand Total Summary

Subtotal (line items) €212,000

Total Additional Charges €38,160

Grand total €276,860

One last step — INCO Terms (Incoterms 2020)

As an international supplier, confirm the delivery, cost and risk terms for this quotation. Your quotation is submitted together with these answers.

Incoterm rule * FOB

Place / port of delivery *

Mode of transport * Sea

Who arranges main freight * Select...

Freight cost borne by * Select...

Who arranges insurance * Select...

Insurance cost borne by * Select...

Export customs clearance * Select...

Import customs & duties * Select...

Risk transfers at * Select...

Loading / unloading responsibility * Select...

Delivery timeline, currency & remarks

Delivery timeline, currency & any remarks...

Submit Terms & Quotation Back to quotation

Answer every required question to submit.

Kolbenschmidt Präzision GmbH prices the machine at **€212,000**, and on clicking submit gets one more step: the **Incoterms 2020 agreement** — twelve questions covering the rule, the place of delivery, the mode of transport, who arranges and who pays for the main freight and the insurance, who clears export and who pays import duty, where risk transfers, and who loads and unloads.

They answer CIP Mundra, sea freight, seller-arranged and seller-paid freight and insurance, seller export clearance, buyer import duty, risk at carrier handoff — and the quotation and the terms are submitted **together**. Close the questionnaire without answering and the quotation is not sent at all.

This is the difference between knowing the landed cost and finding out about it at the port.

Slide 10.3 · Sourcing negotiates the terms like a price

The **Final Decision** column (Price / Disc / Vendor) records the negotiated award per line — the same as the reverse auction. **Accept** finalizes a vendor for the single-vendor Proforma Invoice & fulfillment.

INCO TERMS — FOREIGN VENDORS

Kolbenschmidt Präzision GmbH

Your turn — review the vendor's Incoterms.

Needs Review Close ^

Review the vendor's answers below. Approve them, edit any field and send it back for the vendor to confirm, or reject.

Incoterm rule

CIP

Place / port of delivery

Mundra Port, Gujarat, India

Mode of transport

Sea

Who arranges main freight

Seller

Freight cost borne by

Seller

Who arranges insurance

Seller

Insurance cost borne by

Seller

Export customs clearance

Seller

Import customs & duties

Buyer

Risk transfers at

Carrier handoff

Loading / unloading responsibility

Seller loads / Buyer unloads

< Collapse

NK

Neha Kapoor

Sourcing Member

[→ Log out

The answers land in an **INCO Terms** tracker beside the quotation. Sourcing can approve them, edit any field and send them back with a note for the vendor to confirm, or reject them. The loop runs until both sides agree — and until they do, **the vendor cannot be awarded**. The grid says so, on the vendor's own column: *"INCO Terms open — settle before award."*

Slide 10.4 · Everything that compares vendors converts to rupees first

 **CAPEX Portal**
Amber Enterprises

WORKSPACE

- Dashboard
- Requests
- Vendors
- CAPEX Master
- Budget Planning
- Adhoc Budget
- Accounts

All Plants

CAPEX Detail

Request view

  **Neha Kapoor**
Machinery

 **RFQ — Request for Quotation**
Vendors quote each line first. Counter inline, set the per-line Final Decision, then accept — or escalate to a live auction.

2 need review

 Invite vendors (send link)  Invite new vendor

ITEM	DESCRIPTION	QTY	HSN / GST	Q1 OT-598519 Kolbenschmidt Präzis... Needs Review INCO Terms open — settle before award Counter Copy link	Q2 VND-005 Delta Electronics Needs Review Counter Copy link	FINAL DECISION
Shrink less Vertical M/C	Shrinkless vertical hairpin expander for the HEX line— 1200 mm bed, expansion force not less than 120 kN, suitable for 9.52 mm copper hairpins with NIL shrinkage. Servo-driven mandrel with quick-change tooling that mates with the Amber HEX standard interface, integrated bell-mouth forming, and a PLC with recipe storage. Supply, installation, commissioning and a shrinkage-validation trial are in scope.	1	8462 GST 18%	₹1,97,16,000 €212,000 EUR Subtotal: ₹1,97,16,000 + ₹35,48,880 GST Total: ₹2,32,64,880 €250,160 EUR ↓ Lowest	₹2,04,00,000 Subtotal: ₹2,04,00,000 + ₹36,72,000 GST Total: ₹2,40,72,000	PRICE (₹) 0 DISC % 0 Select vendor... Price x Qty: ₹0
Transportation / Freight				₹9,11,400 (€9,800 EUR)	₹3,40,000	
Packing / Forwarding				₹2,23,200 (€2,400 EUR)	₹95,000	
Service / Installation				₹13,48,500 (€14,500 EUR)	₹5,20,000	
Delivery Lead Time (Weeks)				—	—	
Warranty (Years)				3	2	
Currency				EUR	INR	
Grand Total (incl. GST)				₹2,57,47,980 €276,860 EUR incl. ₹35,48,880 GST	₹2,50,27,000 L1 incl. ₹36,72,000 GST	
ACTIONS				 Accept X Decline	 Accept X Decline	

The Final Decision column (Price / Disc / Vendor) records the negotiated award per line — the same as the reverse auction. **Accept** finalizes a vendor for the single-vendor Proforma Invoice & fulfillment.

INCO TERMS — FOREIGN VENDORS

Kolbenschmidt Präzision GmbH

Your turn — review the vendor's Incoterms.

Needs Review Review

TECHNICAL SPEC APPROVAL — REQUIRED BEFORE AWARD

Kolbenschmidt Präzision GmbH SPEC-4XBFCL

Attach the spec documents and send them to the Technical team.

Spec Not Sent Prepare

Delta Electronics SPEC-LXDA8M

Attach the spec documents and send them to the Technical team.

Spec Not Sent Prepare

Pick a vendor and final price for each line in the Final Decision column to approve & request Pls.

 Escalate to a live reverse auction. The current best price (**₹2,50,27,000**) drops 5% to become the new price to beat, and every vendor's rank resets — vendors must submit a fresh bid to reveal their rank.

Start Reverse Auction

NEGOTIATION HISTORY (2)

STATUS HISTORY

 Collapse

 **Neha Kapoor**
Sourcing Member

Log out

The German quotation is in euros and the Indian one in rupees, so the grid shows **rupees first with the vendor's own currency underneath**:

	Kolbenschmidt Präzision GmbH	Delta Electronics
Machine	₹1,97,16,000 (€212,000)	₹2,04,00,000
Freight	₹9,11,400 (€9,800)	₹3,40,000
Packing	₹2,23,200 (€2,400)	₹95,000
Service / installation	₹13,48,500 (€14,500)	₹5,20,000
Warranty	3 years	2 years
Whole quotation, incl. GST	₹2,57,47,980 (€276,860)	₹2,50,27,000 L1

Read the two rows together and the point becomes obvious: the German machine is **cheaper on the machine itself** and marked ↓ *Lowest* on that line, but once freight, packing and installation are in, the Indian vendor is cheaper on the **whole quotation** and takes L1. Both facts are true, both are shown, and each figure states which basis it is on.

What the vendor contractually offered is always displayed in the currency they offered it in. Anything that **compares** vendors, or that Accounts will act on, converts to rupees first.

Part 11 — The reverse auction

Slide 11.1 · Auctions are escalated, never started cold

At the bottom of the quotation grid sits the escalation offer, with the consequence spelled out before the click:

"Escalate to a live reverse auction. The current best price (₹2,50,27,000) drops 5% to become the new price to beat, and every vendor's rank resets — vendors must submit a fresh bid to reveal their rank."

An auction needs at least two real quotations to escalate from. Without competing prices there is nothing to beat.

Slide 11.2 · Configuring the auction

Accounts

Reverse Auction Setup

Select Vendors (2 selected)

Auction Dates & Times

Auction Date

25/08/2026

Open Time

11:00 AM

Close Time

12:00 PM

Bidder Acceptance Deadline Date

24/08/2026

Bidder Acceptance Deadline Time

05:00 PM

Vendor Revert Expected By

24/08/2026, 02:55 AM

Auction Rules (Optional)

Bid Validity (Days)

180

Max Decrements

5

Extension (Mins)

15

Max Extensions

2

Currency

INR

Auction Configuration

Duration (Days)

7 days

Threshold Price (₹)

25027000

Pre-filled from lowest RFQ quote (₹2,50,27,000) — editable.

Generate & Send to Vendors

Cancel

One form, in four blocks:

- **Auction dates and times** — auction date, opening time, closing time, the deadline by which bidders must accept, and when vendors are expected to revert.
- **Auction rules** — bid validity (180 days), maximum decrements in one go (5), time extension (15 minutes, maximum 2 per bidder), currency.
- **Auction configuration** — duration, and the **threshold price**, pre-filled from the lowest quotation received and editable.
- **Generate & send to vendors.**

Slide 11.3 · The Business Rules document

Business Rules for Reverse Auction - Preview

Print

BUSINESS RULES FOR REVERSE AUCTION

(Annexure – I)

Auction No:
CAP-2627-0002

Closing Date/Time:
25/08/2026 12:00 Hrs

Amber Enterprises India Limited ('Amber') will be finalizing the rates for the procurement of **Shrink less Vertical M/C** through Reverse Auction mode.

Name of Work: Shrink less Vertical M/C

Bidders are requested to go through the guidelines given herein below and submit their acceptance before the **24/08/2026 02:55 AM**.

1. Procedure of Reverse Auctioning:

- Eligibility for Bidding: Price bids shall be opened for all techno-commercially qualified bidders.
- Bid decrement: The bid decrement will be determined by Amber.
- Ranking order for Bids: Lowest to Highest.
- Max decrements at one go: 5

2. Schedule for reverse auction:

Date: 25/08/2026
Opening Time: 11:00 Hrs
Closing Time: 12:00 Hrs

The portal generates a printable "**Business Rules for Reverse Auction (Annexure – I)**" — auction number, closing date and time, the name of work, the acceptance deadline, the bidding procedure, and the embedded Commercial Terms, Performance Bank Guarantee and Delay Liability Clause. This is the document vendors legally accept in order to be allowed to bid.

Slide 11.4 · Nobody bids until they have accepted

Auction Document & Vendor Approvals

View Document

0
APPROVED

2
PENDING

0
REJECTED/EXCLUDED

0
OVERDUE

VENDOR APPROVAL TRACKER

Deadline: 24/8/2026, 2:55:00 am

K	Kolbenschmidt Präzision GmbH OT-598519	Pending	🔔	🚫	📄
D	Delta Electronics VND-005	Pending	🔔	🚫	📄

DURATION (DAYS)

THRESHOLD PRICE (₹)

7 days

25027000

Start Auction (needs ≥1 approval)

🕒 At least one vendor must approve the document before starting the auction.

The **vendor approval tracker** counts approved, pending, rejected/excluded and overdue, shows the revert deadline, and per vendor offers a reminder, an exclusion and a copy-link. **Start Auction is disabled** — "At least one vendor must approve the document before starting the auction."

Slide 11.5 · The vendor's acceptance screen

REVERSE AUCTION
CAP-2627-0002: Shrink less Vertical M/C

You are bidding as: **Delta Electronics** (VND-005)

All prices in **INR**

Auction Rules

☐ Bid validity: **180 days**

☐ Max decrements per bid: **5**

☐ Time extension: **15 minutes** (max 2 per bidder)

☐ Currency: **INR**

 **Commercial Terms**

These commercial terms govern the supply against this enquiry, including scope, quality, inspection, packing, freight, and warranty obligations as communicated by Amber Enterprises India Ltd. Payment terms: 60 Days from the date of Invoice (Open Account).

☐ **Performance Bank Guarantee**

Performance Bank Guarantee (PBG): The supplier shall furnish a Performance Bank Guarantee equal to 10% of the order value, valid through the warranty period, towards due performance of the contract. The PBG will be released on successful completion of supply, installation, and the warranty obligations.

☒ **Delay Liability Clause**

Delay Liability Clause (DLC): A Turn-Around-Time (TAT) begins one week after the Proforma Invoice is raised. A deduction of 0.5% of the order value applies for every week of delay. Once cumulative deductions reach 5%, the deduction rate escalates to 5% of the order value per week thereafter. Deductions stop when the final payment is released.

By confirming your participation, you agree to the Business Rules, the Commercial Terms, the Performance Bank Guarantee, and the Delay Liability Clause. You will be eligible to bid once the auction begins.





Response deadline, auction summary, the four rules, then the commercial terms, the bank guarantee and the delay clause in full, and the binding sentence:

"By confirming your participation, you agree to the Business Rules, the Commercial Terms, the Performance Bank Guarantee, and the Delay Liability Clause. You will be eligible to bid once the auction begins."

Approve & Participate or **Decline Participation**.

Slide 11.6 · Live

CAPEX Portal
 Amber Enterprises

[All Plants](#)
CAPEX Detail
[Request view](#)

€276,860

Shrink less Vertical M/C

€212,000 × 1 = **€212,000**

Sourcing setup

Optionally require an item trial before you approve a vendor. Add vendors from the invite options below.

☐ **Require an item trial before final payment** — after the advance is paid, the awarded vendor uploads a trial video / photo / report for your approval; the final payment stays blocked until you approve it. Set this **before** approving the vendor.

Reverse Auction 6d 23h 59m

Threshold: **₹2,50,27,000** | Ends: **29 Aug 2026, 08:34 am**

[+1d](#) [+3d](#) [+7d](#) [Close Auction Now](#)

APPROVED VENDORS ONLY 2 eligible

K

Kolbenschmidt Präzision GmbH
OT-598519

Invited

Copy Link

D

Delta Electronics
VND-005

Invited

Copy Link

Add vendor to auction... [+ Add](#)

OPENING PRICE TO BEAT — WHOLE QUOTE

₹2,02,87,250

Incl. freight / packing / service. The ranking below is on the bid subtotal — a different basis.

Best RFQ price cut 5% at auction start. All ranks reset — vendors must submit a fresh bid to reveal their rank.

No bids yet — vendors bid to reveal their rank.

ITEM	DESCRIPTION	# QTY	Q1 OT-598519 Kolbenschmidt Pr...	Q2 VND-005 Delta Electronics	+ ADD OFFER	Final Decision Price · Disc · Vendor · Total
Shrink less Vertical M/C cm-7894903a-1613-4fa8-8c18-c8e714074ca2	Shrinkless vertical hairpin expander for the HEX line — 1200 mm bed, expansion force not less than 120 kN, suitable for 9.52 mm copper hairpins with NIL shrinkage. Servo-driven mandrel with quick-change tooling that mates with the Amber HEX standard interface, integrated bell-mouth forming, and a PLC with recipe storage. Supply, installation, commissioning and a shrinkage-validation trial are in scope.	1	₹0 Total: ₹0	₹0 Total: ₹0		PRICE (₹) 0 DISC (%) 0 SELECT VENDOR Select Vendor Price × QTY: ₹0 ₹ freight ₹ packing charges
Transportation / Freight			0	0		
Packing / Forwarding			0	0		

[Collapse](#)[Log out](#)

With both vendors accepted, the auction starts. Sourcing gets a countdown, the threshold, the eligible-vendor list with copy links, quick **+1d / +3d / +7d** extensions, and **Close Auction Now** — an auction can end on the clock or on demand.

The green panel states the opening price and how it was derived: **₹2,02,87,250 — best quotation cut 5% at auction start. All ranks reset — vendors must submit a fresh bid to reveal their rank.** It also names its own basis: *"Incl. freight / packing / service. The ranking below is on the bid subtotal — a different basis."*

Slide 11.7 · The bid screen



REVERSE AUCTION
CAP-2627-0002: Shrink less Vertical M/C

6d 23h 58m

You are bidding as: **Delta Electronics** (VND-005)
All prices in INR

YOUR RANK
Submit a bid to see your rank.

BEST PRICE
₹2,02,87,250
Beat this to take L1

YOUR BID TOTAL
Within threshold of ₹2,50,27,000

Auction Rules

Request Details

Bid Entry

#	DESCRIPTION	QTY	UOM	HSN / GST	UNIT PRICE (₹) *	LINE TOTAL
1	Shrink less Vertical M/C Shrinkless vertical hairpin expander for the HEX line — 1200 mm bed, expansion force not less than 120 kN, suitable for 9.52 mm copper hairpins with NIL shrinkage. Servo-driven mandrel with quick-change tooling that mates with the Amber HEX standard interface, integrated bell-mouth forming, and a PLC with recipe storage. Supply, installation, commissioning and a shrinkage-validation trial are in scope. Shrinkless vertical hairpin expander for the HEX line — 1200 mm bed, expansion force not less than 120 kN, suitable for 9.52 mm copper hairpins with NIL shrinkage. Servo-driven mandrel with quick-change tooling that mates with the Amber HEX standard interface, integrated bell-mouth forming, and a PLC with recipe storage. Supply, installation, commissioning and a shrinkage-validation trial are in scope.	1	EA	8462 · 18%	0	—

Additional Charges

Freight & Handling (₹)
0

Packing & Forwarding (₹)
0

Service / Installation (₹)
0

Grand Total Summary

Subtotal Base
—

Total Additional
—

Grand Total

Reset Submit Bid

The vendor's screen is built around three numbers:

Your Rank	"Submit a bid to see your rank" — rank comes only from a live bid; escalation reset everybody
Best Price	₹2,02,87,250 — "Beat this to take L1"
Your Bid Total	live as they type, with "Within threshold of ₹2,50,27,000"

There is deliberately **one** price to beat, for the whole quotation — no per-line best price to reverse-engineer a competitor's costing from. It opens at the best quotation minus 5% and then moves **only when somebody actually beats it**.



You are bidding as: **Delta Electronics** (VND-005)

All prices in INR

YOUR RANK

Submit a bid to see your rank.

BEST PRICE

₹2,02,87,250

Beat this to take L1

YOUR BID TOTAL

₹1,99,30,000

Within threshold of ₹2,50,27,000

Auction Rules

Request Details

Bid Entry

#	DESCRIPTION	QTY	UOM	HSN / GST	UNIT PRICE (₹) *	LINE TOTAL
1	Shrink less Vertical M/C Shrinkless vertical hairpin expander for the HEX line — 1200 mm bed, expansion force not less than 120 kN, suitable for 9.52 mm copper hairpins with NIL shrinkage. Servo-driven mandrel with quick-change tooling that mates with the Amber HEX standard interface, integrated bell-mouth forming, and a PLC with recipe storage. Supply, installation, commissioning and a shrinkage-validation trial are in scope. Shrinkless vertical hairpin expander for the HEX line — 1200 mm bed, expansion force not less than 120 kN, suitable for 9.52 mm copper hairpins with NIL shrinkage. Servo-driven mandrel with quick-change tooling that mates with the Amber HEX standard interface, integrated bell-mouth forming, and a PLC with recipe storage. Supply, installation, commissioning and a shrinkage-validation trial are in scope.	1	EA	8462 - 18% GST ₹34,38,000	19100000	₹2,25,38,000 ₹1,91,00,000 + ₹34,38,000 GST

Additional Charges

Freight & Handling (₹)

300000

Packing & Forwarding (₹)

80000

Service / Installation (₹)

450000

Grand Total Summary

Subtotal Base

₹1,91,00,000

Total Additional

+₹8,30,000

Grand Total

₹1,99,30,000

Reset

Submit Bid

Delta bids ₹1,91,00,000 on the machine, for a bid total of ₹1,99,30,000 — under the price to beat.

Slide 11.8 · Ranks, on a common basis

CAPEX Portal

Amber Enterprises

All Plants

CAPEX Detail

Request view

NK

Neha Kapoor

Machinery

Shrink less Vertical M/C

₹227,000

₹212,000 × 1 = ₹212,000

Sourcing setup

Optionally require an item trial before you approve a vendor. Add vendors from the invite options below.

☐

Require an item trial before final payment — after the advance is paid, the awarded vendor uploads a trial video / photo / report for your approval; the final payment stays blocked until you approve it. Set this **before** approving the vendor.

Reverse Auction

6d 23h 45m

Threshold: ₹2,50,27,000

Ends: 29 Aug 2026, 08:34 am

+1d +3d +7d Close Auction Now

APPROVED VENDORS ONLY

2 eligible

K Kolbenschmidt Präzision GmbH

OT-598519

negotiating

Copy Link

D Delta Electronics

VND-005

negotiating

Copy Link

Add vendor to auction...

+ Add

OPENING PRICE TO BEAT — WHOLE QUOTE

₹2,02,87,250

Incl. freight / packing / service. The ranking below is on the bid subtotal — a different basis.

Best RFQ price cut 5% at auction start. All ranks reset — vendors must submit a fresh bid to reveal their rank.

VENDOR RANKING

Ranked on the bid subtotal (excl. freight / packing / service), in INR.

RANK	VENDOR	BID SUBTOTAL (₹)	GAP TO L1
L1	Kolbenschmidt Präzision GmbH	₹1,89,72,000 €204,000	Lowest
L2	Delta Electronics	₹1,91,00,000	+₹1,28,000

ITEM	DESCRIPTION	# QTY	Q1 OT-598519 Kolbenschmidt Pr...	Q2 VND-005 Delta Electronics	+ ADD OFFER	Final Decision
Shrink less Vertical M/C	Shrinkless vertical hairpin expander for the HEX line — 1200 mm bed, expansion force not less than 120 kN, suitable for 9.52 mm copper hairpins with NIL shrinkage. Servo-driven mandrel with quick-change tooling that mates with the Amber HEX standard interface, integrated bell-mouth forming, and a PLC with recipe storage. Supply, installation, commissioning and a shrinkage-validation	1	₹1,89,72,000 €204,000 EUR Total: ₹1,89,72,000 €204,000 EUR	₹1,91,00,000 Total: ₹1,91,00,000		Price - Disc - Vendor - Total PRICE (₹) 0 DISC (%) 0 SELECT VENDOR Select Vendor

Collapse

NK

Neha Kapoor

Sourcing Member

Log out

Both vendors rebid, and the ranking is stated with its basis in the heading — *ranked on the bid subtotal, in INR*:

Rank	Vendor	Bid subtotal	Gap to L1
L1	Kolbenschmidt Präzision GmbH	₹1,89,72,000 (€204,000)	Lowest
L2	Delta Electronics	₹1,91,00,000	+₹1,28,000

The German vendor came back at €204,000 and took first place by ₹1,28,000 — a gap of well under one percent, on a machine where the opening quotations were ₹7 lakh apart. That is what the auction is for.

From here the auction path and the quotation path converge completely: the same per-line Final Decision, the same split-award bar, the same technical-specification gate, the same fulfilment chain described in Part 9.

Part 12 — The dashboards

Four dashboards, one per role. Nobody gets a generic "management view" — each person opens the portal onto the work that is actually theirs.

Slide 12.1 · The idea behind all four

Every dashboard in the product is built in the same three bands, in the same order:


1. **My turn** — what is waiting on *you*, right now.
2. **Waiting on** — what you have handed to somebody else, and how long they have had it.
3. **Outcomes** — what the work has actually delivered.

That order is deliberate. A dashboard that opens on a portfolio total tells you how the year is going; a dashboard that opens on *"four things are on your desk and the oldest has been there sixty-six days"* tells you what to do next.

Three rules run through all of them, and they are what make the numbers trustworthy:

- **Every figure states the basis it is on.** A number whose provenance is invisible is worse than no number. Where a figure is an estimate, it says so.
- **A tile and the list it links to always agree.** Click a tile reading 2 and you land on exactly those 2 rows, with the reason marked on each — not on a list of 11 that happens to contain them.
- **Where something cannot be measured, it says so rather than printing zero.** A plant with no budget recorded reads *unmeasurable*, because printing 0% would claim it spent nothing of its budget when the truth is that it has none.

Slide 12.2 · The buyer's dashboard

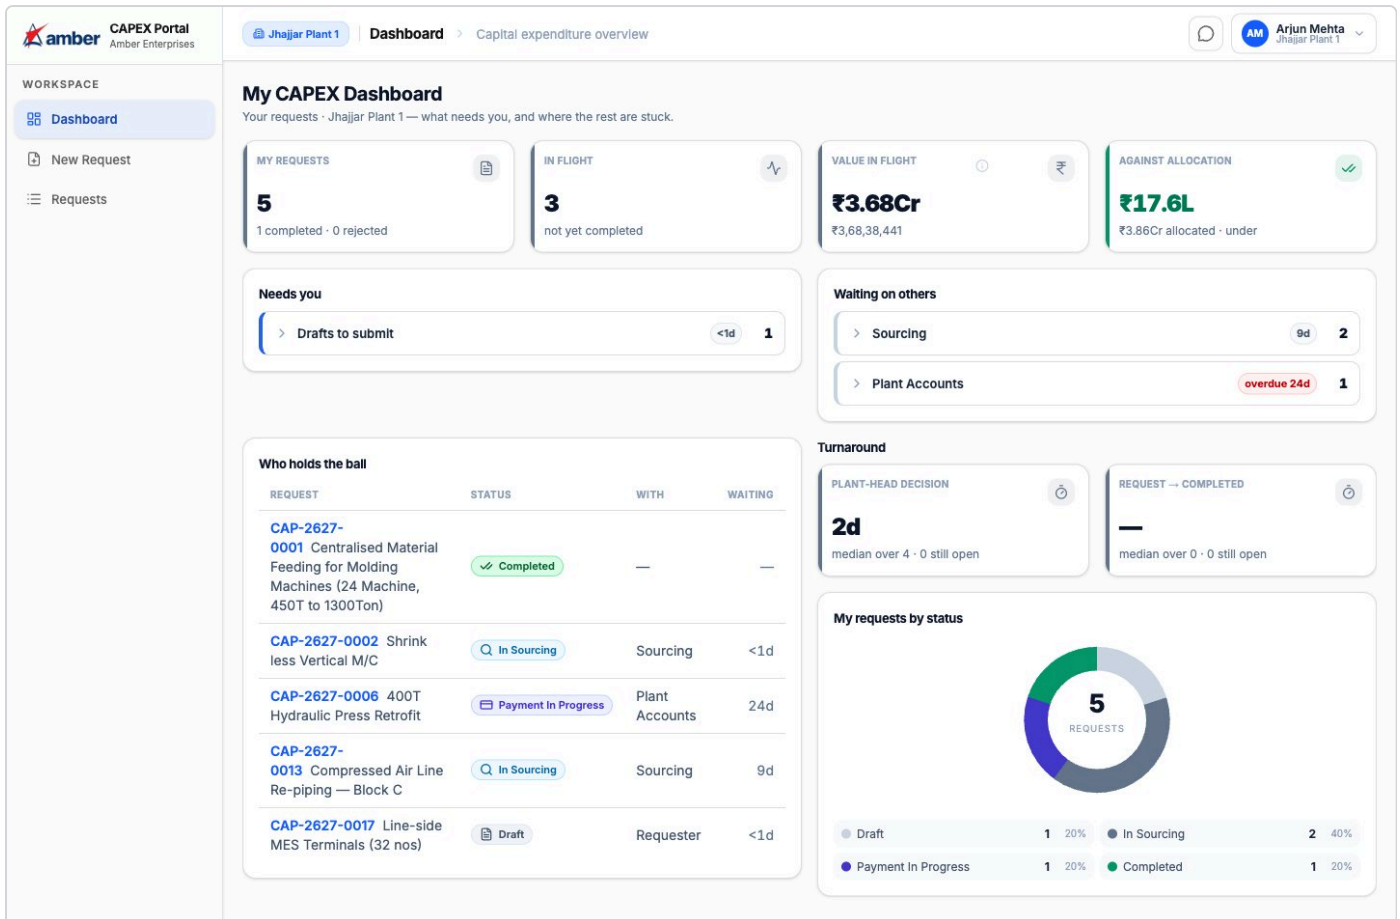

Arjun Mehta's view. It answers one question — *where are my requests, and what is holding them up?*

Title	What it counts	How to read it
My requests	Every request this buyer raised, in any state	5, of which 1 completed and 0 rejected
In flight	Raised but not yet completed	3 still moving
Value in flight	The money represented by those live requests	₹3.68 Cr — the exact figure is shown underneath, because a rounded crore figure is a poor basis for a conversation
Against allocation	Live value compared with the budget allocated to those same lines	₹17.6 L under ₹3.86 Cr allocated — green because under is good

Below the tiles:

- **Needs you** — the queue that is genuinely his: 1 draft to submit.
- **Waiting on others** — Sourcing has 2 of his requests (9 days); Plant Accounts have 1, marked **overdue 24d** in red.
- **Who holds the ball** — every live request, its status, who is holding it, and for how long. This is the table a buyer screenshots and sends to somebody.
- **Turnaround** — how long the plant head typically takes (2 days, measured over 4 decisions), and how long a request takes end to end. Each states how many it measured and how many are still open, because a median measured only over finished work reads fastest exactly when the most work is stuck.
- **My requests by status** — the mix at a glance.

Slide 12.3 · The sourcing cockpit — Desk

amber

CAPEX Portal
Amber Enterprises

Workspace

Dashboard

Requests

Vendors

CAPEX Master

Budget Planning

Adhoc Budget

Accounts

All Plants | Dashboard > Capital expenditure overview

NK

Neha Kapoor
Machinery

Sourcing Cockpit

All plants · what is blocked on you, who you are waiting on, and what your negotiations delivered.

All plants 18

Jhajjar Plant 1 5

Jhajjar Plant 2 4

SUPA 4

DDN-4 3

Sri City-1 2

Desk

Performance

Act on this first

ON YOUR DESK

12

oldest 66d · biggest: Tech spec to send (5)

PAST THRESHOLD (WHERE SET)

11

5 on you · 6 with others · measured over 4 of 6 live queues

WAITING ON OTHERS

7

oldest 24d · most with Plant Head (3)

LIVE AUCTIONS

1

next closes in 6d 23h 15m

Your turn

> New requests to pick up

24d

4

> Quotations to review

<1d

3

> Tech spec to send

overdue 66d

5

Waiting on others

> Vendor

overdue 22d

2

> Plant Head

overdue 9d

3

> Plant Accounts

overdue 24d

2

Auction watch

CAP-2627-0002

Shrink less Vertical M/C

2 bidders ₹1.99Cr 6d 23h 15m

Aging

Buckets are 0-3 / 3-7 / 7-14 / 14+ days, upper bound exclusive (a wait of exactly 7 days is in 7-14). 12 of 12 live request(s) have someone holding them and are bucketed below.

● Live requests

● Oldest bucket

0-3 days

Live requests

2

3-7 days

Live requests

1

7-14 days

Live requests

3

14+ days

oldest bucket — the one that matters

OLDEST BUCKET

6

6 of 12 live request(s) have been waiting 14 days or more — the oldest is CAP-2627-0006 at 24d with Plant Accounts.

CAP-2627-0006

400T Hydraulic Press Retrofit

with Plant Accounts 24d past threshold

CAP-2627-0010

Fire Hydrant Network Upgrade

with Sourcing 24d

CAP-2627-0008

Robotic Part Removal — 1300T Press

with Vendor 22d past threshold

CAP-2627-0011

Line-side MES Terminals (32 nos)

with Sourcing 18d

CAP-2627-0009

Scissor Lifter

with Vendor 17d past threshold

Showing the 5 oldest of 6.


Neha Kapoor runs sourcing across all plants, so her dashboard starts with a plant filter — *All plants 18*, then a chip per plant — and two tabs. **Desk** is the working tab.

Tile	What it counts	Reading it here
On your desk	Everything currently waiting on sourcing	12 · oldest 66 days · biggest single queue is <i>Tech spec to send</i> with 5
Past threshold	Items older than the agreed service level, split by who is holding them	11 · 5 on sourcing, 6 with others, measured over 4 of 6 live queues
Waiting on others	Handed out and not yet returned	7 · oldest 24 days · most sitting with plant heads
Live auctions	Auctions currently running	1 · next closes in 6d 23h

- **Your turn** — new requests to pick up (4), quotations to review (3), technical specs to send (5, flagged *overdue 66d*).
- **Waiting on others** — vendor (2, overdue 22d), plant head (3, overdue 9d), plant accounts (2, overdue 24d).
- **Auction watch** — every live auction with its bidder count, current best price and time left.
- **Aging** — live requests bucketed 0–3 / 3–7 / 7–14 / 14+ days, with the oldest bucket highlighted and its contents listed by name: *"6 of 12 live requests have been waiting 14 days or more — the oldest is CAP-2627-0006 at 24d with Plant Accounts."*

That last line is the whole design in miniature: not a chart to interpret, a sentence to act on.

Slide 12.4 · The sourcing cockpit — Performance

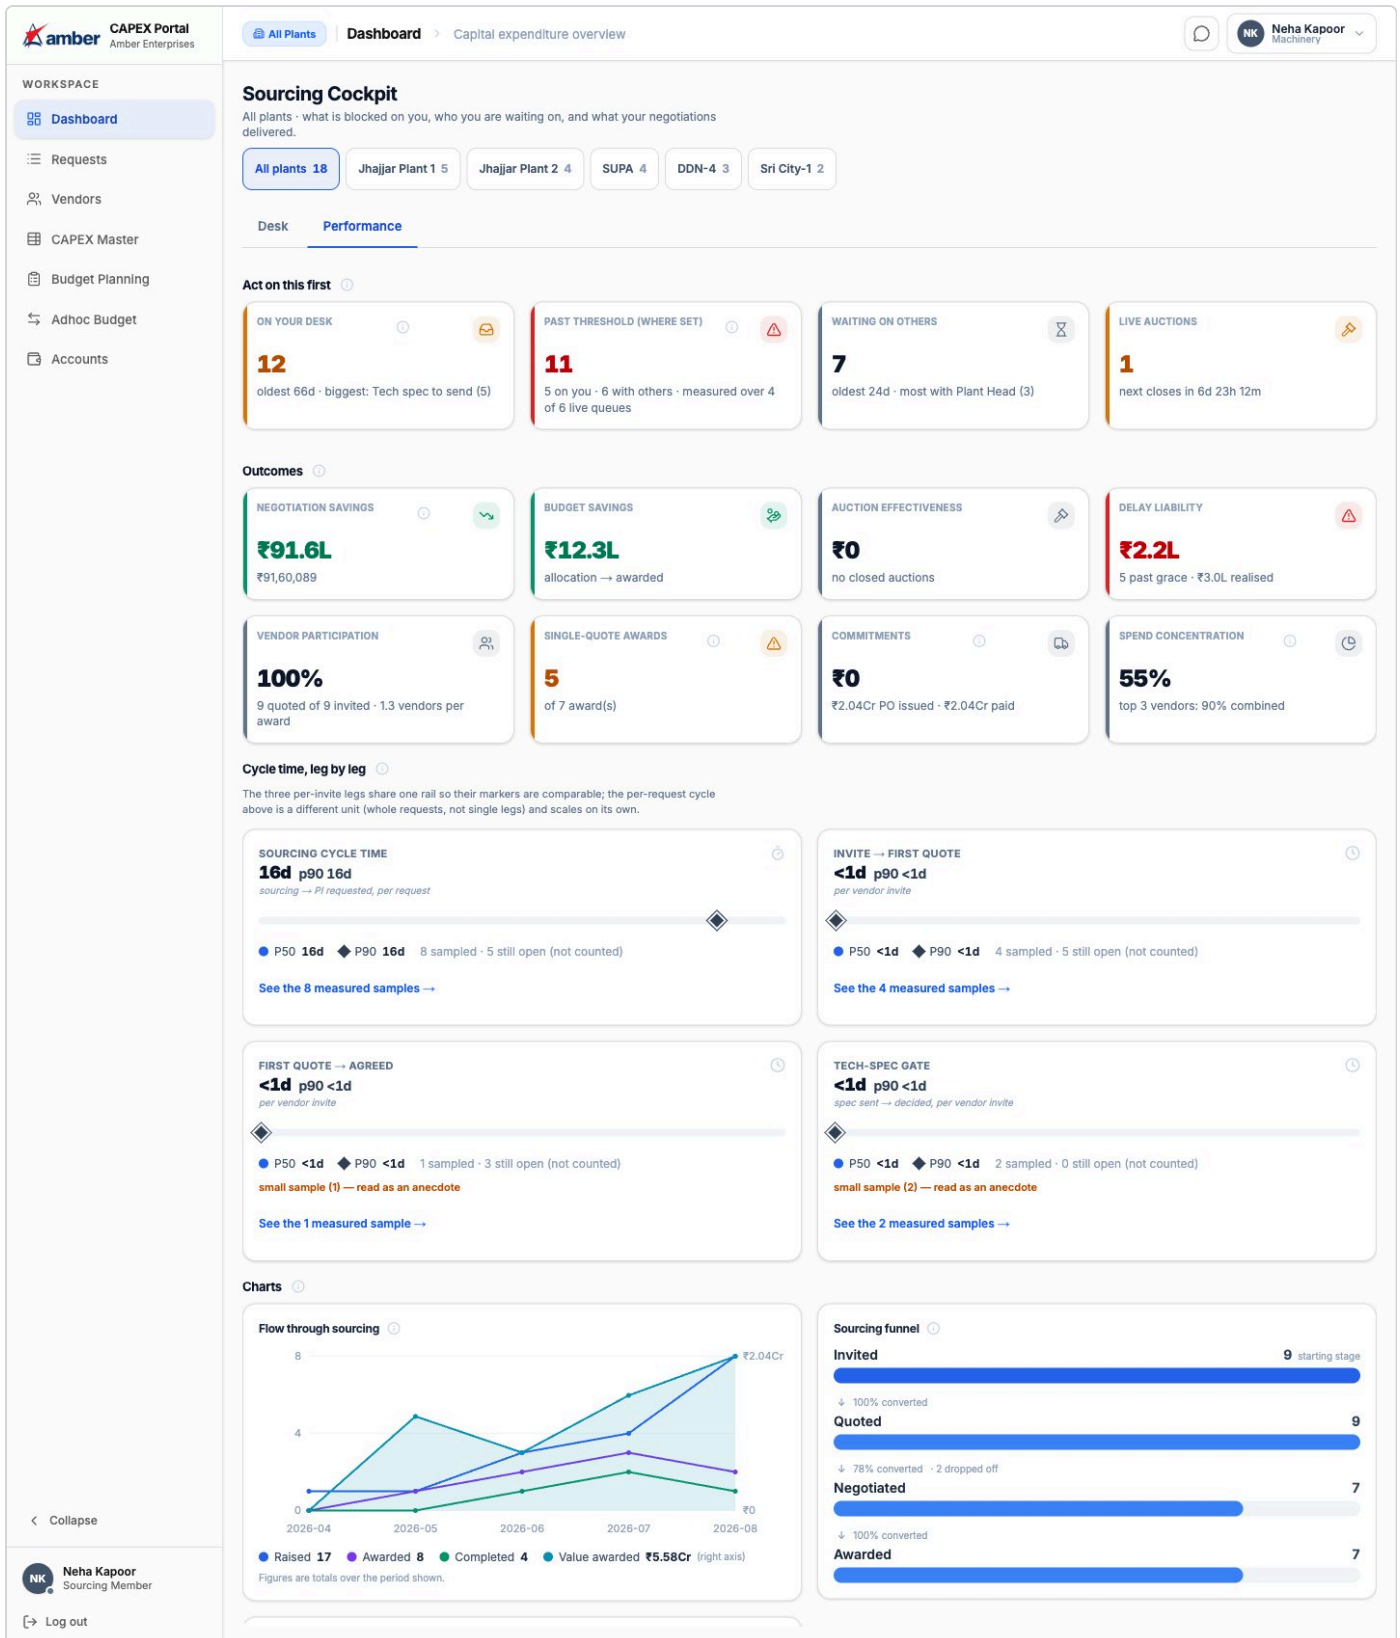

The same person, asking a different question: *did the negotiating actually deliver anything?*

Title	What it measures	Here
Negotiation savings	First quotation → final awarded price, like for like	₹91.6 L
Budget savings	Allocated budget → awarded price	₹12.3 L
Auction effectiveness	Value taken out by reverse auctions	₹0 — no auction has closed yet, and it says so rather than showing a flattering blank
Delay liability	Penalty accruing on late vendors	₹2.2 L · 5 past grace · ₹3.0 L already realised
Vendor participation	How many invited vendors actually quoted	100% — 9 of 9 · 1.3 vendors per award
Single-quote awards	Awards made against only one quotation	5 of 7 — amber, because a single-quote award is a governance flag, not an achievement
Commitments	PO issued against paid	₹2.04 Cr issued · ₹2.04 Cr paid
Spend concentration	Share of spend with the largest vendor, and the top three	55% · top 3 combined 90%

Cycle time, leg by leg measures four separate legs — sourcing cycle, invite → first quote, first quote → agreed, and the technical-spec gate — each showing the median and the 90th percentile, how many were measured, **how many are still open and therefore not counted**, and a plain warning when the sample is too small to mean anything (*"small sample (1) — read as an anecdote"*).

Then two charts: **flow through sourcing** month by month, and the **sourcing funnel** — invited 9 → quoted 9 → negotiated 7 → awarded 7, with the conversion and drop-off between each stage.

Slide 12.5 · Administration — My Desk


The screenshot shows the 'Administration - My Desk' dashboard in the CAPEX Portal. The interface includes a sidebar with navigation options like 'New Request', 'Requests', 'Vendors', 'CAPEX Master', 'Budget Planning', 'Adhoc Budget', 'Budget Approvals', 'Accounts', and 'Configurations'. The main area is titled 'Administration' and features a 'My Desk' tab. Under 'Waiting on you', there are four cards: 'PROPOSALS TO DECIDE' (0), 'ADHOC TRANSFERS' (0), 'AWAITING ACCOUNTS LINK' (0), and 'STUCK AT PLANT HEAD' (2). Below these is a 'Your approvals' section showing 'Requests stuck at the plant head' with a red 'overdue 9d' label and a count of 2. On the right, an 'Elsewhere in the chain' section shows a list of items: 'Sourcing' (24d, 5), 'Vendor' (overdue 22d, 2), and 'Plant Accounts' (overdue 24d, 2). The top navigation bar includes 'All Plants', 'Dashboard', and 'Capital expenditure overview'. The user is logged in as 'Super Admin' with 'Full Access'.

The administrator's dashboard opens, like everyone else's, on their own queue rather than on the portfolio.

Tile	What it counts
Proposals to decide	Budget proposals sitting at the admin gate, with their value
Adhoc transfers	Budget transfer requests awaiting approval
Awaiting accounts link	Approved budgets whose Global Accounts sign-off link still needs sending or chasing
Stuck at plant head	Requests waiting on a plant head past the threshold — 2 here, older than 3 days

Elsewhere in the chain shows where everything else in the company is sitting: 5 with sourcing, 2 with vendors, 2 with plant accounts, each with the oldest wait.

Slide 12.6 · Administration — Portfolio

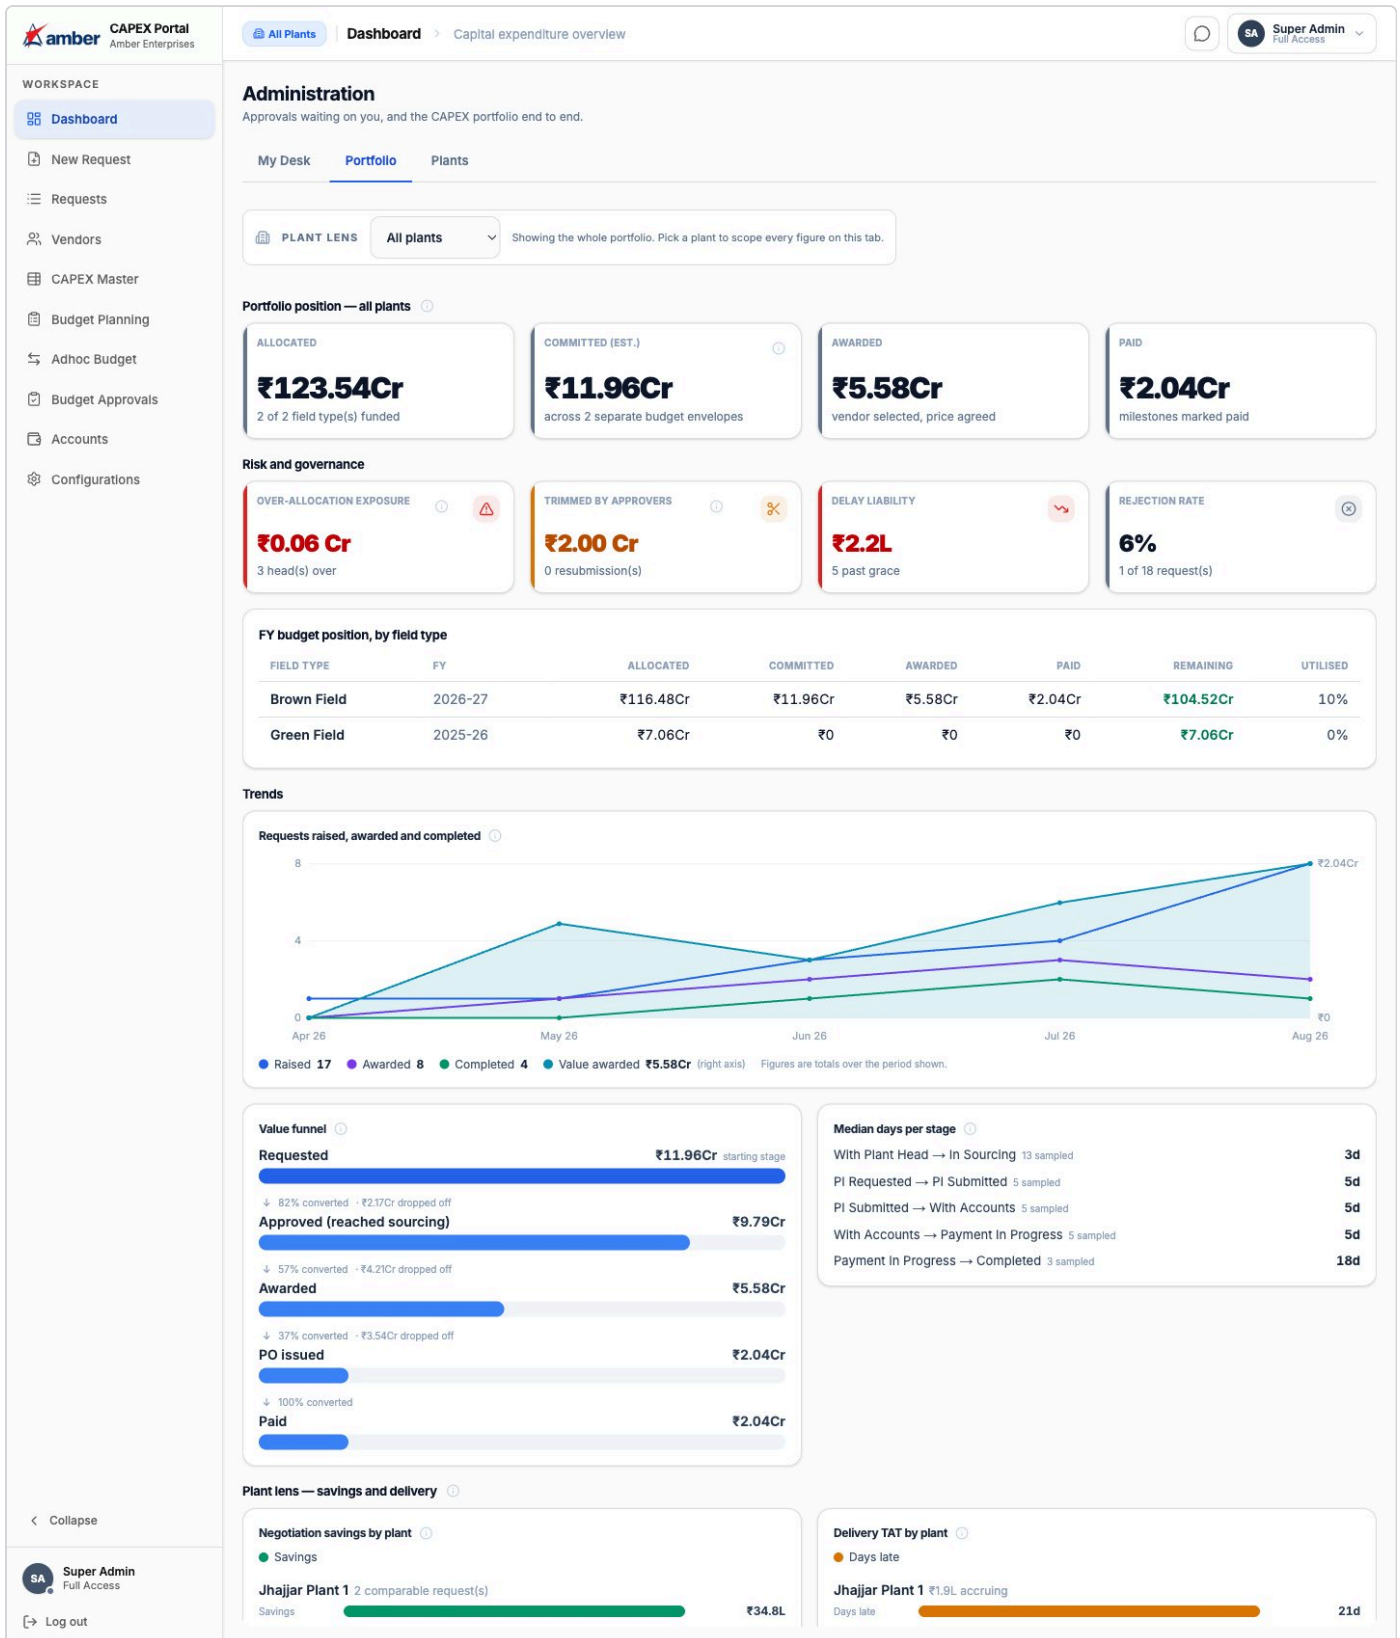

The money view, for all plants or for one — the **plant lens** at the top scopes every figure on the tab, and travels with you into the lists you click through to.

Portfolio position

Title	Meaning
Allocated ₹123.54 Cr	Approved budget across every funded kind of capital expenditure
Committed (est.) ₹11.96 Cr	What live requests represent — the awarded price where awarded, else the agreed or best quotation, else the estimate. An estimate basis, and labelled as one
Awarded ₹5.58 Cr	Vendor selected, price agreed
Paid ₹2.04 Cr	Milestones actually marked paid


Risk and governance

Title	Meaning
Over-allocation exposure ₹0.06 Cr	Committed against effective head allocation, wherever a head is over — 3 heads here, measured per plant on that plant's own live year. Part 13 clears one of them
Trimmed by approvers ₹2.00 Cr	Money taken out by approvers editing budgets while sending them forward — the plant head's ₹2.00 Cr trim from Part 2, surfaced as a number
Delay liability ₹2.2 L	Penalty accruing across every live order
Rejection rate 6%	1 request rejected of 18 raised

Then the **FY budget position by field type** — allocated, committed, awarded, paid, remaining and utilised, **per kind of capital expenditure and never blended**, because Brown Field and Green Field are separate envelopes and a ratio across them would be meaningless.

Below that, the **trend** of requests raised, awarded and completed with the value awarded on a second axis; the **value funnel** — requested ₹11.96 Cr → approved ₹9.79 Cr → awarded ₹5.58 Cr → PO issued ₹2.04 Cr → paid ₹2.04 Cr, with the conversion and the drop-off at each step; and the **median days per stage**, measured from the record rather than assumed.

Slide 12.7 · Administration — Plants

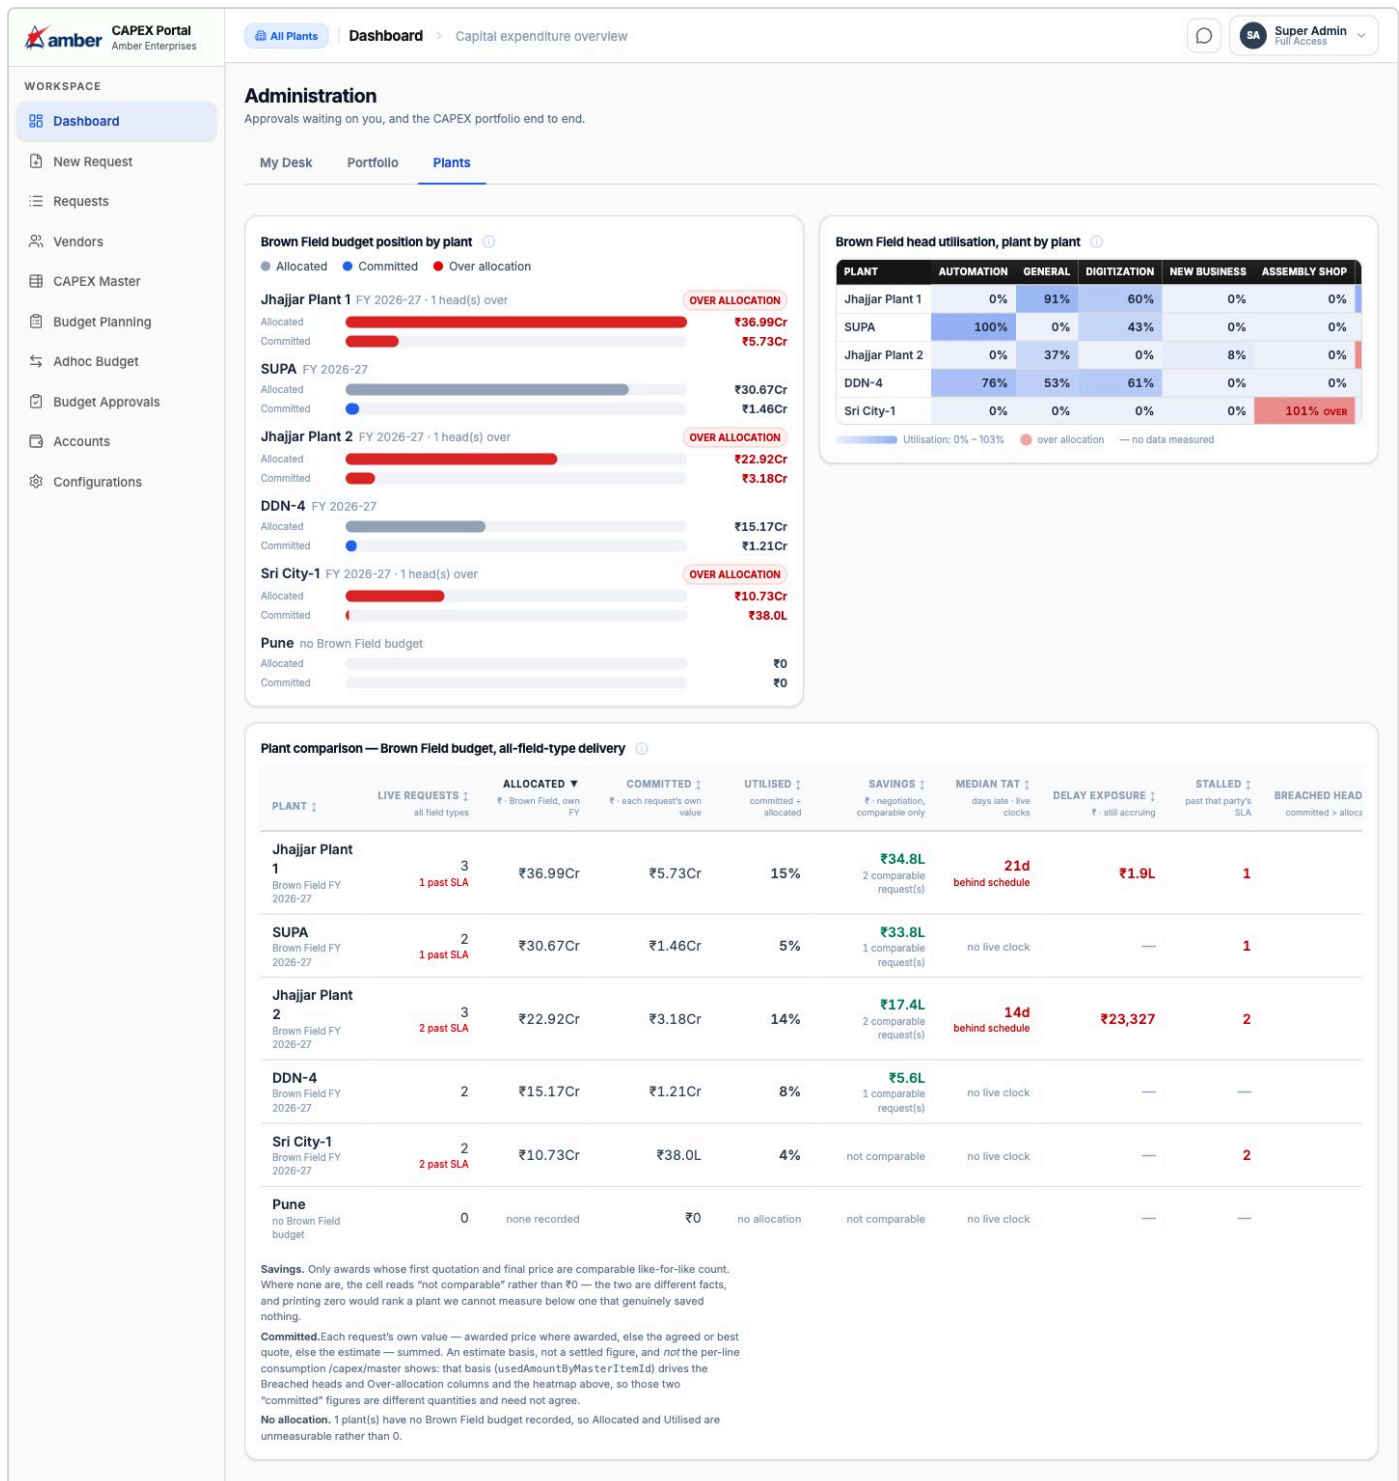

Plant against plant, which is where a capital budget is actually managed.


- **Budget position by plant** — allocated against committed, with an **over allocation** flag where a head has been overspent.
- **Head utilisation, plant by plant** — a heatmap of every head in every plant, so a 101% cell stands out at a glance.
- **Plant comparison** — a sortable table with live requests and how many are past service level, allocated, committed, utilisation, negotiation savings, median delivery delay, delay exposure, stalled requests and breached heads.

Read the footnotes under that table; they are the product being careful in public:

"Savings. Only awards whose first quotation and final price are comparable like-for-like count. Where none are, the cell reads 'not comparable' rather than ₹0 — the two are different facts, and printing zero would rank a plant we cannot measure below one that genuinely saved nothing."

"No allocation. 1 plant has no Brown Field budget recorded, so Allocated and Utilised are unmeasurable rather than 0."

Slide 12.8 · The budget author's dashboard

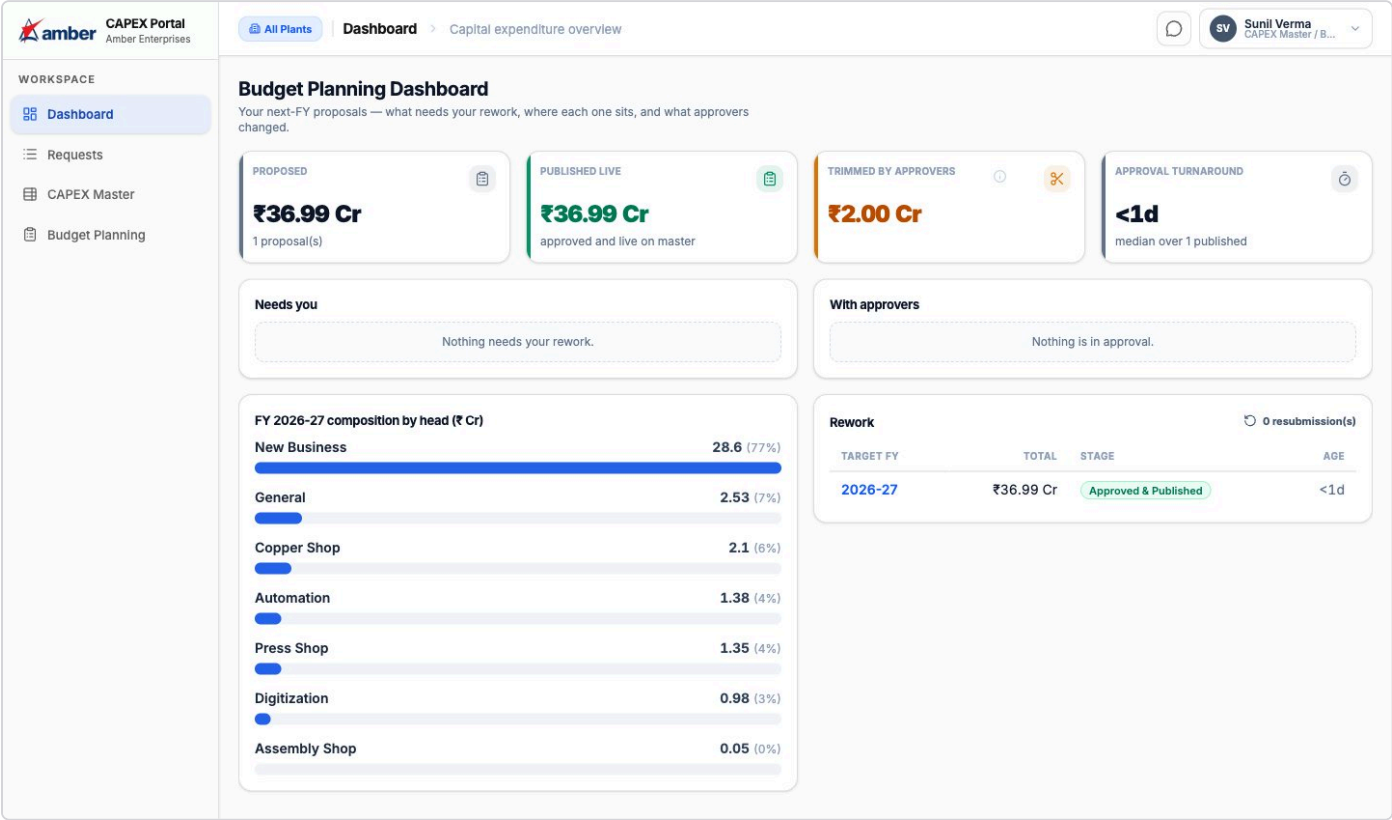


Sunil Verma's view is about proposals, not requests.

Title	Meaning
Proposed ₹36.99 Cr	What he has put up, across 1 proposal
Published live ₹36.99 Cr	What cleared all three gates and is now spendable
Trimmed by approvers ₹2.00 Cr	What approvers took out on the way through, and how many resubmissions it cost
Approval turnaround <1d	How long the three gates took, measured over what has actually published

Then **needs you** (nothing to rework), **with approvers** (nothing in flight), the **composition of the year by head** — New Business 77%, General 7%, Copper Shop 6%, Automation 4%, Press Shop 4%, Digitization 3%, Assembly Shop 0% — and a rework table showing where each target year stands.

Slide 12.9 · Every number can show its own definition

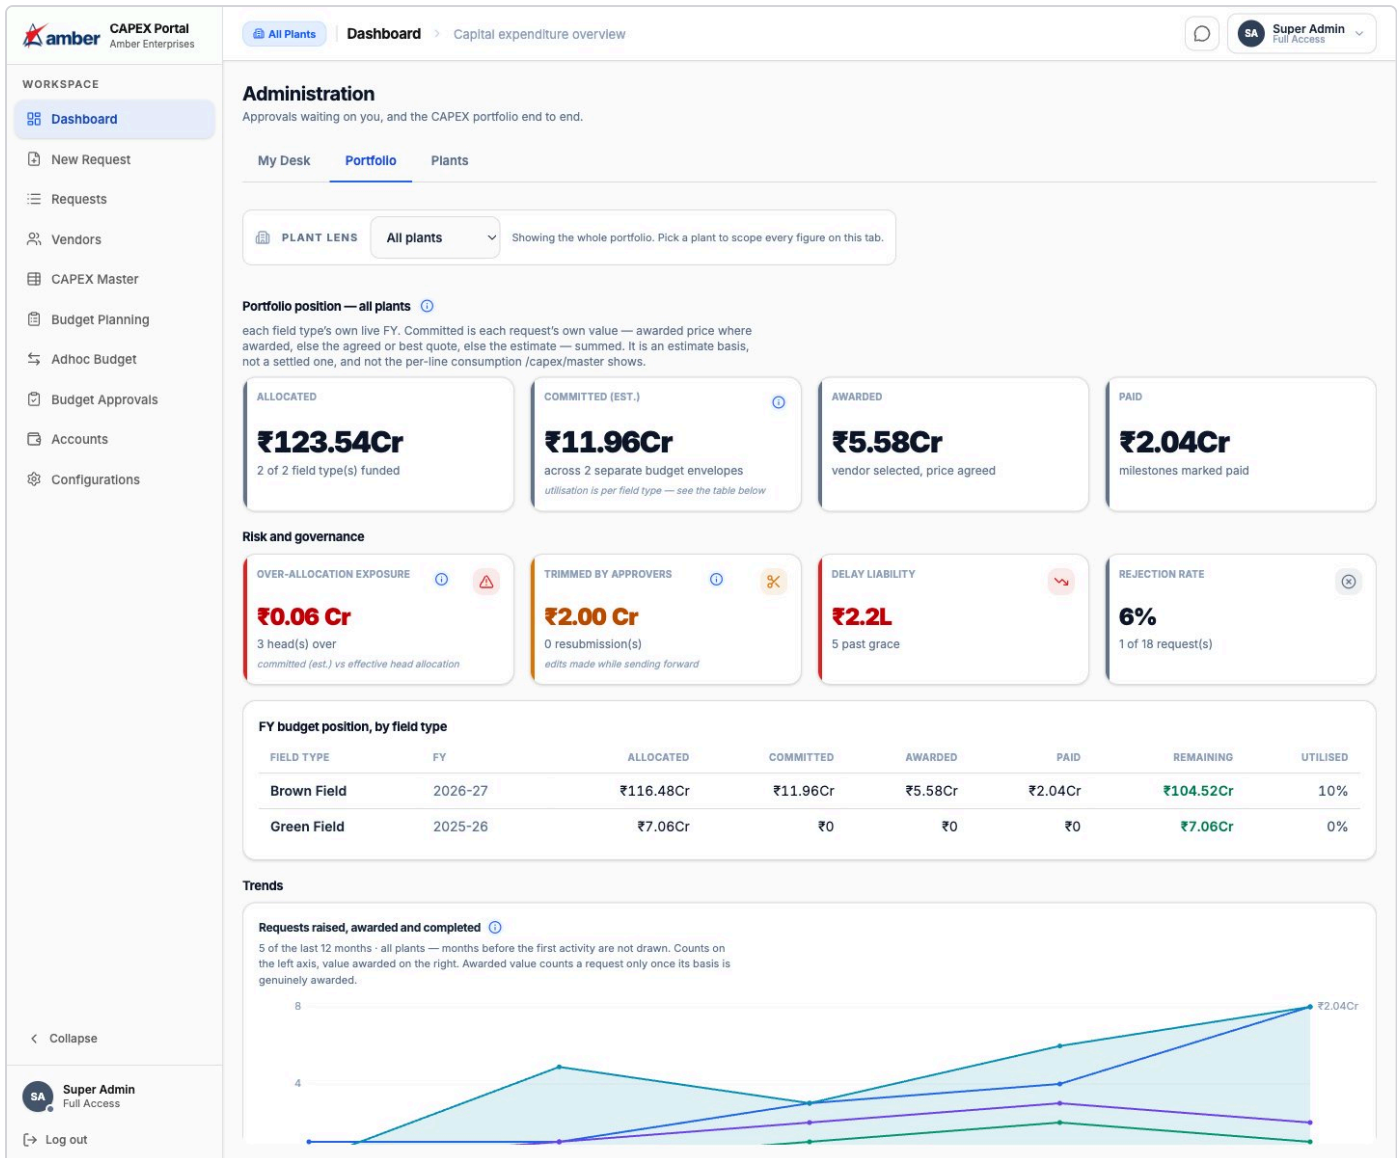

Next to most figures is a small ⓘ. Open it and the figure explains itself in place — which year it is on, what it includes, what it deliberately excludes, and what it cannot measure. For example:

"Committed is each request's own value — awarded price where awarded, else the agreed or best quote, else the estimate — summed. It is an estimate basis, not a settled one."

"Median days late on LIVE delivery clocks — a settled track is history, not current pace. 4 plants have no clock running and are not shown."

"Both charts compare ALL plants regardless of the lens, because a comparison of one plant is not a comparison; the selected plant is marked instead."

Folded away, the dashboards stay readable. Opened, every number can be defended in a meeting. That is the difference between a report somebody trusts and one they quietly stop using.

Slide 12.10 · A tile and its list always agree

The screenshot shows the CAPEX Portal interface. On the left is a sidebar with a 'WORKSPACE' menu containing links to Dashboard, New Request, Requests (highlighted), Vendors, CAPEX Master, Budget Planning, Adhoc Budget, Budget Approvals, Accounts, and Configurations. At the bottom of the sidebar is a user profile for 'Super Admin' with 'Full Access' and a 'Log out' button. The main content area has a breadcrumb trail: 'All Plants' > 'CAPEX Requests' > 'Vendor sourcing & negotiation'. Below this is a 'Filter by status:' dropdown set to 'All Statuses'. A filter chip is applied: 'Stuck at plant head · older than 3d'. Below the filter, a banner states: 'Awaiting plant-head approval for longer than the 3d threshold — the same predicate the tile counts. 2 requests past the 3d plant-head threshold. 1 other request(s) are with the plant head but still inside it.' Below the banner is a table with the following data:

REQ. NO.	SUBJECT	STATUS	WAITING	PLANT	FINALIZED	ASSIGNED TO	DATE
CAP-2627-0014	400T Hydraulic Press Ret...	With Plant Head	9d with Plant Head · past the 3d Plant Head threshold	Sri City-1	—	Neha Kapoor	13 Aug 2026
CAP-2627-0015	Mezzanine, Goods Lift & ...	With Plant Head	6d with Plant Head · past the 3d Plant Head threshold	Jhajjar Plant 2	—	Neha Kapoor	16 Aug 2026

Click the administrator's **Stuck at plant head — 2** tile and this is where you land: two requests, not eleven.

The chip states the filter that was applied — *Stuck at plant head · older than 3d* — the banner restates the rule in words, an extra column marks **why each row qualifies** (9 days and 6 days, both *past the 3d Plant Head threshold*), and the disclosure underneath names what is **not** shown: "*1 other request is with the plant head but still inside it.*"

The tile and the destination are driven by the same rule, so they cannot drift apart. If a link ever carries a filter the portal cannot apply, it says so in an amber banner and tells you exactly what you are looking at instead — it never silently shows you a different list.

Slide 12.11 · The full request list

 **CAPEX Portal**
Amber Enterprises

WORKSPACE

Dashboard

New Request

Requests

Vendors

CAPEX Master

Budget Planning

Adhoc Budget

Budget Approvals

Accounts

Configurations

< Collapse

SA Super Admin

Full Access

[> Log out

All Plants

CAPEX Requests

Vendor sourcing & negotiation

SA Super Admin

Full Access

Filter by status:

All Statuses

CAPEX Requests

All requests — 18 requests

REQ. NO.	SUBJECT		STATUS	PLANT	FINALIZED	ASSIGNED TO	DATE	ACTION
CAP-2627-0001	Centralised Material... 2 items		Completed	Jhajjar Plant 1	—	Neha Kapoor	22 Aug 2026	View
CAP-2627-0002	Shrink less Vertical M/C		In Sourcing	Jhajjar Plant 1	—	Neha Kapoor	22 Aug 2026	View
CAP-2627-0003	Shrink less Vertical M/C		Completed	Jhajjar Plant 2	—	Neha Kapoor	26 Apr 2026	View
CAP-2627-0004	Centralised Material Feeding...		Completed	DDN-4	—	Neha Kapoor	18 May 2026	View
CAP-2627-0005	HEX Black Copper Detection		Completed	SUPA	—	Neha Kapoor	09 Jun 2026	View
CAP-2627-0006	400T Hydraulic Press Retrofit		Payment In Progress	Jhajjar Plant 1	—	Neha Kapoor	25 Jun 2026	View
CAP-2627-0007	Compressed Air Line Re-pipi...		Payment In Progress	Jhajjar Plant 2	—	Neha Kapoor	04 Jul 2026	View
CAP-2627-0008	Robotic Part Removal — 130...		PI Requested	SUPA	—	Neha Kapoor	12 Jul 2026	View
CAP-2627-0009	Scissor Lifter		PI Requested	Sri City-1	—	Neha Kapoor	17 Jul 2026	View
CAP-2627-0010	Fire Hydrant Network Upgrade		In Sourcing	Jhajjar Plant 2	—	Neha Kapoor	26 Jul 2026	View
CAP-2627-0011	Line-side MES Terminals (32...		In Sourcing	DDN-4	—	Neha Kapoor	01 Aug 2026	View
CAP-2627-0012	Plant ESG / EMS Monitoring		In Sourcing	SUPA	—	Neha Kapoor	06 Aug 2026	View
CAP-2627-0013	Compressed Air Line Re-pipi...		In Sourcing	Jhajjar Plant 1	—	Neha Kapoor	10 Aug 2026	View
CAP-2627-0014	400T Hydraulic Press Retrofit		With Plant Head	Sri City-1	—	Neha Kapoor	13 Aug 2026	View
CAP-2627-0015	Mezzanine, Goods Lift & Utili...		With Plant Head	Jhajjar Plant 2	—	Neha Kapoor	16 Aug 2026	View
CAP-2627-0016	Robotic Part Removal — 130...		With Plant Head	DDN-4	—	Neha Kapoor	20 Aug 2026	View
CAP-2627-0017	Line-side MES Terminals (32...		Draft	Jhajjar Plant 1	—	Neha Kapoor	21 Aug 2026	View
CAP-2627-0018	New HEX Line — Phase 1 Civ...		Rejected	SUPA	—	Neha Kapoor	20 Jun 2026	View

The unfiltered list behind all of it: 18 requests across five plants and every state in the pipeline — completed, payment in progress, PI requested, in sourcing, with plant head, draft and rejected — each with its number, subject, plant, owner and date. Filter by status from the corner, or arrive here from any dashboard tile with the filter already applied.

Part 13 — Trackers, transfers and configuration

Slide 13.1 · The accounts queue

CAPEX Portal
Amber Enterprises

WORKSPACE

Dashboard

New Request

Requests

Vendors

CAPEX Master

Budget Planning

Adhoc Budget

Budget Approvals

Accounts

Configurations

All PlantsAccounts QueueFA codes, PO & payments

SA Super AdminFull Access

Accounts Queue

Track FA codes, purchase orders and milestone payments (one row per awarded vendor on split reverse auctions). Plant Accounts action these on their emailed link — open a request to copy the link or preview the email.

IN PROGRESS (2)

REQUEST	SUBJECT	PLANT	VENDOR	STATUS	PAYMENTS
CAP-2627-0006	400T Hydraulic Press Retrofit	Jhajjar Plant 1	Delta Electronics	Payment In Progress	—
CAP-2627-0007	Compressed Air Line Re-piping — Block C	Jhajjar Plant 2	Tata Motors Ancillaries	Payment In Progress	—

COMPLETED (5)

REQUEST	SUBJECT	PLANT	VENDOR	STATUS	PAYMENTS
CAP-2627-0001	Centralised Material Feeding for Molding Machi...	Jhajjar Plant 1	Tata Motors Ancillaries	Completed	Paid ₹1,61,07,000
CAP-2627-0001	Centralised Material Feeding for Molding Machi...	Jhajjar Plant 1	L&T Infrastructure	Completed	Paid ₹43,07,000
CAP-2627-0003	Shrink less Vertical M/C	Jhajjar Plant 2	Tata Motors Ancillaries	Completed	—
CAP-2627-0004	Centralised Material Feeding for Molding Machi...	DDN-4	Siemens India	Completed	—
CAP-2627-0005	HEX Black Copper Detection	SUPA	L&T Infrastructure	Completed	—

A read-only tracker of every order in the accounts stage, split into *in progress* and *completed*, with the paid figure where there is one.

One row per awarded vendor, which is why CAP-2627-0001 appears twice — Tata's award and L&T's award are separate orders with separate purchase orders and separate payments. It answers "where is every rupee?" without giving anybody the ability to move one.

Slide 13.2 · Ad-hoc budget reallocation — the only mid-year change

amber

CAPEX Portal
Amber Enterprises

WORKSPACE

Dashboard

New Request

Requests

Vendors

CAPEX Master

Budget Planning

Adhoc Budget

Budget Approvals

Accounts

Configurations

< Collapse

SA

Super Admin
Full Access

[->

Log out

All Plants

Adhoc Budget

Reallocate budget between heads

SA

Super Admin
Full Access

↩

Adhoc Budget Reallocation

Move budget between heads within the same plant (Brown Field, FY 2026-27). Requires admin approval.

RAC

EMS

Component

Fan

Jhajjar Plant 1

New Transfer · Jhajjar Plant 1

From Head (source)

New Business — ₹28.60 Cr spare

Spare available: ₹28.60 Cr

To Head (destination)

Press Shop — ₹1.40 Cr used / ₹1.35 Cr

Amount (Cr)

0.15

Reason (optional)

Cr from New Business, where the Phase 1 civil scope was trimmed at approval.

Submit for Admin Approval

Requests · RAC

No adhoc requests yet for this scope.

A live budget year is read-only. The one exception is a transfer **between heads within the same plant and the same year**, and it needs the administrator's approval.

Here the Press Shop head has gone ₹0.05 Cr over after the 400T press retrofit came in above estimate. Sourcing raises a transfer of ₹0.15 Cr from New Business — where the plant head trimmed the civil scope back in Part 2 — and states the reason.

The administrator sees the transfer with **both heads' positions before and after** spelled out — *New Business ₹28.60 Cr → ₹28.45 Cr · Press Shop ₹1.35 Cr → ₹1.50 Cr* — and approves or rejects. Approving rewrites the head's effective allocation, and the over-allocation flag on the dashboard clears on the next refresh.


Note what did **not** happen: nobody edited an approved budget line. The original numbers stand, the transfer is a separate, attributable, approved act on top of them.

Slide 13.3 · Configuration


Administrator only. Four tabs — **Plants**, **Categories**, **Users** and **System** — holding the reference data the rest of the portal depends on. The nine Amber plants shown here are what every plant picker in the product offers.

Slide 13.4 · The other three kinds of capital expenditure

Everything so far followed a Brown Field request, because that is the longest route. The other three work the same way with different structure.

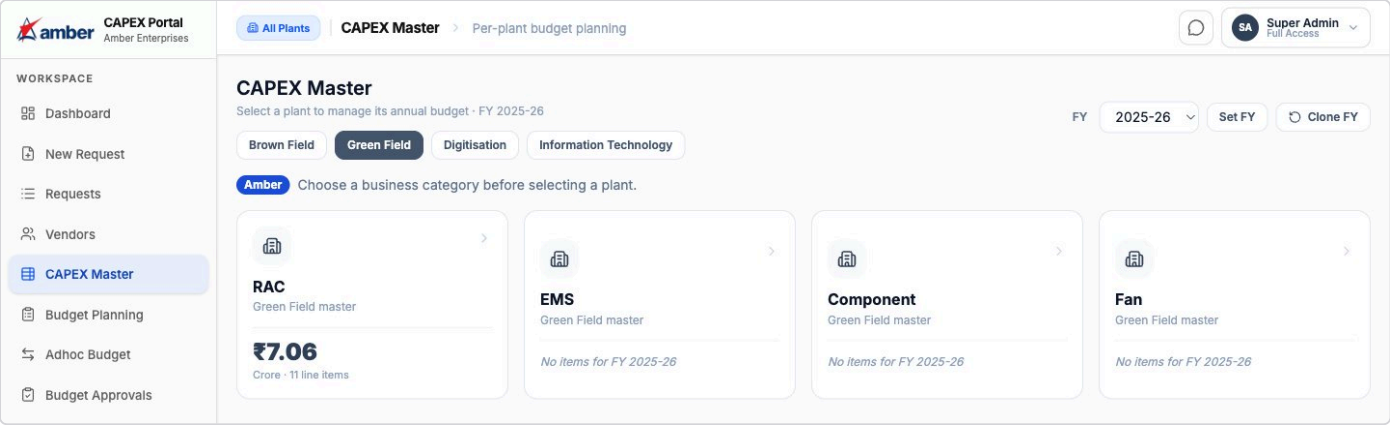

Green Field — a brand-new plant — is budgeted in a hierarchy rather than a flat list: plant → section → head → line item, with a budget assigned at each level and each level deducting from the one above it.

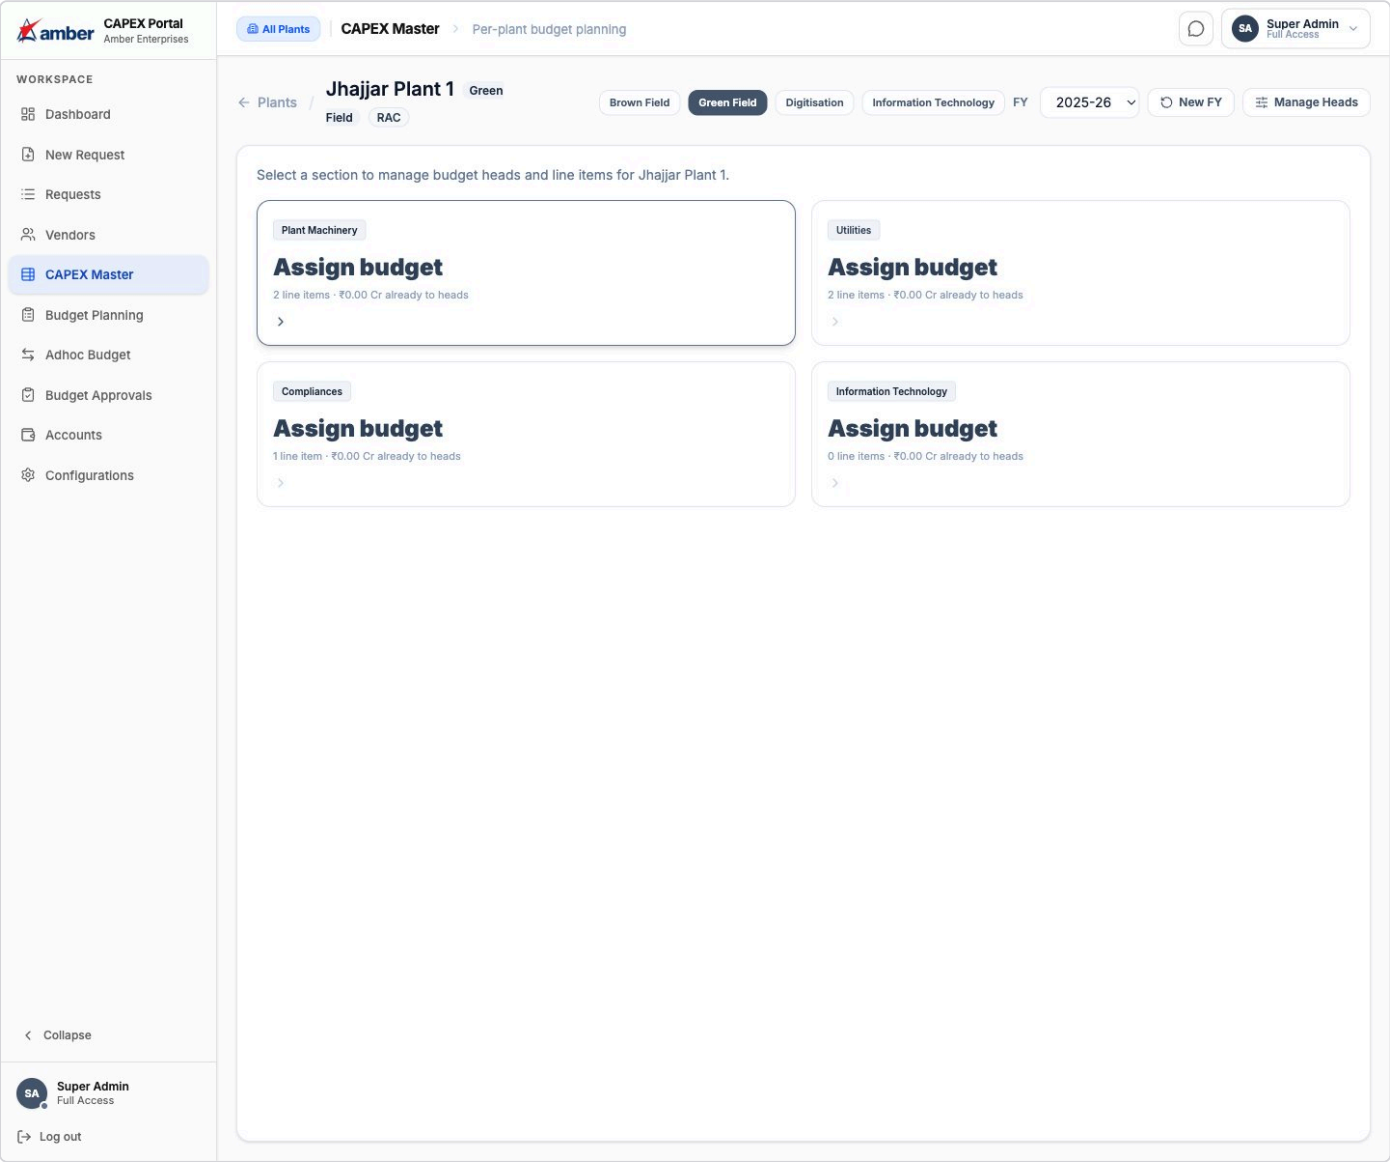

The four sections are **Plant Machinery**, **Utilities**, **Compliances** and **Information Technology**; opening one for the first time prompts for its share of the plant's envelope, and opening a head inside it prompts for its share of the section's. Green Field requests skip the plant-head gate, because the plant does not have a head yet.

Digitisation and **Information Technology** each have their own master and their own heads, and route like Brown Field.

Part 14 — Every email in one place

The portal composes and previews the mail; a person still sends it. Each message carries a single-purpose link that does exactly one job for exactly one person.

#	Sent when	To	What the link lets them do
1	A budget proposal is submitted	Plant head	Approve, edit-and-send-forward, or reject the plant's budget
2	The admin approves the budget	Global Accounts	Final sign-off, which publishes the year
3	A request is submitted	Sourcing engineer	Notification of new work
4	A Brown Field / Digitisation / IT request is submitted	Plant head	Approve the request for sourcing
5	Vendors are invited	Each vendor	Accept the terms, then quote, negotiate, bid
6	A specification is sent	Technical team	Approve, send back, or reject the machine spec — vendor anonymous
7	A vendor uploads the proforma invoice	Plant Accounts	Assign the FA codes, then record payments
8	The FA codes are submitted	Global Accounts	Issue the purchase order to the vendor

The links are unguessable. The decision links — the budget sign-off and the technical specification — are **consumed on use** and **replaced when a package is re-sent**, so a forwarded email cannot re-decide something. The accounts links are not consumed, because those two people come back to the same page over several days.

Part 15 — On any device



REVERSE AUCTION
CAP-2627-0001: Centralised Mate...

You are bidding as: **Tata Motors Ancillaries** (VND-001)
ⓘ All prices in INR

⌛ No action needed — waiting on Amber.

Quotation Approved

✓

Proforma Invoice Submitted
Thank you. Your PI has been sent to Amber's buyer and accounts team for PO processing and payment.

✓

TAT Closed — Final Payment Made
Delivered within TAT — no delay deduction.

📄

Purchase Order

PO NUMBER

PO/JP1/2627/0091

PO AMOUNT

₹1,61,07,000

⬇️

Download PO Document

⌚ PO received from
Amber

· issued 22 Aug 2026,
07:54

Payment Status

Advance (30%)

₹48,32,100

⌚ Paid

On Dispatch (60%)

₹96,64,200

⌚ Paid

On Installation (10%)

₹16,10,700

⌚ Paid

⌚ Trial approved by Amber

Every screen an outsider touches — the plant head's approval page, the technical team's sign-off, both accounts pages and every vendor screen — is built to work on a phone as well as a desktop. That is not decoration: a plant head approving a budget from a plant floor and a vendor checking a payment from a factory in Pune are the normal cases, not the exceptions.


On a phone the pricing tables become card stacks rather than shrinking to unreadable columns, and the maths behind them is the same code, so the desktop and mobile figures cannot disagree.

Closing · The story in one paragraph

A maintenance engineer writes next year's budget from a blank sheet, uploads it as a spreadsheet, and it clears three independent gates — plant head, administrator, Global Accounts — before a single rupee is spendable, with each approver able to trim a number and send it forward, and the next approver shown exactly what changed and why. A plant buyer then raises a request that can only point at money already approved, and the plant head waves it through from an email. Sourcing invites two vendors, who accept Amber's commercial terms, bank guarantee and delay penalty *before* they are allowed to see a price field, quote line by line with their own HSN codes, and get countered inline. Amber's technical team signs off each machine on its own link, without being told which supplier it came from. Sourcing splits the award across both vendors, and each award runs its own track: the vendor raises an invoice, Plant Accounts code the asset, Global Accounts issue the purchase order, the vendor proves the machine with a trial, and the final 10% is released only once sourcing accepts it. A second machine goes to a live reverse auction and closes ₹1.28 lakh apart on a common rupee basis. And at every point, four dashboards say who is holding what, for how long, and what the negotiating actually delivered — with every figure willing to explain where it came from.

One tracked pipeline. Named gates. Nobody outside the buying team ever needs a login. And every rupee traceable from the budget line it came out of to the milestone it was paid against.

Appendix · The route a request takes



Green Field requests skip the plant-head gate and enter **In sourcing** directly. A **split award** keeps the request itself coarse — it reads **PI requested** while awards are in flight and **Completed** once every award has finished — while each awarded vendor runs the whole chain on its own. Any stage from **With plant head** onward can end in **Rejected**.
